PROJECT PROCESSES

PROJECT MANAGEMENT MANUAL

15/05/2025

L/\\//\\
LABORATORY FOR
VISIONARY
ARCHITECTURE

TABLE OF CONTENTS

1. INTRODUCTION

1. Project Processes Overview
2. Templates Register
3. Project Definition
4. Types of Projects at LAVA
5. Projects and Company Operations
6. Core Processes and Kit of Parts
7. Project Process Groups
8. Project Core Competencies
9. Framework of Processes

2. BEFORE THE PROJECT

1. **BIDDING**
    1. Bidding Code
    2. Technical Proposal
    3. Company Information
    4. Portfolio & Selected Projects
    5. CVs
    6. External Coordination
    7. Confidentiality & NDAs

2. **PROJECT CHECKLIST**
    1. Project Checklist Overview
    2. Document Checklist
    3. Processes Checklist

3. DURING THE PROJECT

1. **KNOWLEDGE MANAGEMENT**
    1. Project Code
    2. Folder Structure
    3. Digital Collaboration
    4. File Naming Conventions

2. **PLANNING**
    1. Project Leadership & Roles
    2. Timeline
    3. List of Deliverables
    4. Resourcing
    5. Scope & Responsibilities
    6. Project Directory

3. **EXECUTION**
    1. Internal Kick-Off
    2. Tasks & Activities
    3. Design Direction
    4. Coordination
    5. Reporting
    6. Quality Control

4. AFTER THE PROJECT

1. **KNOWLEDGE MANAGEMENT**
    1. Archiving
    2. PR Content Selection
    3. Project Fact Sheet

01
INTRODUCTION

1.1 PROJECT PROCESSES OVERVIEW


WHAT ARE THE **OBJECTIVES** OF PROJECT PROCESSES AT LAVA ?

- Empower design teams by **streamlining** processes and **improving our use of time**
- **Protect both LAVA and client interests**
- **Spread knowledge** internally on best practices
- Strengthen credibility to external parties by **standardizing our documentation and approaches**
- **Improve quality** of our work (**professionalism** - e.g. design typologies, efficiency in structure, sustainable practices, etc.)
- Better understanding of **briefing, materials and standards**
- Reduce reliance on **external Project Management Consultants (PMCs)**


1.1 PROJECT PROCESSES OVERVIEW

WHAT IS THE PROJECT PROCESSES MANUAL ?


This document is a record of the main **management processes** which are expected to be used on Projects at LAVA. It is intended to be reviewed by all Project Staff and especially Project Leadership Teams, and includes **orientation and guidance** on the following :

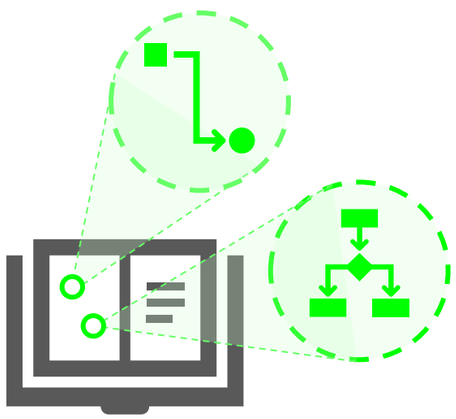

1. **General explanation of responsibilities and different approaches**

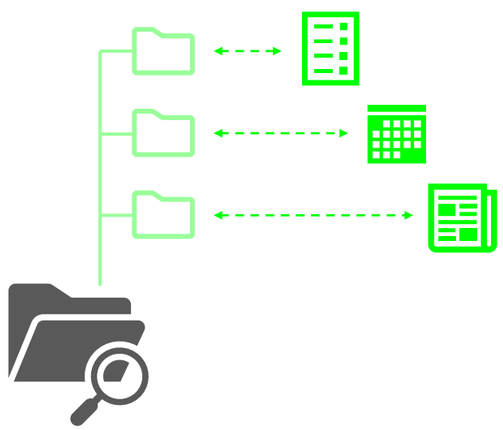

2. **Links To Templates, Components & Tools**



3. **Guidance and Tips on how to use them**

As part of certain specific processes, it is expected to use **Templates, Components and Tools.** These can be configured and tailored for each project as needed, but should start from a common starting point developed by LAVA to ensure the following :

Simplicity | Easy to use, minimal effort
Continuity | Consistent and standardized
Accessibility | Easy to find & collaborate

1.2 TEMPLATES REGISTER

WHERE TO FIND THE MANAGEMENT TOOLS & TEMPLATES ?

The following is the list of templates currently available and required for use which are referenced in this manual, along with their respective **locations** on the server under the links.

Process Group	Template Name	Format	Revision	Date	Link	Comments
Standards	**Logos**	EPS/PNG/SVG		19-Dec-24	L:\4_GENERAL OFFICE\01_Logo	Check with Roxanne (PR Team) for updates
Standards	**Fonts**	OpenType		19-Dec-24	**L:\4_GENERAL OFFICE\02_Font**	Check with Roxanne (PR Team) for updates
Bidding	**Company Profile**	InDesign		01-Sep-24	**L:\4_BIDDING\Components\1_Company Profile**	Current Company Profile is the latest which has been used in recent Bids in Berlin. Company information to be updated at earliest possibility by Graphic Designer and LAVA PR Team pending feedback from partners.
Bidding	**Portfolio**	InDesign		1-May-2025	**L:\4_BIDDING\Components\1_Portfolio**	Current Portfolio is the latest which has been used in recent Bids in Berlin. Portfolio to be updated at earliest possibility by Graphic Designer and LAVA PR Team pending feedback from partners.
Bidding	**CV Database**	InDesign		19-Sep-2025	**L:\4_BIDDING\Components\2_CVs**	CV Template is the latest which has been used in recent Bids in Berlin. CV Template to be updated at earliest possibility by Graphic Designer and LAVA PR Team pending feedback from partners.
Bidding	**CV Template**	InDesign		1-Apr-2025	**L:\4_BIDDING\Internal Templates and Standards\2_CV**	CV Template is the latest which has been used in recent Bids in Berlin. CV Template to be updated at earliest possibility by Graphic Designer and LAVA PR Team pending feedback from partners.
Bidding	**In-Design Template**	InDesign		**10-Jun-2024**	**L:\4_BIDDING\Internal Templates and Standards\1_Technical Proposal & EOI**	Current In-Design Template is the latest which has been used in recent Bids in Berlin (NODE graphics style). To be updated at earliest possibility by Graphic Designer and LAVA PR Team pending feedback from partners.
Bidding	**NDA**	Word	v0.1	27-May-25	L:\4_BIDDING\Internal Templates and Standards\3_Non-Disclosure Agreement	Based on document originally authored by company legal counsel.
Bidding	**Sub-Consultancy Agreement**	Word	v0.1	27-May-25	L:\4_BIDDING\Internal Templates and Standards\3_Sub-consultancy Agreement	Multiple documents exist for certain projects - to be produced by company legal counsel as required.

1.2 TEMPLATES REGISTER

WHERE TO FIND THE MANAGEMENT TOOLS & TEMPLATES ?

The following is the list of templates currently available and required for use which are referenced in this manual, along with their respective **locations** on the server under the links.

Process Group	Template Name	Format	Revision	Date	Link	Comments
Knowledge Management	**Project Checklist**	Excel	v0.1	16-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\01_Project Checklist	Project Checklist includes two tabs - Documents Checklist and Processes Checklist.
Knowledge Management	**Project Folder Structure**	-	v1.0	2023	L:\4_PROJECT MANAGEMENT\01_Templates\02_Folder Structure	Standard structure to be deployed for each Project on the Server
Knowledge Management	**Project Fact Sheet**	Excel	v0.1	16-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\05_Knowledge Management	Fact Sheet based on draft from January 2025 - check with PR Team for any updates. Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Planning	**High-Level Schedule**	Excel	v0.1	12-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\03_Planning\01_Timeline	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Planning	**Daily Schedule**	Excel	v0.1	12-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\03_Planning\01_Timeline	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Planning	**Master Schedule**	Excel	v0.1	12-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\03_Planning\01_Timeline	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Planning	**Deliverables List**	Excel	v0.1	16-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\03_Planning\02_Deliverables	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Planning	**Project Directory**	Excel	v0.1	12-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\03_Planning\03_Project Directory	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Reports & Drawings	**Powerpoint Report**	Powerpoint	v0.1	16-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\04_Execution\01_Reports & Presentations\02_Powerpoint	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Reports & Drawings	**In-Design Report**	InDesign	v0.1	16-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\04_Execution\01_Reports & Presentations\01_InDesign	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Coordination	**MoMs**	Word	v0.1	16-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\04_Execution\02_Coordination	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Coordination	**Issues Tracker**	Excel	v0.1	16-Jun-25	L:\4_PROJECT MANAGEMENT\01_Templates\04_Execution\02_Coordination	Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)
Coordination	**Company Letterhead**	Word	v0.1	27-May-25	L:\4_GENERAL OFFICE\04_Letterhead	Graphic Designer to update Letterhead at earliest possibility. Links currently to Sharepoint - to be updated upon rollout with Server links to respective LAVA Library (L:)


1.3 PROJECT DEFINITION

WHAT NORMALLY DEFINES A PROJECT ?

Projects are temporary, have a start and end date, and are unique.

Operations are ongoing and repeatable.


Both are driven by overarching company **strategies, objectives and policies** set by leadership.

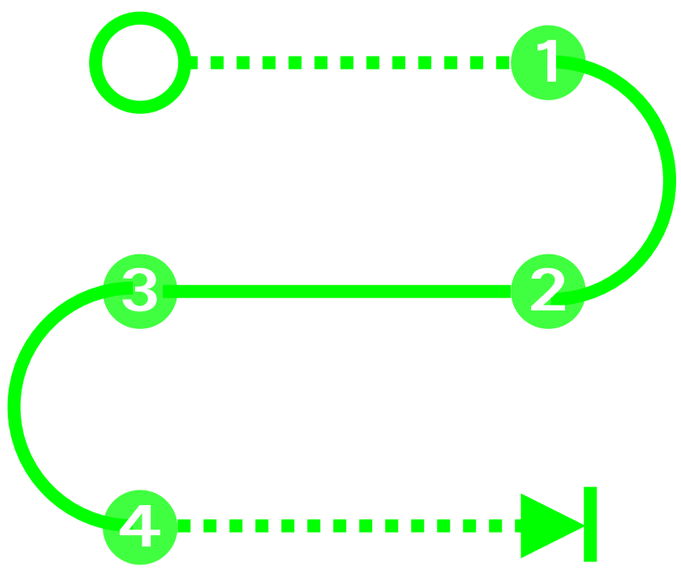

1.3 PROJECT DEFINITION

WHAT NORMALLY DEFINES A PROJECT ?

Projects are often organized in **Stages**, each having its own kick-off, interim milestones and final deliveries which are reviewed and evaluated at Stage Gates.

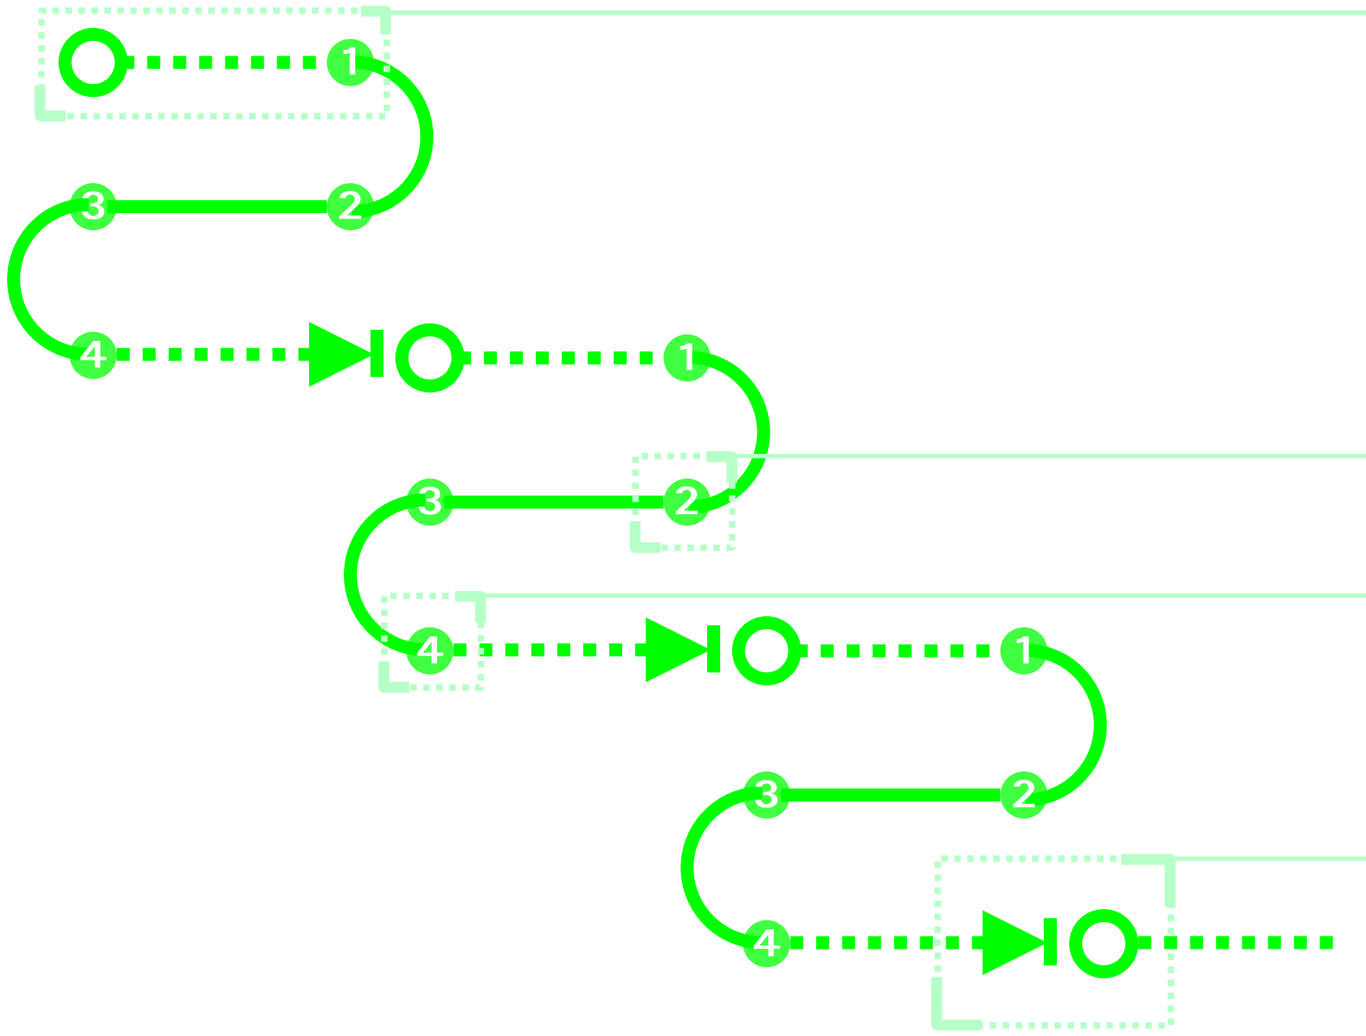

Notice to Proceed is a formal document issued by a client authorizing the project stage to start. It is normally followed by a **Mobilization** period (e.g. 1 or 2 weeks), during which the team prepares to formally initiate a project through a **Kickoff**.

Interim Milestones provide a structured approach to formally issue deliverables and receive comments from the client. In some cases invoicing can happen at these milestones.


Final Submissions are when project deliverables are issued in full to a client, signaling that the project has been completed according to the scope.

Stage Gate is a formal review period during which a client decides if a project can proceed further, or if changes or corrections are required.

1.3 PROJECT DEFINITION

HOW DOES A PROJECT INTERFACE WITH OPERATIONS ?


Core project processes (MVPs) include critical activities which are necessary to keep the LAVA ship running smoothly beyond the project scope and timeline (e.g. resource tracking, archiving PR content, personnel development, etc.)

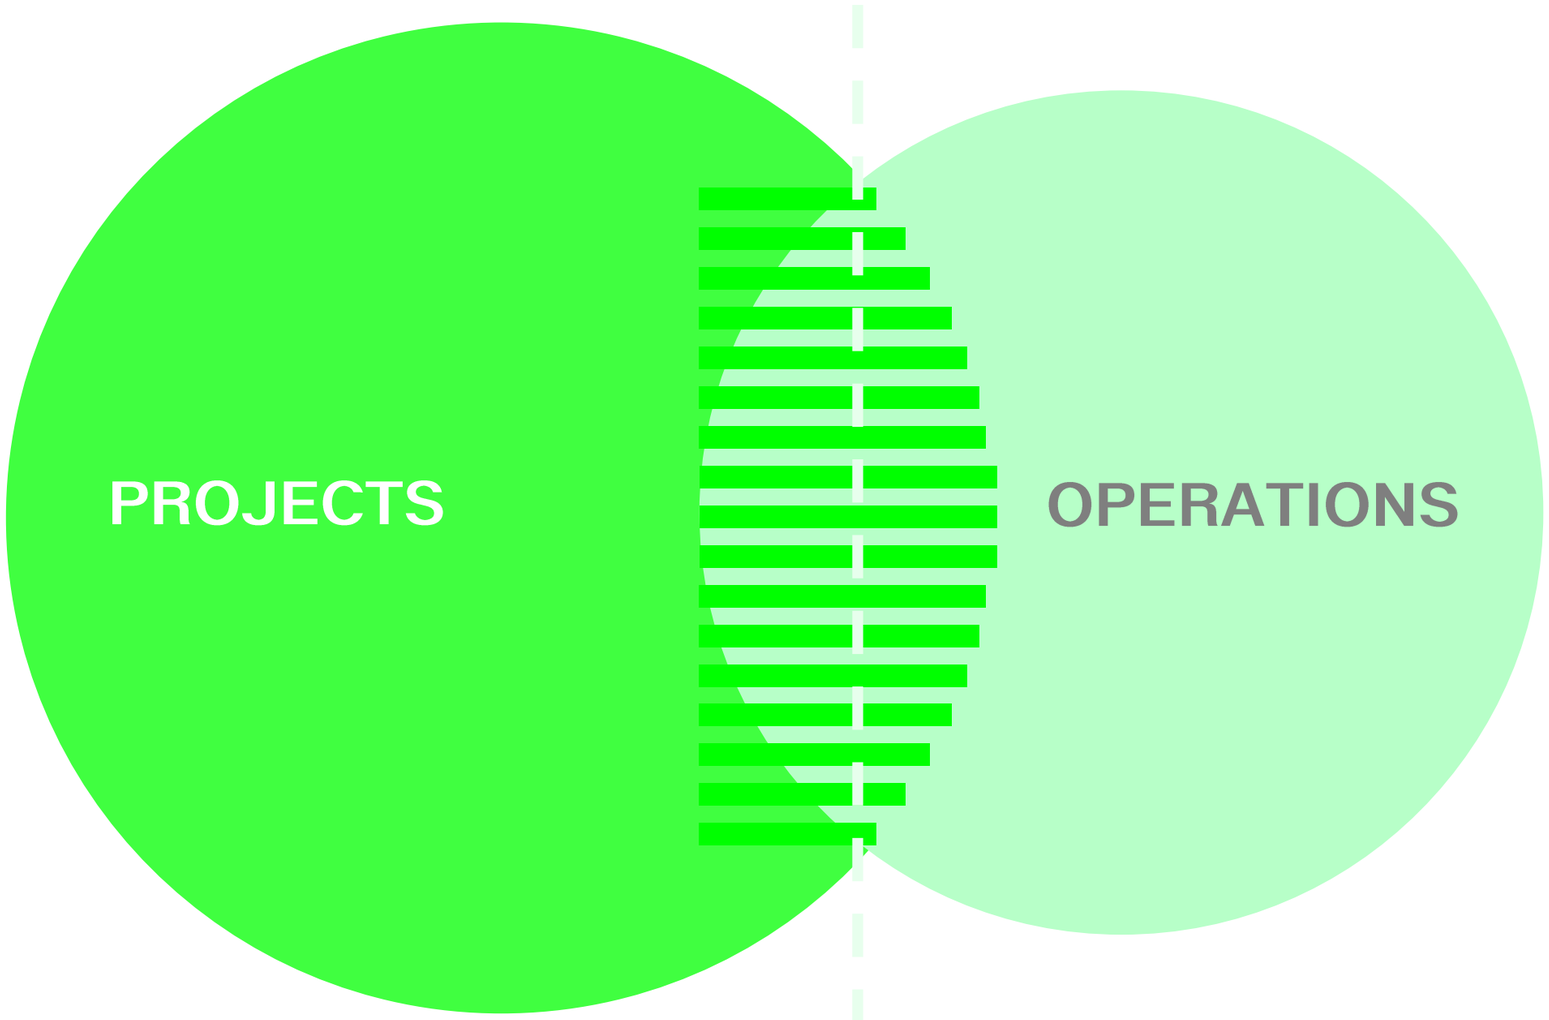

1.3 PROJECT DEFINITION

HOW DOES A PROJECT INTERFACE WITH OPERATIONS ?

Core project processes (MVPs) include critical activities which are necessary to keep the LAVA ship running smoothly beyond the project scope and timeline (e.g. resource tracking, archiving PR content, personnel development, etc.)

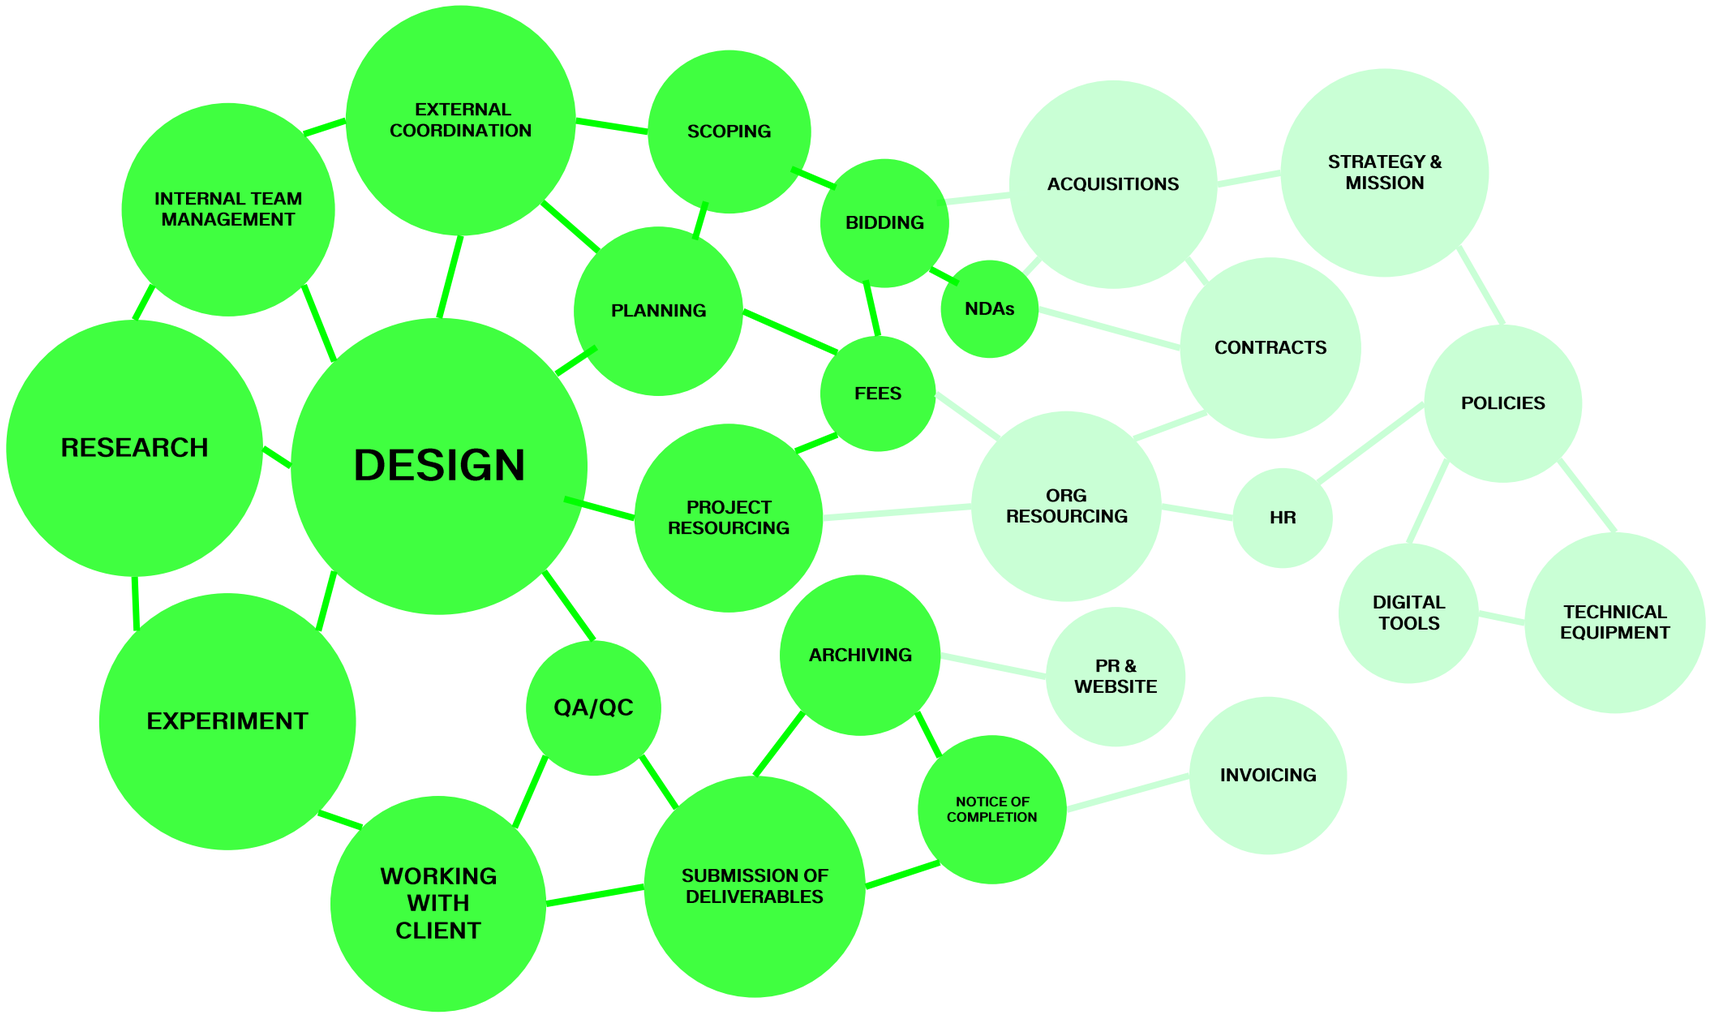


1.4 TYPES OF PROJECTS AT LAVA

WHAT ARE THE TYPES OF PROJECTS AT LAVA ?

Projects at LAVA are **unique and can range anywhere** from a focused scope with a small design team to a multidisciplinary project with a massive consortium across multiple stages.


LAVA AS ARCHITECT

Projects with **LAVA as a Design Architect with little to no subconsultants**, working together with a small client group.




LAVA AS LEAD CONSULTANT

Projects involving **LAVA as an LDC with consortiums**, multiple external parties and complex organizational structures.

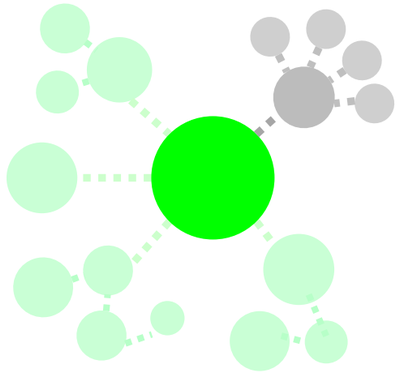

LAVA WITH EXTERNAL PMC

Projects with LAVA as an LDC with consortiums including an **external Project Management Consultant**.

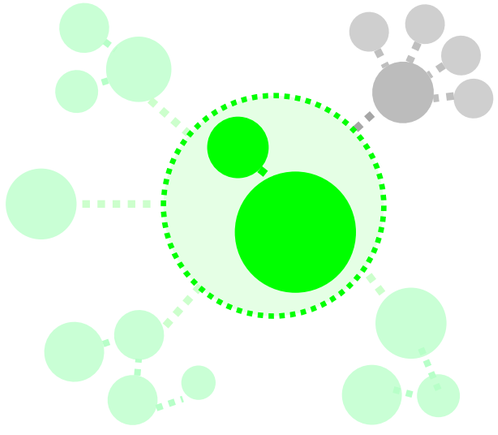


1.5 CORE PROCESSES & KIT OF PARTS

HOW DO WE APPROACH EACH TYPE OF PROJECT ?

A **scalable** approach to management and design processes which can start from a **common denominator**, can be **tailored** when needed, and **evolve** with time.


CORE PROCESSES

What are the critical functions and activities required on **all projects** at LAVA ?




KIT-OF-PARTS PROCESSES

What other tools, techniques and approaches might be required when working on large or complex projects at LAVA ?

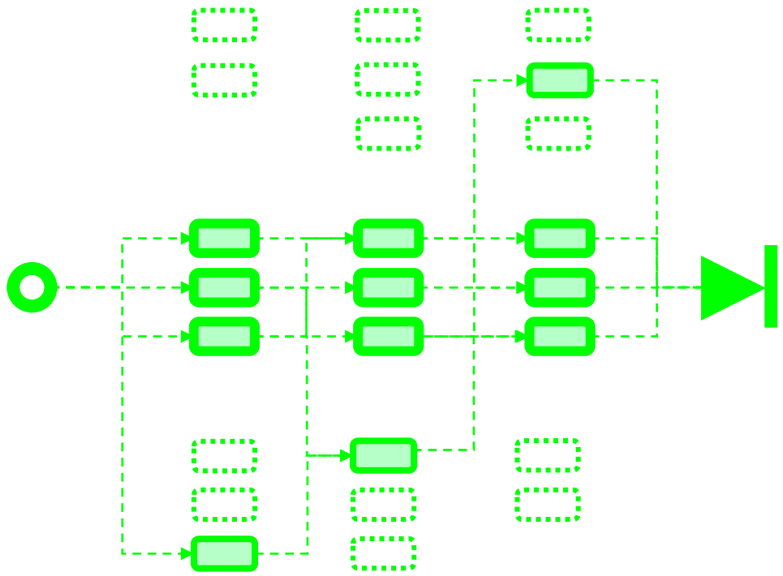

CAN WE **TAILOR** OUR APPROACH FOR EACH PROJECT ?

Each project is unique and faces its own challenges. In addition to a **standardized approach** for all projects, LAVA's processes should allow for **customization** based on a **centralized knowledge base**.

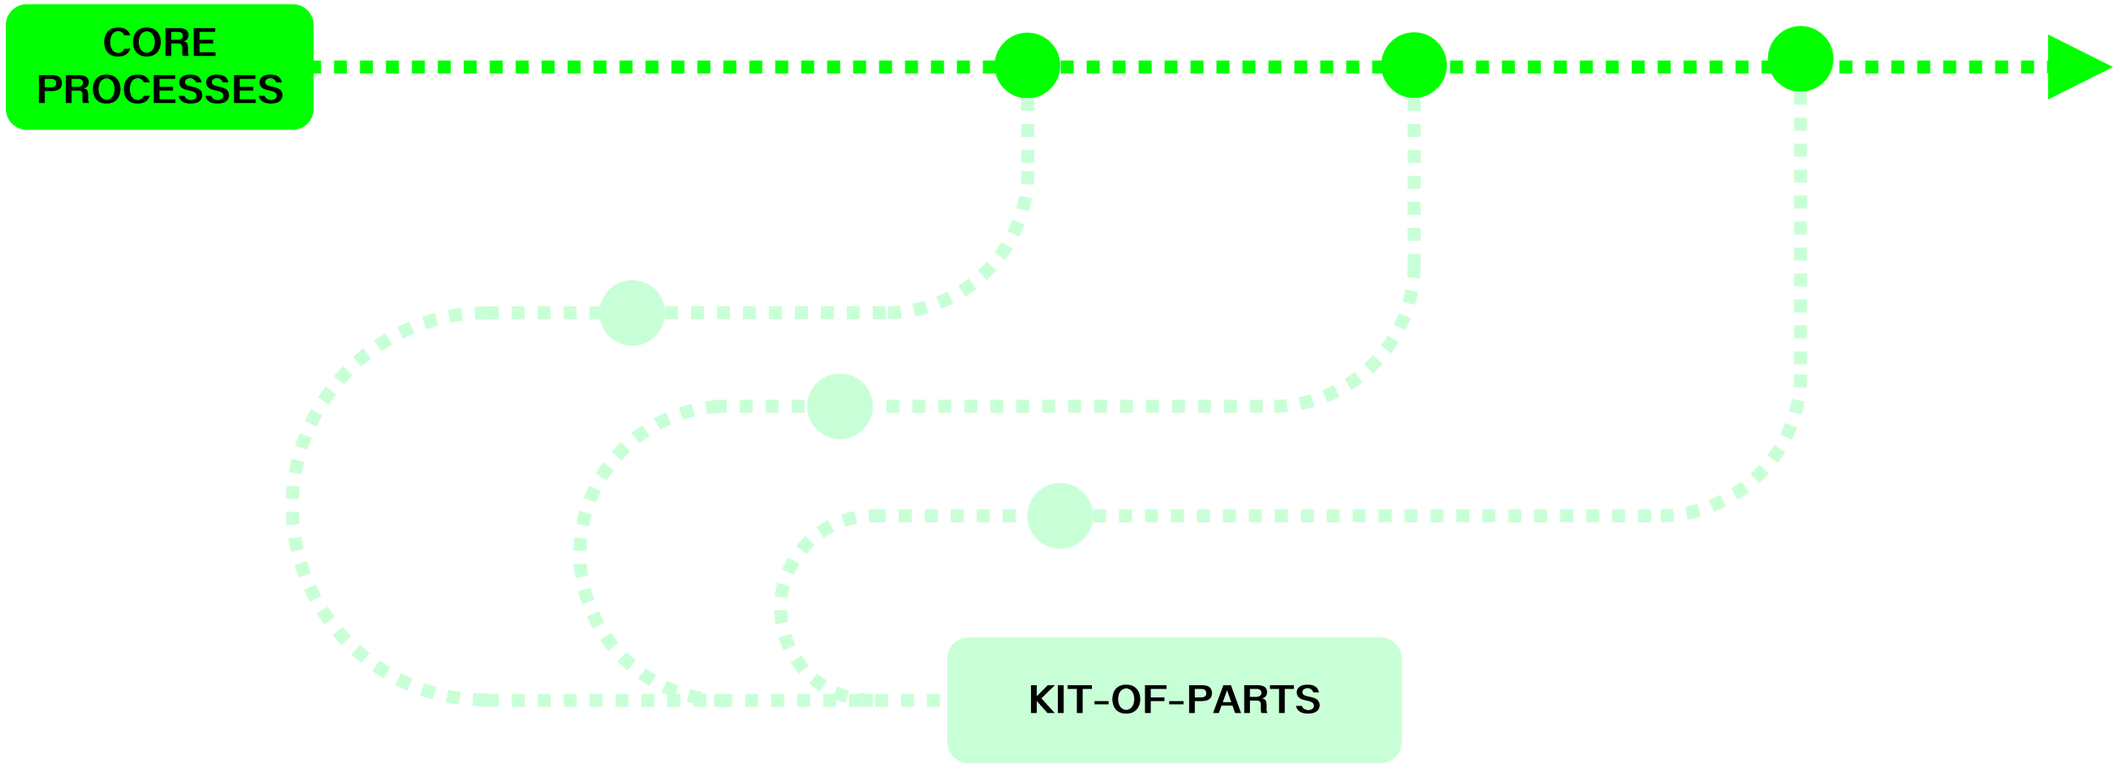

1.6 PROJECT PROCESS GROUPS

WHAT ARE THE PROJECT PROCESS GROUPS ?

According to global practice, project processes are grouped based on time.

LAVA processes should be **lean, efficient and streamlined.**

“After the game is before the game” -> Instead of 5 groups, only 3 are proposed.

Project Management Institute. PMP®

	INITIATING	PLANNING	EXECUTING	MONITORING & CONTROLLING	CLOSING
LAVA	BEFORE THE PROJECT		DURING THE PROJECT		AFTER THE PROJECT


1.6 PROJECT PROCESS GROUPS

WHAT ARE THE PROJECT PROCESS GROUPS ?

Before the Project – The parameters of the project such as Scope, Time and Resourcing are not yet confirmed.

During the Project – Green light to start. Project is planned, design is developed and services are delivered.

After the Project – Once service are completed, all relevant files are archived accordingly and team demobilizes.

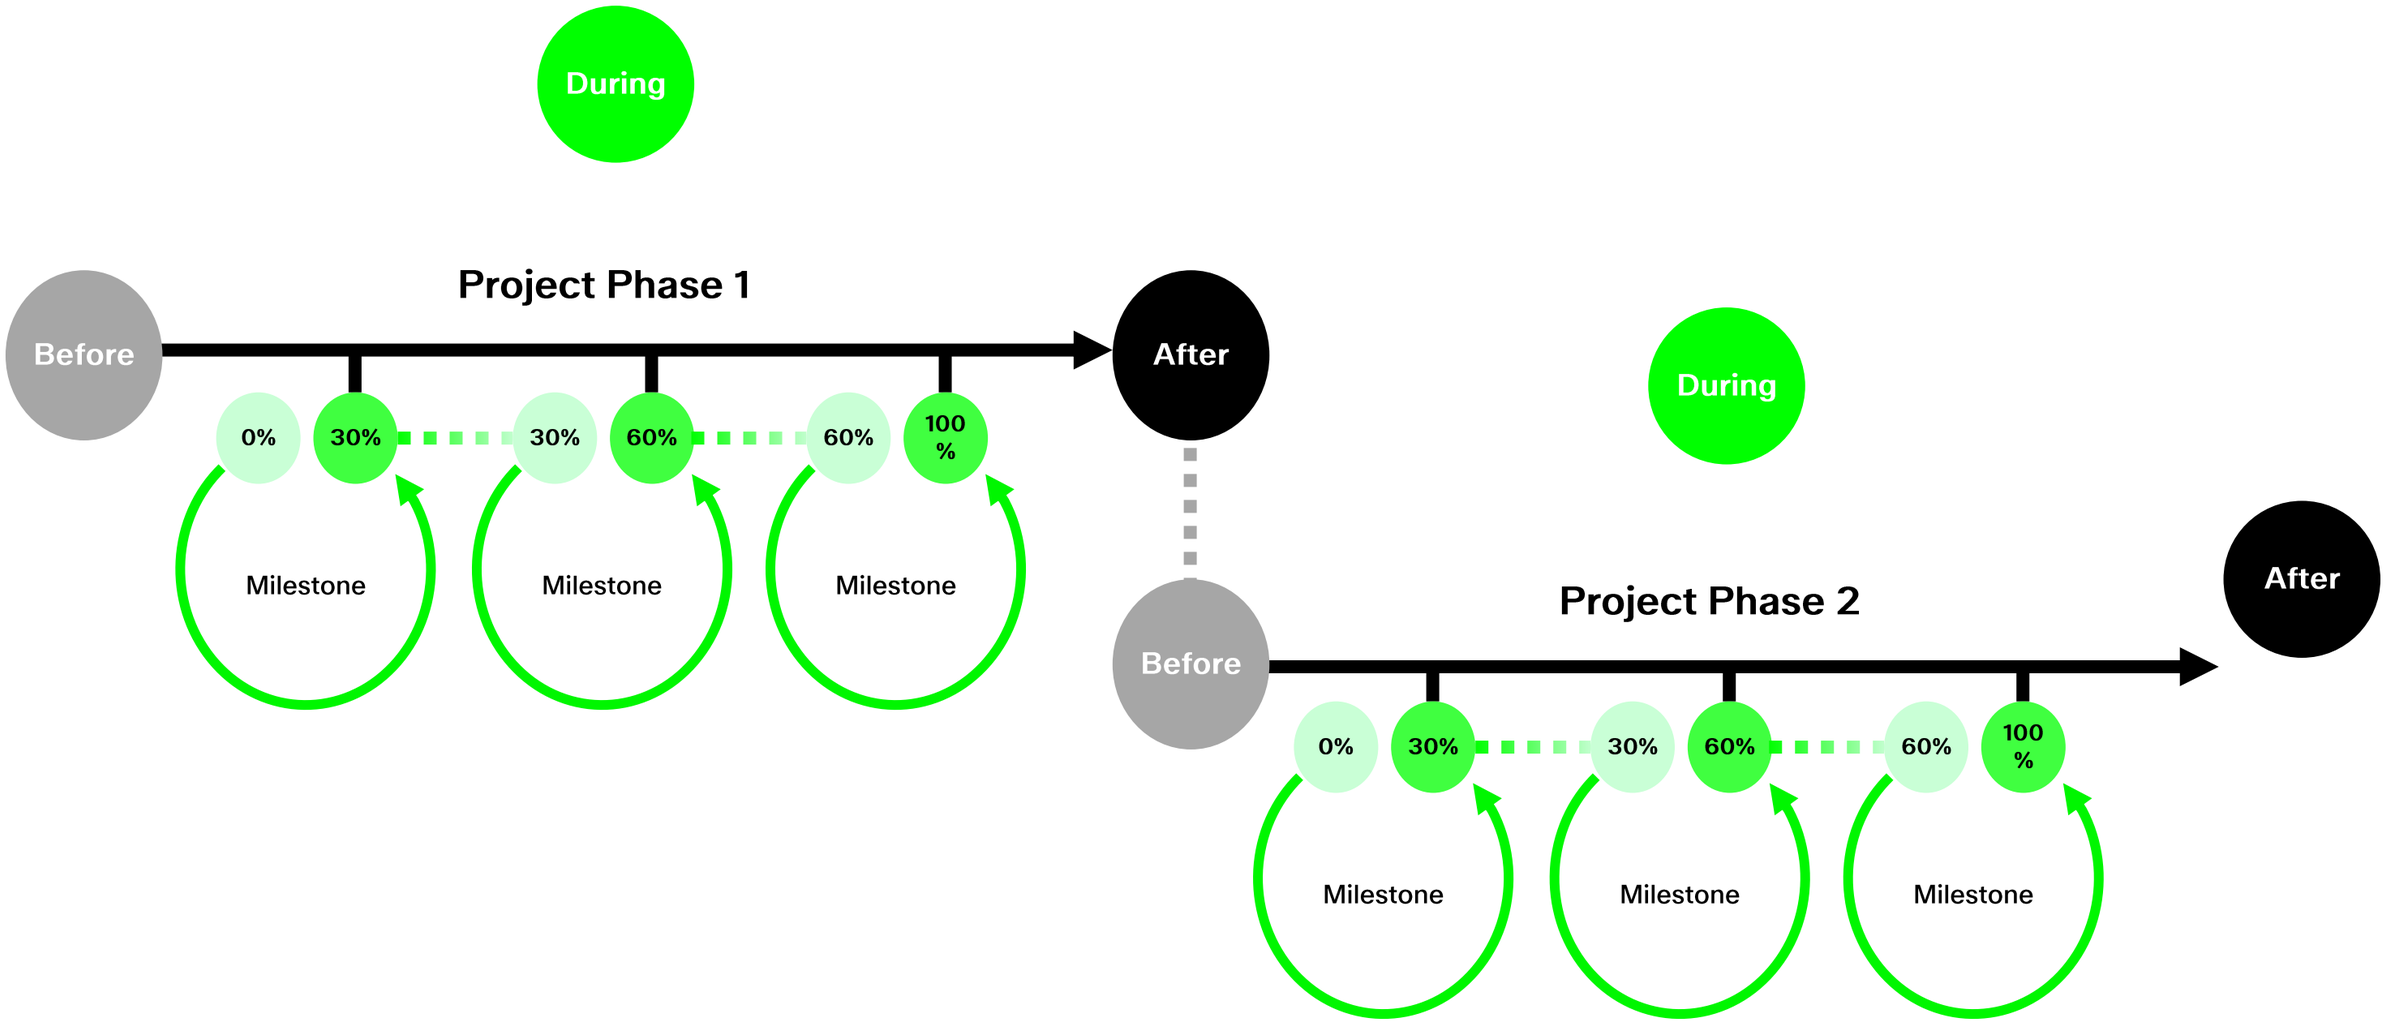

1.7 PROJECT COMPETENCIES

WHAT ARE THE PROJECT CORE COMPETENCIES ?

According to global practice, areas of focus for project management are driven by constraints.
LAVA's processes should be **streamlined and design-driven.**
Instead of 10 competencies, only 3 are defined.

Project Management Institute. PMP

INTEGRATION MANAGEMENT	**SCOPE MANAGEMENT**	**SCHEDULE MANAGEMENT**	**COST MANAGEMENT**	**RESOURCING MANAGEMENT**
QUALITY MANAGEMENT	**RISK MANAGEMENT**	**PROCUREMENT MANAGEMENT**	**STAKEHOLDERS MANAGEMENT**	**COMMUNICATIONS MANAGEMENT**

LAVA


PLANNING
SCOPE, SCHEDULE, COST & RESOURCES


EXECUTION
DESIGN, COORDINATION, COMMUNICATIONS

KNOWLEDGE MANAGEMENT
DATA, FILES & DOCUMENTATION

1.8 PROJECT PROCESSES FRAMEWORK

WHAT ARE OUR PROJECT PROCESSES ?

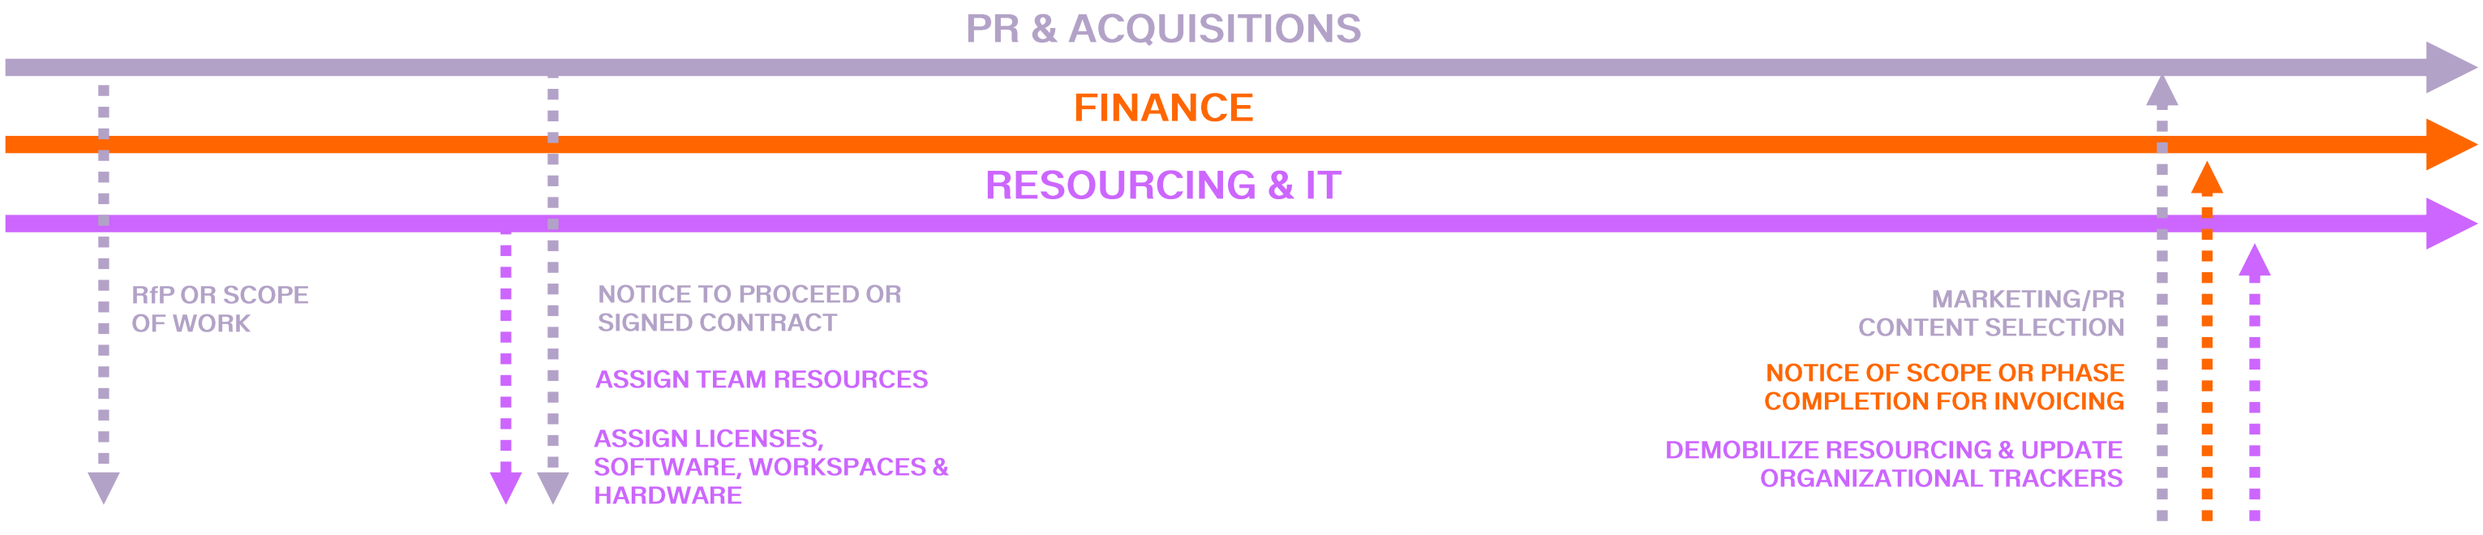

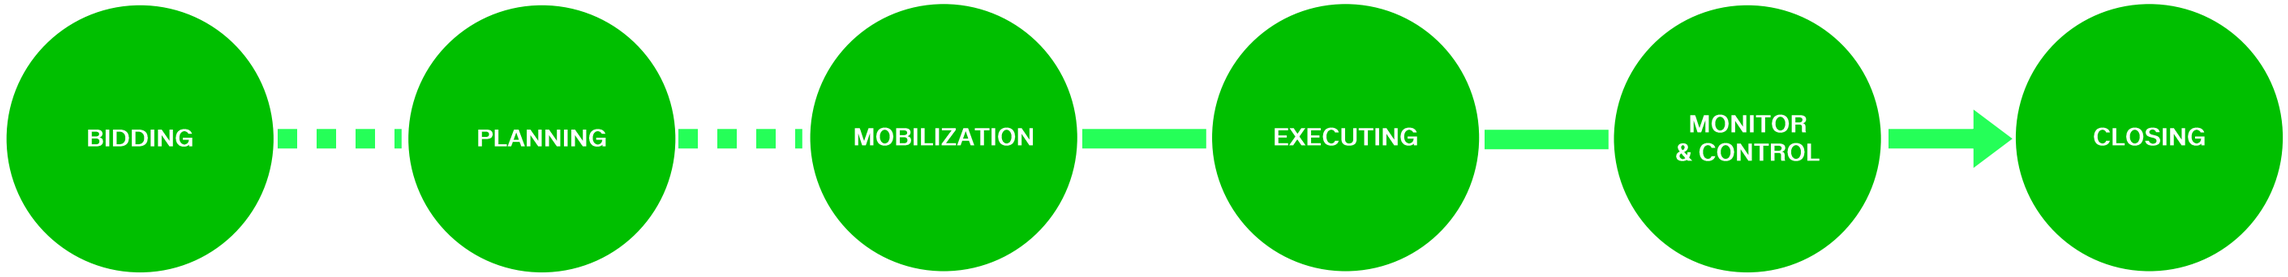

- CONFIRM INTEREST IN BIDDING
- ASSIGN BID CODE
- ASSIGN DIRECTOR & PM TEAM
- NDA SIGNATURES
- PROJECT CHECKLIST
- CONTACT SUBCONSULTANTS
- TECHNICAL PROPOSAL
- COMMERCIAL PROPOSAL

- ASSIGN PROJECT CODE
- ASSIGN PROJECT LEAD
- EXECUTE CONTRACTS
- FOLDER STRUCTURES
- ASSIGN RESOURCES
- ROUTEMAP / SCHEDULE
- PROJECT DIRECTORY
- DELIVERABLES LIST
- UPDATE ORG PLANNING

- RESOURCE DEPLOYMENT
- INTERNAL KICK-OFF
- VISION
- OBJECTIVES
- ROLES & RESPONSIBILITIES
- QUALITY ASSURANCE
- TEMPLATES
- CODES & STANDARDS

- RESEARCH & ANALYSIS
- DESIGN STUDIES
- DESIGN OPTIMIZATION
- DESIGN DEVELOPMENT
- COORDINATION
- COMMUNICATIONS
- DIGITAL COLLABORATION
- DRAWINGS & DIAGRAMS

- CLIENT REPORTING
- DESIGN TEAM MEETINGS
- PARTNER REVIEWS
- ADDRESS COMMENTS
- QUALITY CONTROL
- SCOPE CONTROL
- SCHEDULE CONTROL
- RESOURCE CONTROL
- VARIATIONS / CHANGES
- UPDATE PLANNING

- SUBMIT DELIVERABLES
- ARCHIVE ON SERVER
- SELECT PR CONTENT
- FILL PROJECT FACTSHEET
- DEBRIEF TEAM
- DEMOBILIZE RESOURCING
- LESSONS LEARNED

BEFORE THE PROJECT

DURING THE PROJECT

AFTER THE PROJECT

1.8 PROJECT PROCESSES FRAMEWORK

WHAT ARE OUR PROJECT PROCESSES ?

	BEFORE THE PROJECT	DURING THE PROJECT	AFTER THE PROJECT
PLANNING SCOPE, SCHEDULE, COST & RESOURCES	○ REVIEW RFP AND CLIENT BRIEFING ○ PREPARE PROJECT CHECKLIST ○ CONTACT SUB-CONSULTANTS & OBTAIN NDA SIGNATURES ○ DELINEATE SCOPE RESPONSIBILITIES ○ COORDINATE OFFERS FROM SUBCONSULTANTS ○ ESTIMATE LAVA RESOURCING REQUIREMENTS ○ PRODUCE TECHNICAL PROPOSAL ○ SUPPORT DIRECTOR WITH COMMERCIAL PROPOSAL	○ CONFIRM PROJECT LEADERSHIP & ROLES ○ PRODUCE TIMELINE ○ PRODUCE DELIVERABLES LIST ○ PRODUCE PROJECT DIRECTORY ○ EXECUTE CONTRACTS ○ DEFINE COMMUNICATIONS PLAN ○ UPDATE PLANNING AS REQUIRED ○ UPDATE PROJECT CHECKLIST AS REQUIRED ○ SCOPE, TIME & RESOURCE CONTROL ○ CHANGE MANAGEMENT & VARIATIONS TO CONTRACT	○ NOTIFY FINANCE TEAM OF MILESTONE SUBMISSIONS
EXECUTION DESIGN, COORDINATION & COMMUNICATIONS		○ MOBILIZE RESOURCING ○ CONDUCT INTERNAL LAVA KICKOFF ○ IDENTIFY LAVA THEMES & PROJECT VISION ○ SET UP REPORTING TEMPLATES ○ ASSIGN INTERNAL TEAM RESPONSIBILITIES ○ DEFINE TASKS & ACTIVITIES ○ INQUIRE : CONDUCT RESEARCH & ANALYSIS ○ IMAGINE : EXPERIMENT & TEST OPTIONS ○ INVENT : DEVELOP INNOVATIVE DESIGN ○ CONDUCT COORDINATION WITH ALL PARTIES ○ PROGRESS REPORTING TO CLIENT ○ BIWEEKLY REPORTING TO PARTNERS ○ ADDRESS FEEDBACK FROM ALL PARTIES ○ TRACK ISSUES & RESOLVE INTERNALLY ○ QUALITY CONTROL ○ SUBMIT MILESTONE PACKAGES	○ COMPLETE STAGE GATE REVIEWS ○ ADDRESS CLIENT COMMENTS AS NEEDED ○ SELECT BEST DIAGRAMS AND IMAGES OF PROJECT ○ FILL PR QUICKLINKS SHEET ○ DEBRIEF TEAM AND PROVIDE FEEDBACK ○ COMMUNICATE LESSONS LEARNED ○ DEMOBILIZE TEAM RESOURCING
KNOWLEDGE MANAGEMENT DATA, COLLABORATION TOOLS, & DOCUMENTATION	○ ASSIGN BID CODE ○ CREATE BID FOLDER STRUCTURE ON SERVER ○ SET UP SHAREPOINT FOR BID IF REQUIRED ○ ARCHIVE BIDDING DOCUMENTS & INPUTS FROM CLIENT ○ ARCHIVE SUBCONSULTANTS NDA SIGNATURES ○ ARCHIVE SUBCONSULTANTS OFFERS & INPUTS	○ ASSIGN PROJECT CODE ○ CREATE PROJECT FOLDER STRUCTURE ON SERVER ○ SET UP DIGITAL COLLABORATION TOOLS ○ SET UP EXTERNAL COMMUNICATION CHANNELS ○ ARCHIVE ALL OUTGOING AND INCOMING FILES ○ IMPLEMENT FILE NAMING CONVENTIONS	○ ARCHIVE EDITABLE FILES FOR DIAGRAMS ○ ARCHIVE ALL MILESTONE SUBMISSIONS ○ SHUT DOWN DIGITAL COLLABORATION TOOLS ○ FILL PROJECT FACTSHEET ON SERVER

02


BEFORE THE PROJECT

2 BEFORE THE PROJECT


WHAT TAKES PLACE BEFORE THE PROJECT ?

Building on LAVA's PR and Acquisitions activities by leadership, LAVA is often invited by potential Clients to work on Projects - produce designs, fulfill certain roles, or deliver services and deliverables. Two key processes are identified at this stage :


1. **Bidding** – The initial form of Planning. Before we start a Project, LAVA might need to reach an **Agreement** with Clients. This takes place after an offer is extended by LAVA including **Technical and Commercial Proposals** for a specific project, and it is accepted by the Client.
2. **Project Checklist** - In parallel to Bidding, it is also required to review any documents received from Clients such as **RfPs (Requests for Proposals)**, **Service Agreements (Contractual documents)** and any potential **Supporting Documents** which might contain data or information relevant for the project.

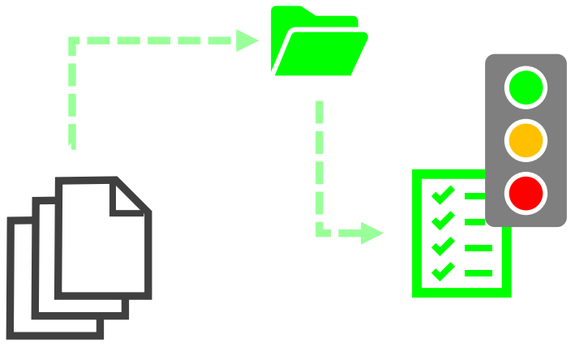

1. **Initial Briefing and Information** for the Project provided by the Client must be archived and reviewed to determine if, and how, LAVA can do a project

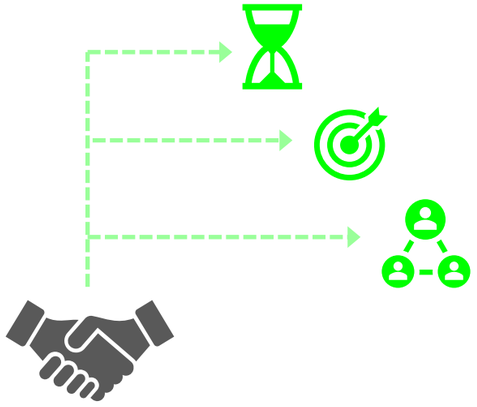

2. **Constraints for the Project including Time, Scope and Resourcing** are defined via Bidding and must be closely monitored during the project by leadership

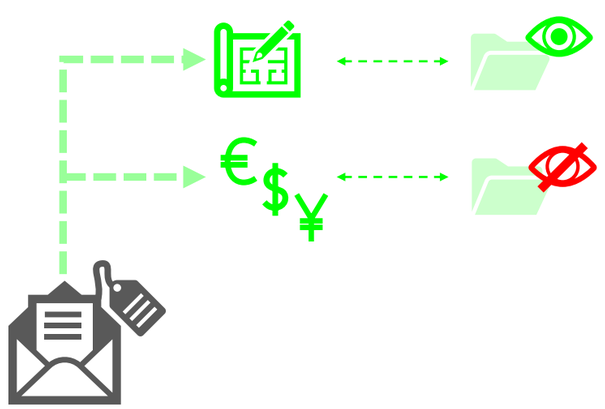

3. **Technical and Commercial proposals** are closely related, but must be produced, stored and submitted separately by LAVA to Clients

2.1 BEFORE THE PROJECT


WHO IS RESPONSIBLE FOR WHAT BEFORE THE PROJECT ?

	PARTNERS	DIRECTORS	PR & ACQUISITIONS	PROJECT MANAGEMENT	OFFICE MANAGEMENT	STAFF
1. Initiation	Engage in Acquisitions activities prior to Bidding such as **submitting Qualifications** to prospective clients. Review RfPs and **decide** to bid on a Project.		**Informed. Liaise** with Client. **Collect and submit** Bid documents via Ariba or similar platforms.		**Responsible.** Create a **Bidding Code** for the project on Poolarserver upon confirmation.	
			Confirmation to Bid		Confirmation to create a Bid Code	
2. Portfolio, Company Info & CVs	**Consulted.** Review the documents and approve updates for use in PR & Acquisitions or Bidding.		**Responsible.** Maintain the latest **Company Info** and **Portfolio** which can be used at any given time for Bidding.	**Informed.** For Bidding, uses the latest **PR & Acquisitions Documents and CVs** as updated by others.		**Responsible.** Ensure individual **CVs** are updated on the Server every 6 months at a minimum.
	Review & Confirm Documents				Update CVs	
3. Project Checklist	**Informed.** Given a summary of project viability by Director based on Checklist.	**Accountable.** Reviews Project Checklist and determine viability of project during Bidding.	**Consulted.** Ensure documents transmitted via platforms such as Ariba are shared with Director/PM.	**Responsible.** Review initial documents and fill out Project Checklist during Bidding.		
	Summarize Viability of Project		Prepare Project Checklist			
4. Technical Proposal	**Consulted.** Review and confirm the selected Consultants. Review the Technical Proposal and provide feedback if required.	**Accountable.** Ensure that Technical Proposal preparation and choice of Subconsultants is conducted. May delegate tasks to PM.	**Informed. Submit** the Technical Proposal once it is shared by Director or Project Management.	**Responsible.** Collaborate with Director on Technical Proposal content, **organize bidding files**, communicate with all Subconsultants and ensure **NDAs** are signed.		May support PM Team with preparation of Technical Proposal content if required and appointed by Director / Partner.
	Review & Confirm		Prepare Technical Proposal			
5. Commercial Proposal	**Consulted.** Review and approve the fees prior to submission to the Client.	**Responsible.** Ensure that fees are estimated and Commercial Proposal is prepared accordingly. May request support from PM.	**Informed. Submit** the Commercial Proposal once it is shared by Director or Project Management.	**Consulted.** Support Director with collection of fee proposals from Subs, with estimating of resourcing and of time requirements for the Project.		
	Prepare Commercial Proposal		Support			

2.1 BIDDING

WHAT ARE THE CORE PROCESSES USED IN BIDDING ?

1. **Technical Proposal** – *Company Information, CVs, Methodology, etc.*
2. **Commercial Proposal** – by *Fee Estimation Team*
3. **Portfolio** – *Selected Projects from LAVA*
4. **Bidding Code** – *Unique Code assigned by Administration.*

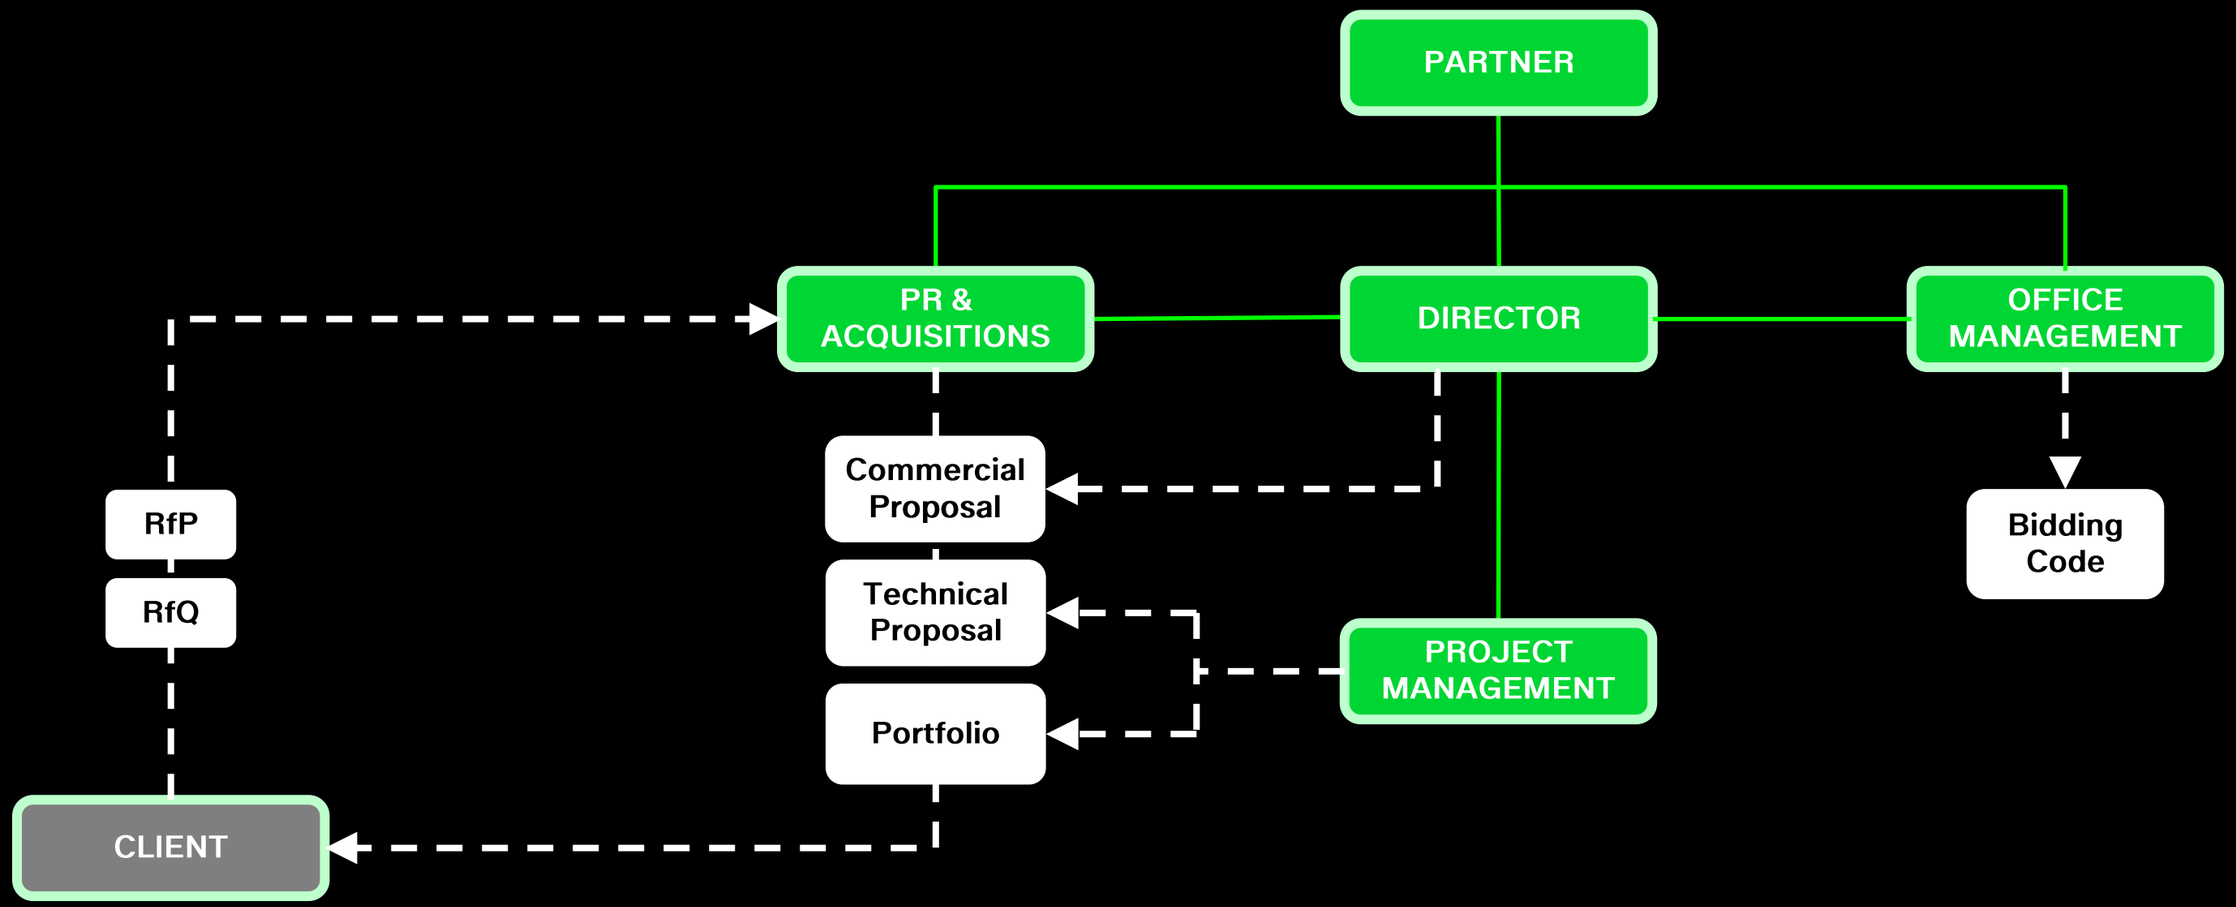


2.1.1 BIDDING CODE

WHAT IS THE BIDDING CODE ?

A unique code or reference number is assigned to a specific tender or bid package when it's put out for proposals.

It is used to keep track of submission documents when multiple bids are being handled and for staff to log their hours invested working on each proposal on Poolarserver accordingly.

Bids are to be archived on a **separate server network**, mapped to a **drive (Q)** next to the projects drive for convenience.

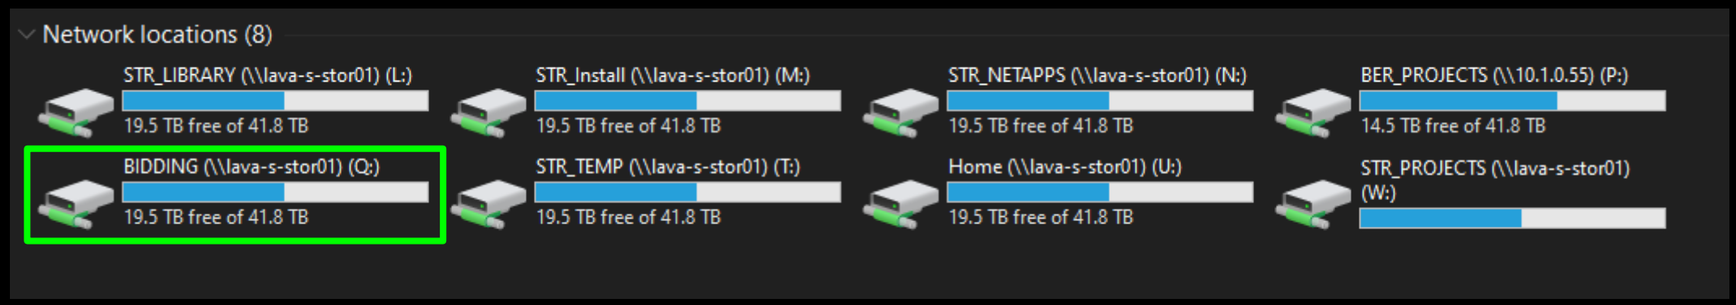

2.1.1 BIDDING CODE

WHAT IS THE BIDDING CODE ?

Multiple options for the Bidding Code system are proposed below, **subject for approval** by the Directors/Partners and subsequently to be instructed for implementation by the Administration and any staff engaged in Bidding.

Bidding code format :

- **BID-YY-NNN**
- **BID-25-001**

Naming has a different segments as projects:

<BID Code>_<Bid Short Name>


Poolarserver & local server folder numbering:

BID – <YEAR NUMBER> – <BID NUMBER>_<BID SHORT NAME>

BID-25-001_XYZ

Option 2 for Bidding Code format to simplify number for quick search :


- **BYYNNN**
- **B25001**

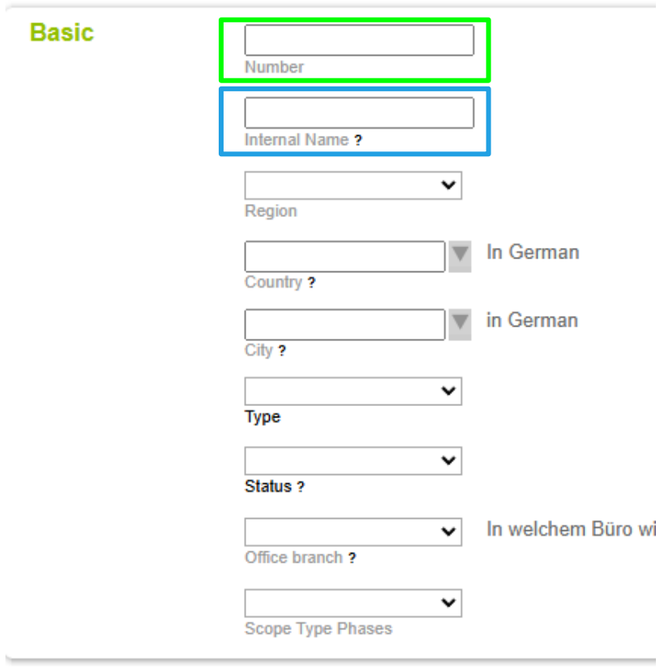

2.1.2 TECHNICAL PROPOSAL

WHAT IS A TECHNICAL PROPOSAL ?

Certain templates and documents are repetitively used for Bids based on a common standard or templates. All of these are not new documents, but are readily available, and would be clearly placed on the Server moving forward.

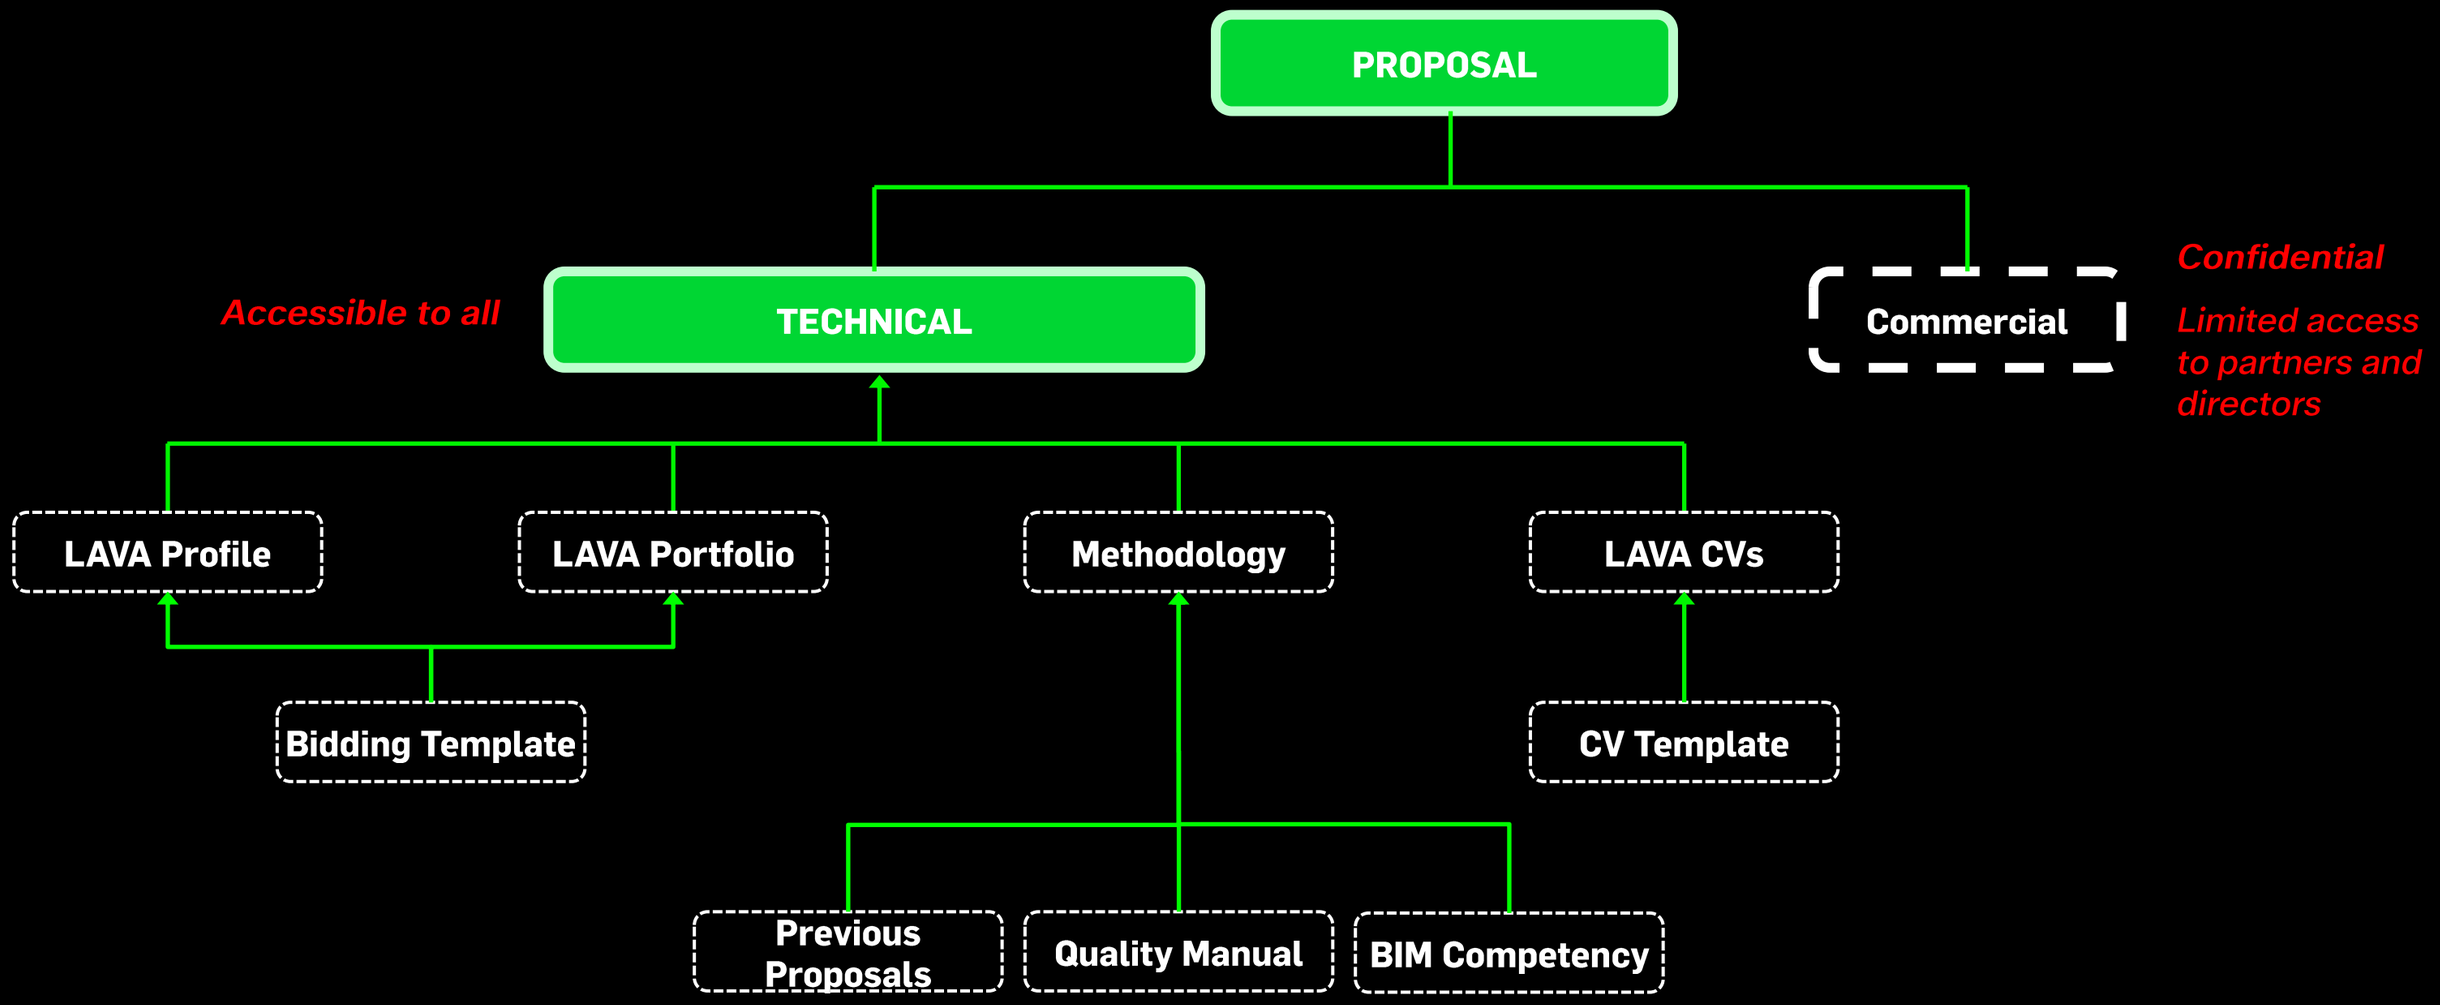


2.1.2 TECHNICAL PROPOSAL

ARCHIVING BIDDING CONTENT ON THE LAVA SERVER


Putting **Technical Proposals** together requires using established/approved templates such as Company Information and the Portfolio which is easily accessible.

Previous or Ongoing Work on Bids equally needs to be stored on the Server accordingly.

Commercial Proposals will be stored separately and only accessible to select few at LAVA.

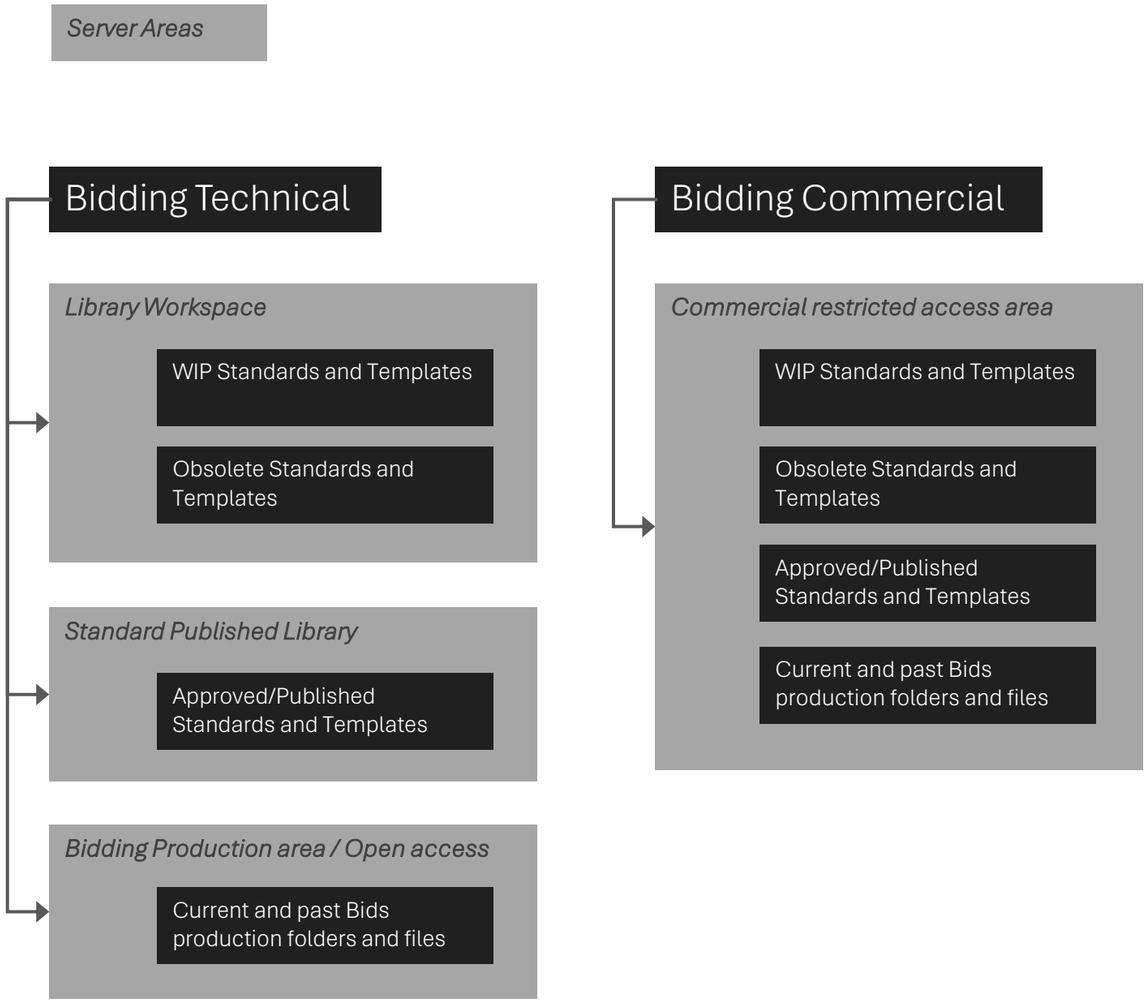

Content usage and development workflow

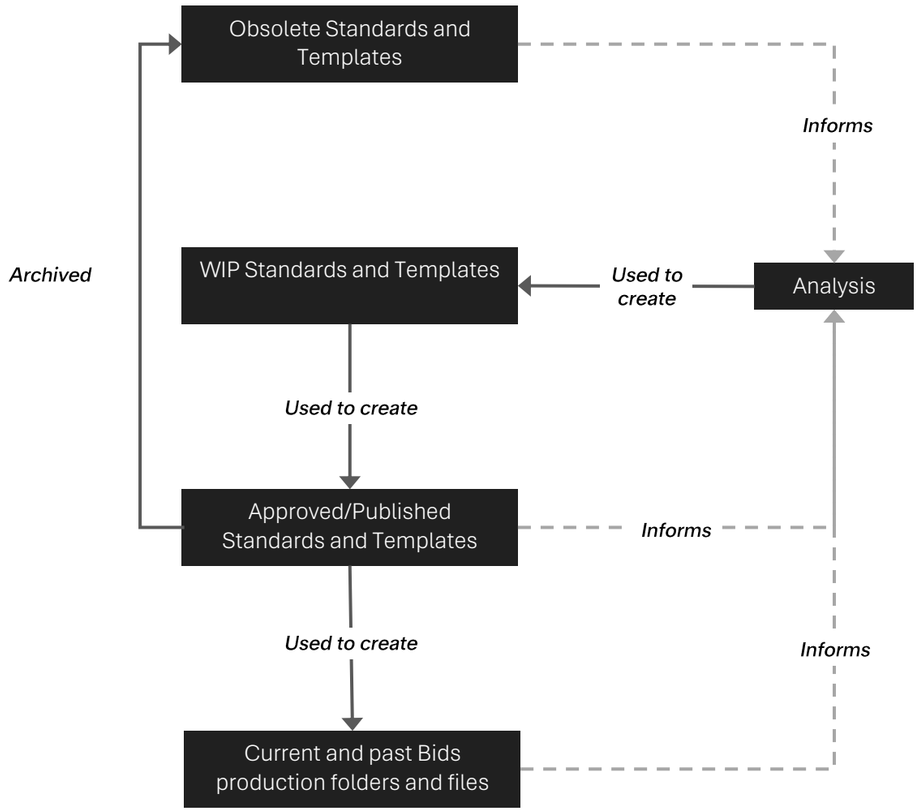

2.1.2 TECHNICAL PROPOSAL

ARCHIVING BIDDING CONTENT ON THE LAVA SERVER

Putting **Technical Proposals** together requires using established/approved templates such as Company Information and the Portfolio which is easily accessible.


Previous or Ongoing Work on Bids equally needs to be stored on the Server accordingly.

Commercial Proposals will be stored separately and only accessible to select few at LAVA.

For **WIP bidding standard documents and templates** and archiving old versions. Files under development which are not for use.

Approved / finished documents and templates to be published to Standard LAVA Library
Similar concept of 2 areas (workspace + standard library) will be applied to all topics in the Library

Hidden Library Workspace Area on Server

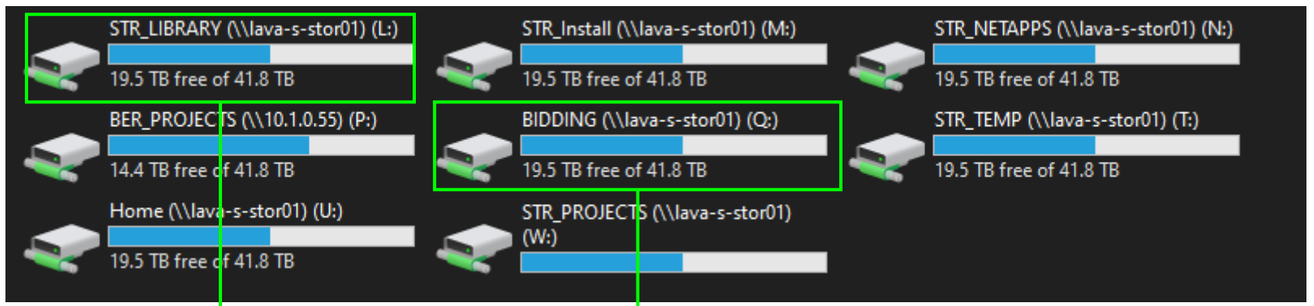

LAVA Standard Library, containing Bidding **Templates and standards** to be used in new Bids

LAVA Bidding Folder
Bidding workspace / production area
Similar to Projects drive/workspace/production area
One folder per Bid

2.1.2 TECHNICAL PROPOSAL

WHERE TO FIND BIDDING TEMPLATES ON THE LAVA SERVER


Bidding Templates are the standard documents any employee at LAVA could access, and might be required to use when putting together a Technical Proposal. This includes the latest versions of the Company Profile, the Portfolio, CVs and other relevant content for Bidding (InDesign and PDF files). **Content approved by leadership only.**

LAVA Main Library Folders (Topics)

Bidding Folders Level 1

Bidding Folders Level 2

Bidding Folders Level 3

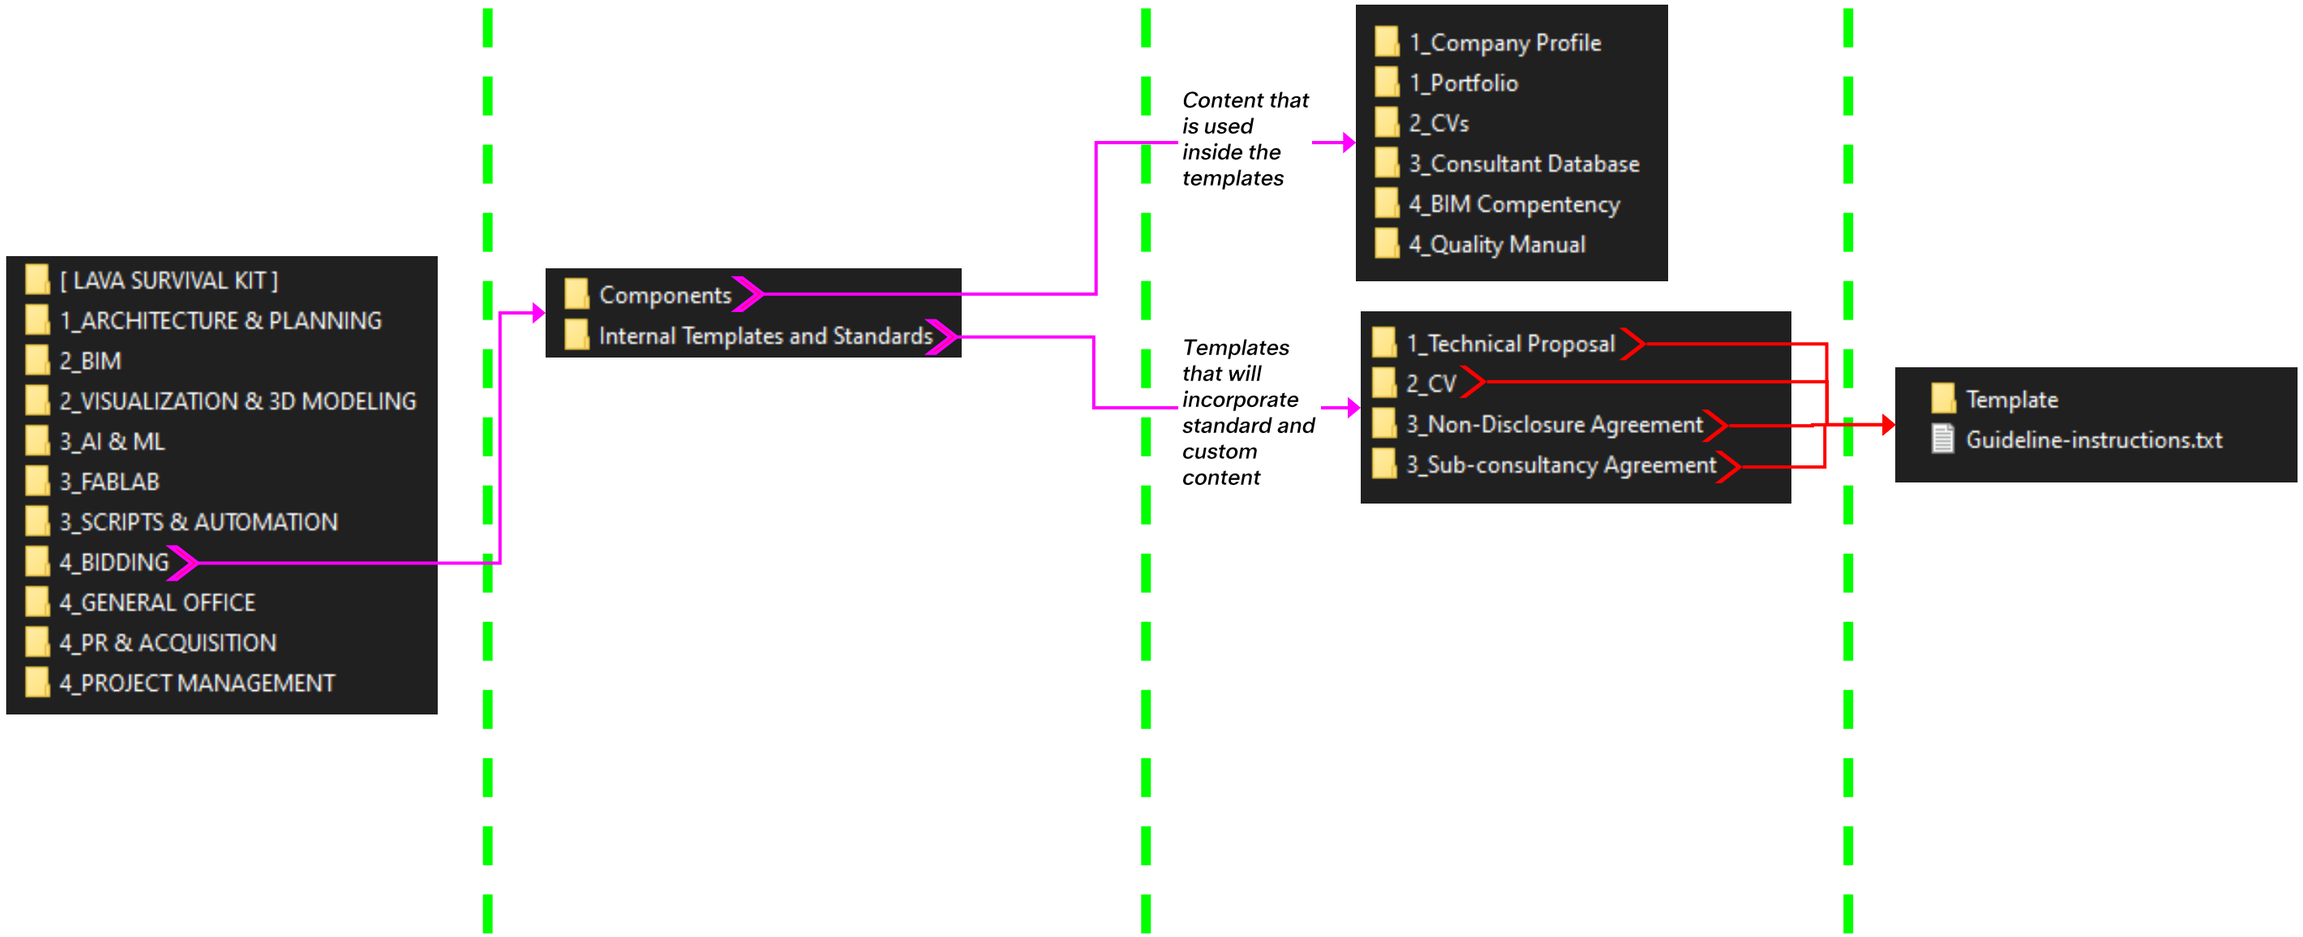


2.1.3 COMPANY INFORMATION


WHAT IS COMPANY INFORMATION?


The **Company Information** provides an Introduction to LAVA, profiling **who we are**, our **office locations**, our list of **awards** and what our **philosophy** and **methodology** is in when it comes to architecture. The company information relatively remains the same, but it might be updated every once in a while to align with LAVA's **Corporate Identity (CI)**; hence, it is separated from the Portfolio InDesign file.

- **LAVA Profile**
  - LAVA Introduction
  - LAVA Philosophy
  - LAVA Offices
  - LAVA Projects
  - LAVA Design Themes
  - LAVA Awards & Recognition

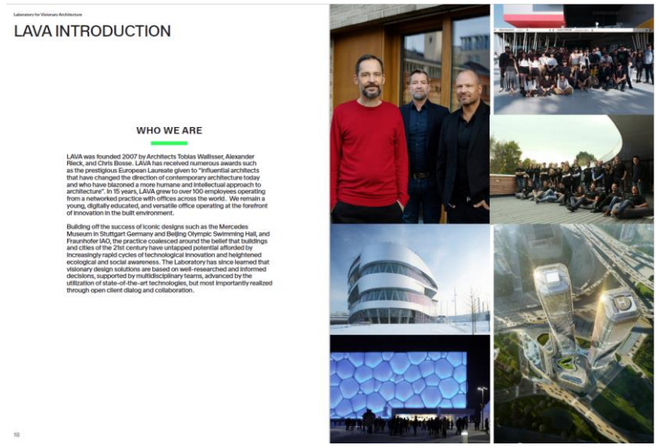



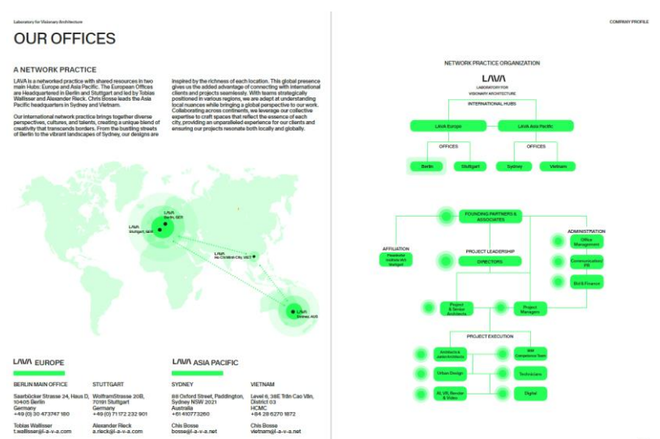

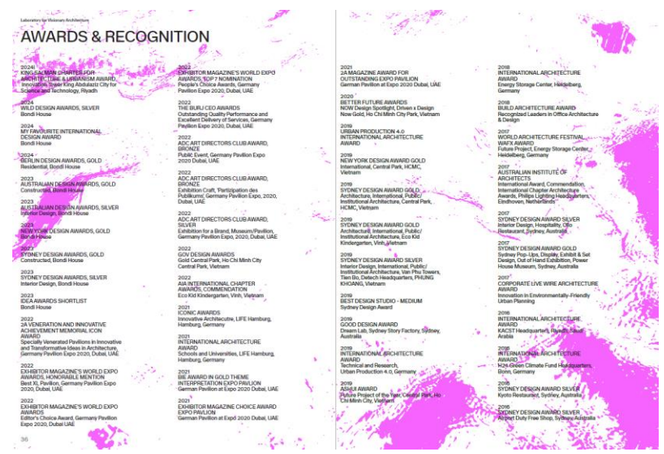

2.1.4 PORTFOLIO & SELECTED PROJECTS

WHERE TO FIND THE LAVA PORTFOLIO & SELECTED PROJECTS ?

Each Technical Proposal should include **Selected Projects** relevant to the brief, to demonstrate our suitability to the Client depending on the required scope. Projects are to be selected from the latest **LAVA Portfolio** which is extensive and curates our best projects based on **Themes** and **Project Typologies.**

LAVA Portfolio


indesign file which can be edited as required

Projects to be selected according to :

- **RFP**
- **Project Themes**
- **Project Typology** (Vertical Building, Masterplan, etc...)





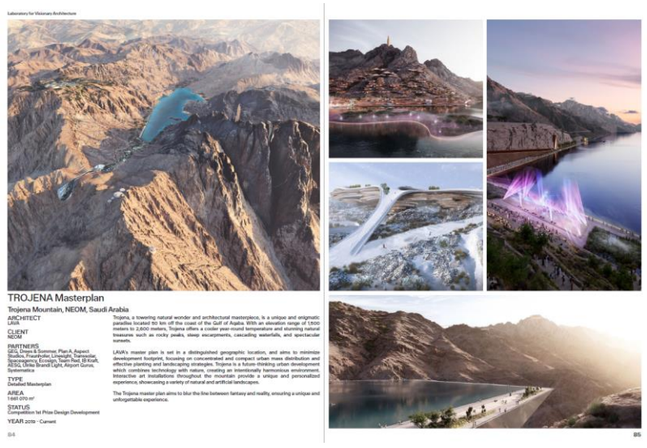



2.1.5 CVs

WHERE TO FIND THE LAVA STAFF CVs ?

Each Technical Proposal should include **Key Personnel CVs** to reflect the experience and skillsets required by the Client for the Project we are bidding on. Each proposal should include at least one partner and director CV respectively to reflect the leadership anticipated to work on the Project. Additionally, the number of CVs should be coordinated with the client's briefing and proportional to our proposed resourcing (align with Commercial Proposal)


LAVA CV

indesign file with fixed elements

CVs to follow the exact format found here:

W:\00_Project_proposals

CVs to be updated by every person every 6 months.

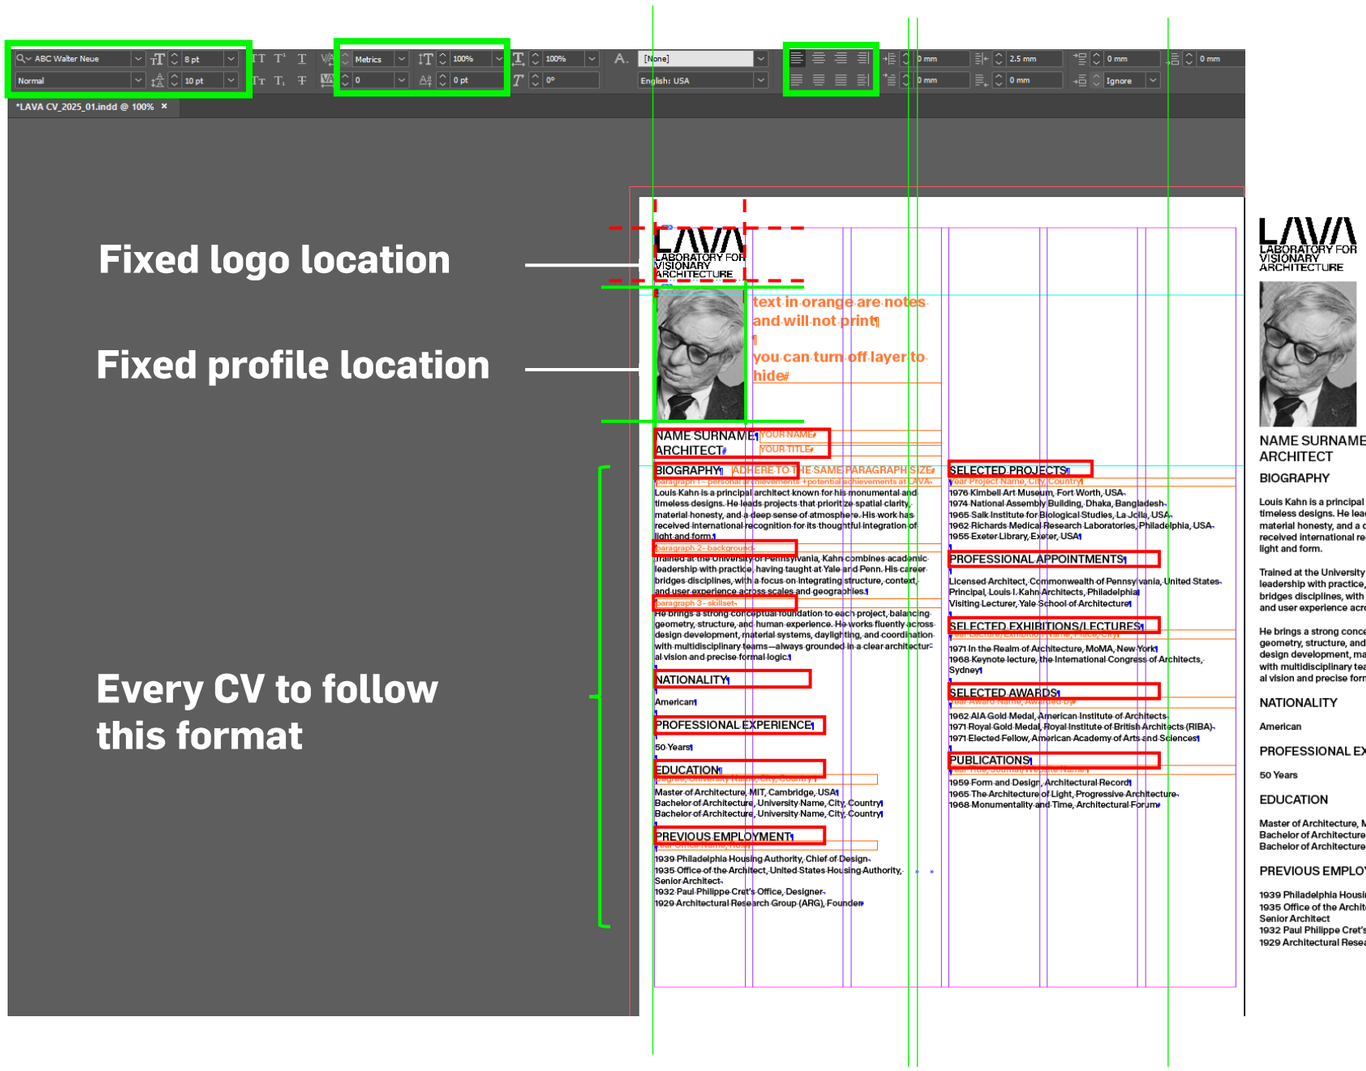

2.1.6 EXTERNAL COORDINATION

HOW TO EXCHANGE INFORMATION WITH SUBCONSULTANTS ?

Some projects require SMEs (Subject Matter Experts) to cover certain disciplines under LAVA as a Lead Consultant. During Bidding, a step-by-step process must be followed to **ensure confidentiality** while **sharing information to facilitate discussions** with potential companies that might be interested in being part of our Project Team.

Step 1: Create a SharePoint for External Communications

- Create a **dedicated folder structure** for a particular Bid

Step 2: Set Permissions Carefully

- Set up common folders for sharing **project briefing documents** from the Client (e.g. RfP, Contract, Procedures, etc.)
- **Internal Inputs - LAVA**: Only internal team has access.
- **External Inputs - Consultants**: Give ***Can Edit*** access to consultants. Don't let consultants see each other's technical and/or commercial proposals. You can use individual folders with specific permissions:
    - Consultant A can only see and upload to their folder
    - Consultant B can only see and upload to their folder

Step 3: Contact prospective Subconsultant(s)

- Send e-mail to confirm their interest in reviewing RfP documents – **do not share any details or documents at this stage**
- Attach an **NDA (Non-Disclosure Agreement) template** and request signature.
- Following NDA signature, **share RfP documents** and provide access to **LAVA Sharepoint** as described in Step 2

Step 4: Coordinate Proposals from Subconsultant(s)

- Request any necessary information to support compilation of the **Technical and Commercial Proposal**
- **Ensure confidentiality** as described in Step 2


2.1.6 EXTERNAL COORDINATION

HOW TO EXCHANGE INFORMATION WITH SUBCONSULTANTS ?


1. Creation of bidding folder for each new bid

Only internal access


Separate external access




2. Grant access to each consultant alone

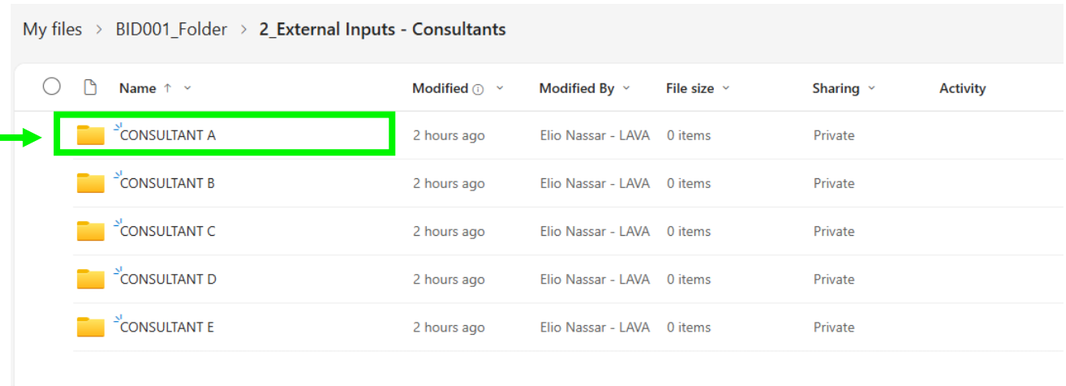

- Right-click on each consultant's folder > "Share" > "Grant Access"
- Share links individually with each consultant

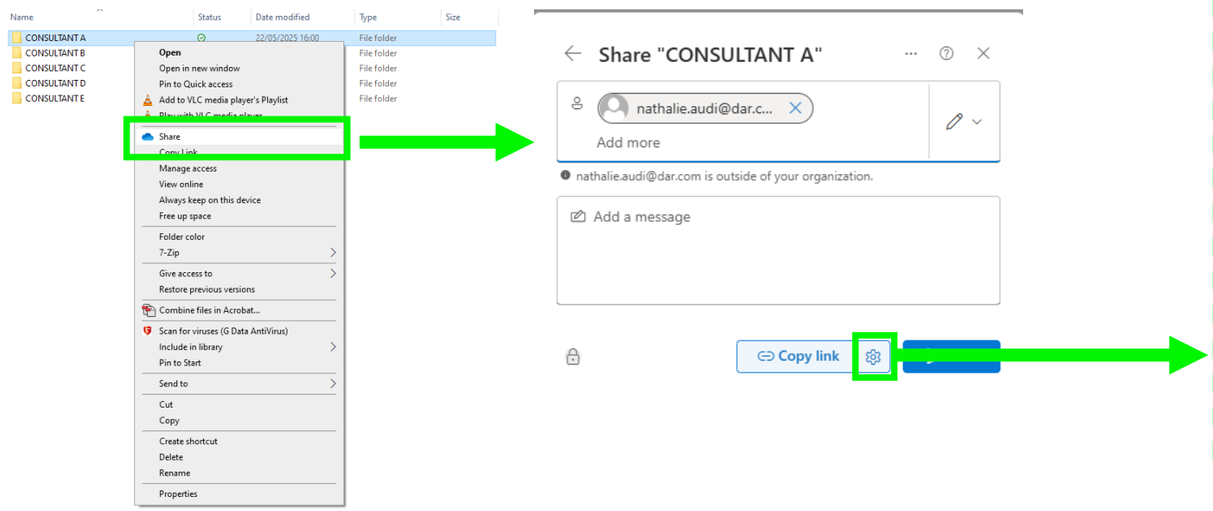

Ensure complete privacy and only access to their correspondent folder

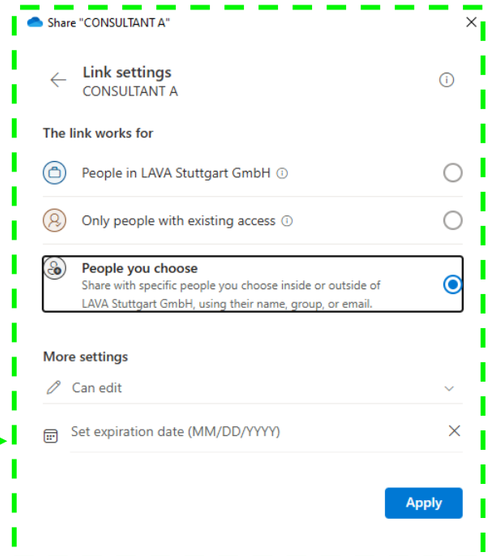

2.1.7 CONFIDENTIALITY & NDAs

WHAT IS A NON-DISCLOSURE AGREEMENT ?

Confidentiality is often a strict, legal and contractual requirement which LAVA is obliged to follow. Often, LAVA signs an **NDA (Non-Disclosure Agreement)** with the Client during Bidding, or later during the Project phases, before receiving any specific project documentation. By extension, LAVA is required to ensure any parties which receive the same project documents (e.g. potential Sub-Consultants during Bidding) are also committed to the NDA.

Ensure the document is **signed before sharing Bidding or Project documents**, and that the **NDA is archived accordingly.**

Receiving Party is the subconsultant's information:

Registered Company Name,

Address Line 1

Address Line 2


Disclosing Party is LAVA's information :

Registered Company Name,

Address Line 1

Address Line 2

Project-specific references in the text must be updated as highlighted to the right

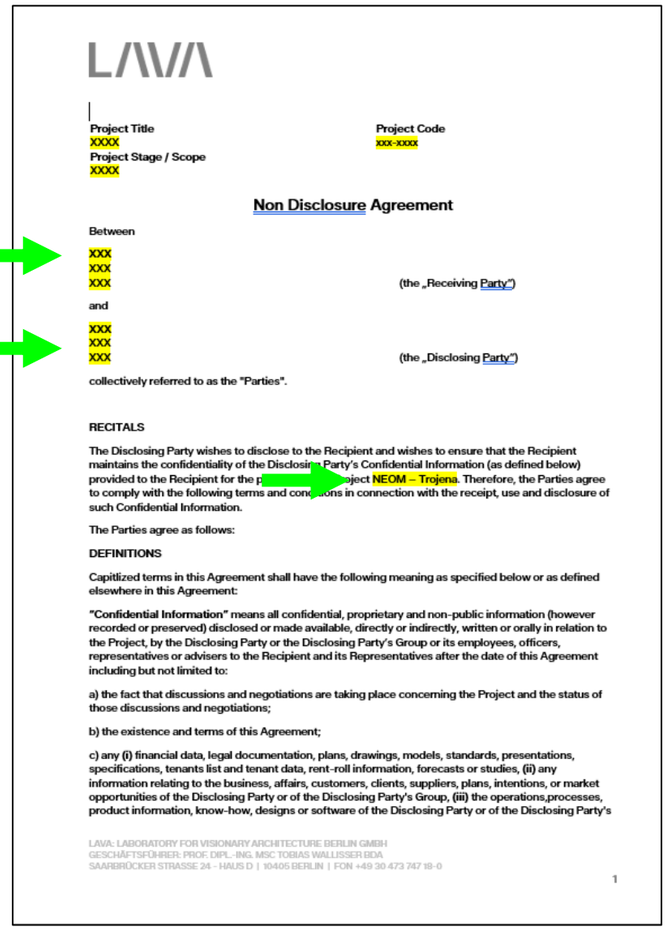

LAVA

Project Title
XXXX
Project Stage / Scope
XXXX

Project Code
xxx-xxxx

Non Disclosure Agreement

Between

XXX
XXX
XXX (the „Receiving Party")

and

XXX
XXX
XXX (the „Disclosing Party")

collectively referred to as the "Parties".

RECITALS

The Disclosing Party wishes to disclose to the Recipient and wishes to ensure that the Recipient maintains the confidentiality of the Disclosing Party's Confidential Information (as defined below) provided to the Recipient for the project NEOM – Trojena. Therefore, the Parties agree to comply with the following terms and conditions in connection with the receipt, use and disclosure of such Confidential Information.

The Parties agree as follows:

DEFINITIONS

Capitilized terms in this Agreement shall have the following meaning as specified below or as defined elsewhere in this Agreement:

"Confidential Information" means all confidential, proprietary and non-public information (however recorded or preserved) disclosed or made available, directly or indirectly, written or orally in relation to the Project, by the Disclosing Party or the Disclosing Party's Group or its employees, officers, representatives or advisers to the Recipient and its Representatives after the date of this Agreement including but not limited to:


a) the fact that discussions and negotiations are taking place concerning the Project and the status of those discussions and negotiations;

b) the existence and terms of this Agreement;

c) any (i) financial data, legal documentation, plans, drawings, models, standards, presentations, specifications, tenants list and tenant data, rent-roll information, forecasts or studies, (ii) any information relating to the business, affairs, customers, clients, suppliers, plans, intentions, or market opportunities of the Disclosing Party or of the Disclosing Party's Group, (iii) the operations,processes, product information, know-how, designs or software of the Disclosing Party or of the Disclosing Party's

LAVA: LABORATORY FOR VISIONARY ARCHITECTURE BERLIN GMBH
GESCHÄFTSFÜHRER: PROF. DIPL.-ING. MSC TOBIAS WALLISSER BDA
SAARBRÜCKER STRASSE 24 – HAUS D | 10405 BERLIN | FON +49 30 473 747 18-0

1

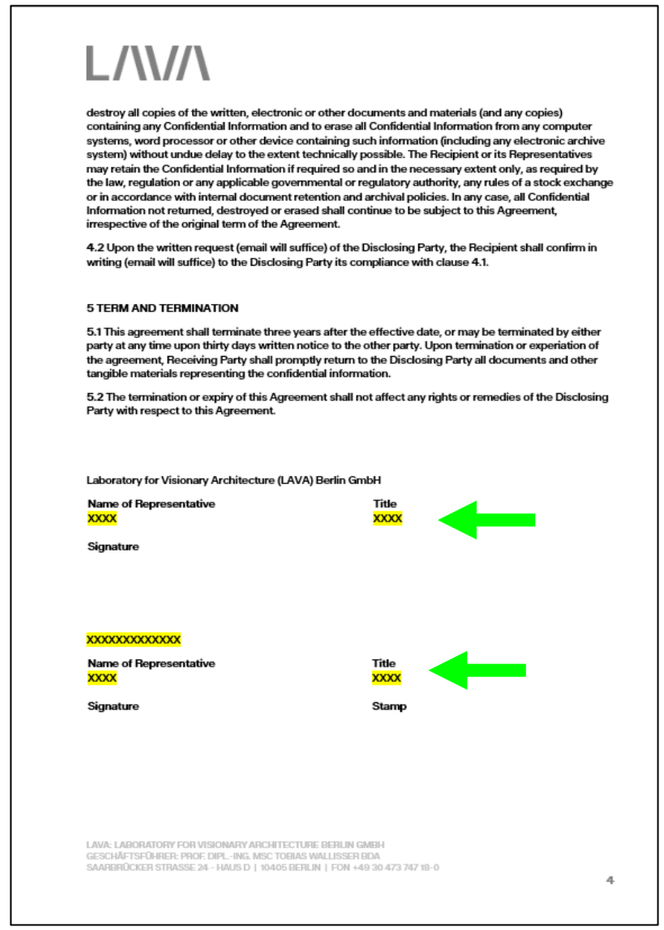

LAVA

destroy all copies of the written, electronic or other documents and materials (and any copies) containing any Confidential Information and to erase all Confidential Information from any computer systems, word processor or other device containing such information (including any electronic archive system) without undue delay to the extent technically possible. The Recipient or its Representatives may retain the Confidential Information if required so and in the necessary extent only, as required by the law, regulation or any applicable governmental or regulatory authority, any rules of a stock exchange or in accordance with internal document retention and archival policies. In any case, all Confidential Information not returned, destroyed or erased shall continue to be subject to this Agreement, irrespective of the original term of the Agreement.

4.2 Upon the written request (email will suffice) of the Disclosing Party, the Recipient shall confirm in writing (email will suffice) to the Disclosing Party its compliance with clause 4.1.

5 TERM AND TERMINATION

5.1 This agreement shall terminate three years after the effective date, or may be terminated by either party at any time upon thirty days written notice to the other party. Upon termination or experiation of the agreement, Receiving Party shall promptly return to the Disclosing Party all documents and other tangible materials representing the confidential information.

5.2 The termination or expiry of this Agreement shall not affect any rights or remedies of the Disclosing Party with respect to this Agreement.

Laboratory for Visionary Architecture (LAVA) Berlin GmbH

Name of Representative
XXXX
Title
XXXX

Signature

XXXXXXXXXXXX

Name of Representative
XXXX
Title
XXXX

Signature
Stamp

LAVA: LABORATORY FOR VISIONARY ARCHITECTURE BERLIN GMBH
GESCHÄFTSFÜHRER: PROF. DIPL.-ING. MSC TOBIAS WALLISSER BDA
SAARBRÜCKER STRASSE 24 – HAUS D | 10405 BERLIN | FON +49 30 473 747 18-0

4

Signatures on behalf of LAVA and the Sub-Consultant are required.

Add any relevant information including :


Name of Representative

Title

2.2 PROJECT CHECKLIST

WHY DO WE NEED A PROJECT CHECKLIST ?

The Project Checklist can serve as a **central source of key information** relating to a project, allowing LAVA to keep track of data, information and reports which have been received. It is initiated during the Bidding phase, to support **decision-making** by leadership and to confirm the **amount of effort and expertise** required while acknowledging the **risks** such as data gaps or delays / re-work which might occur down the line.

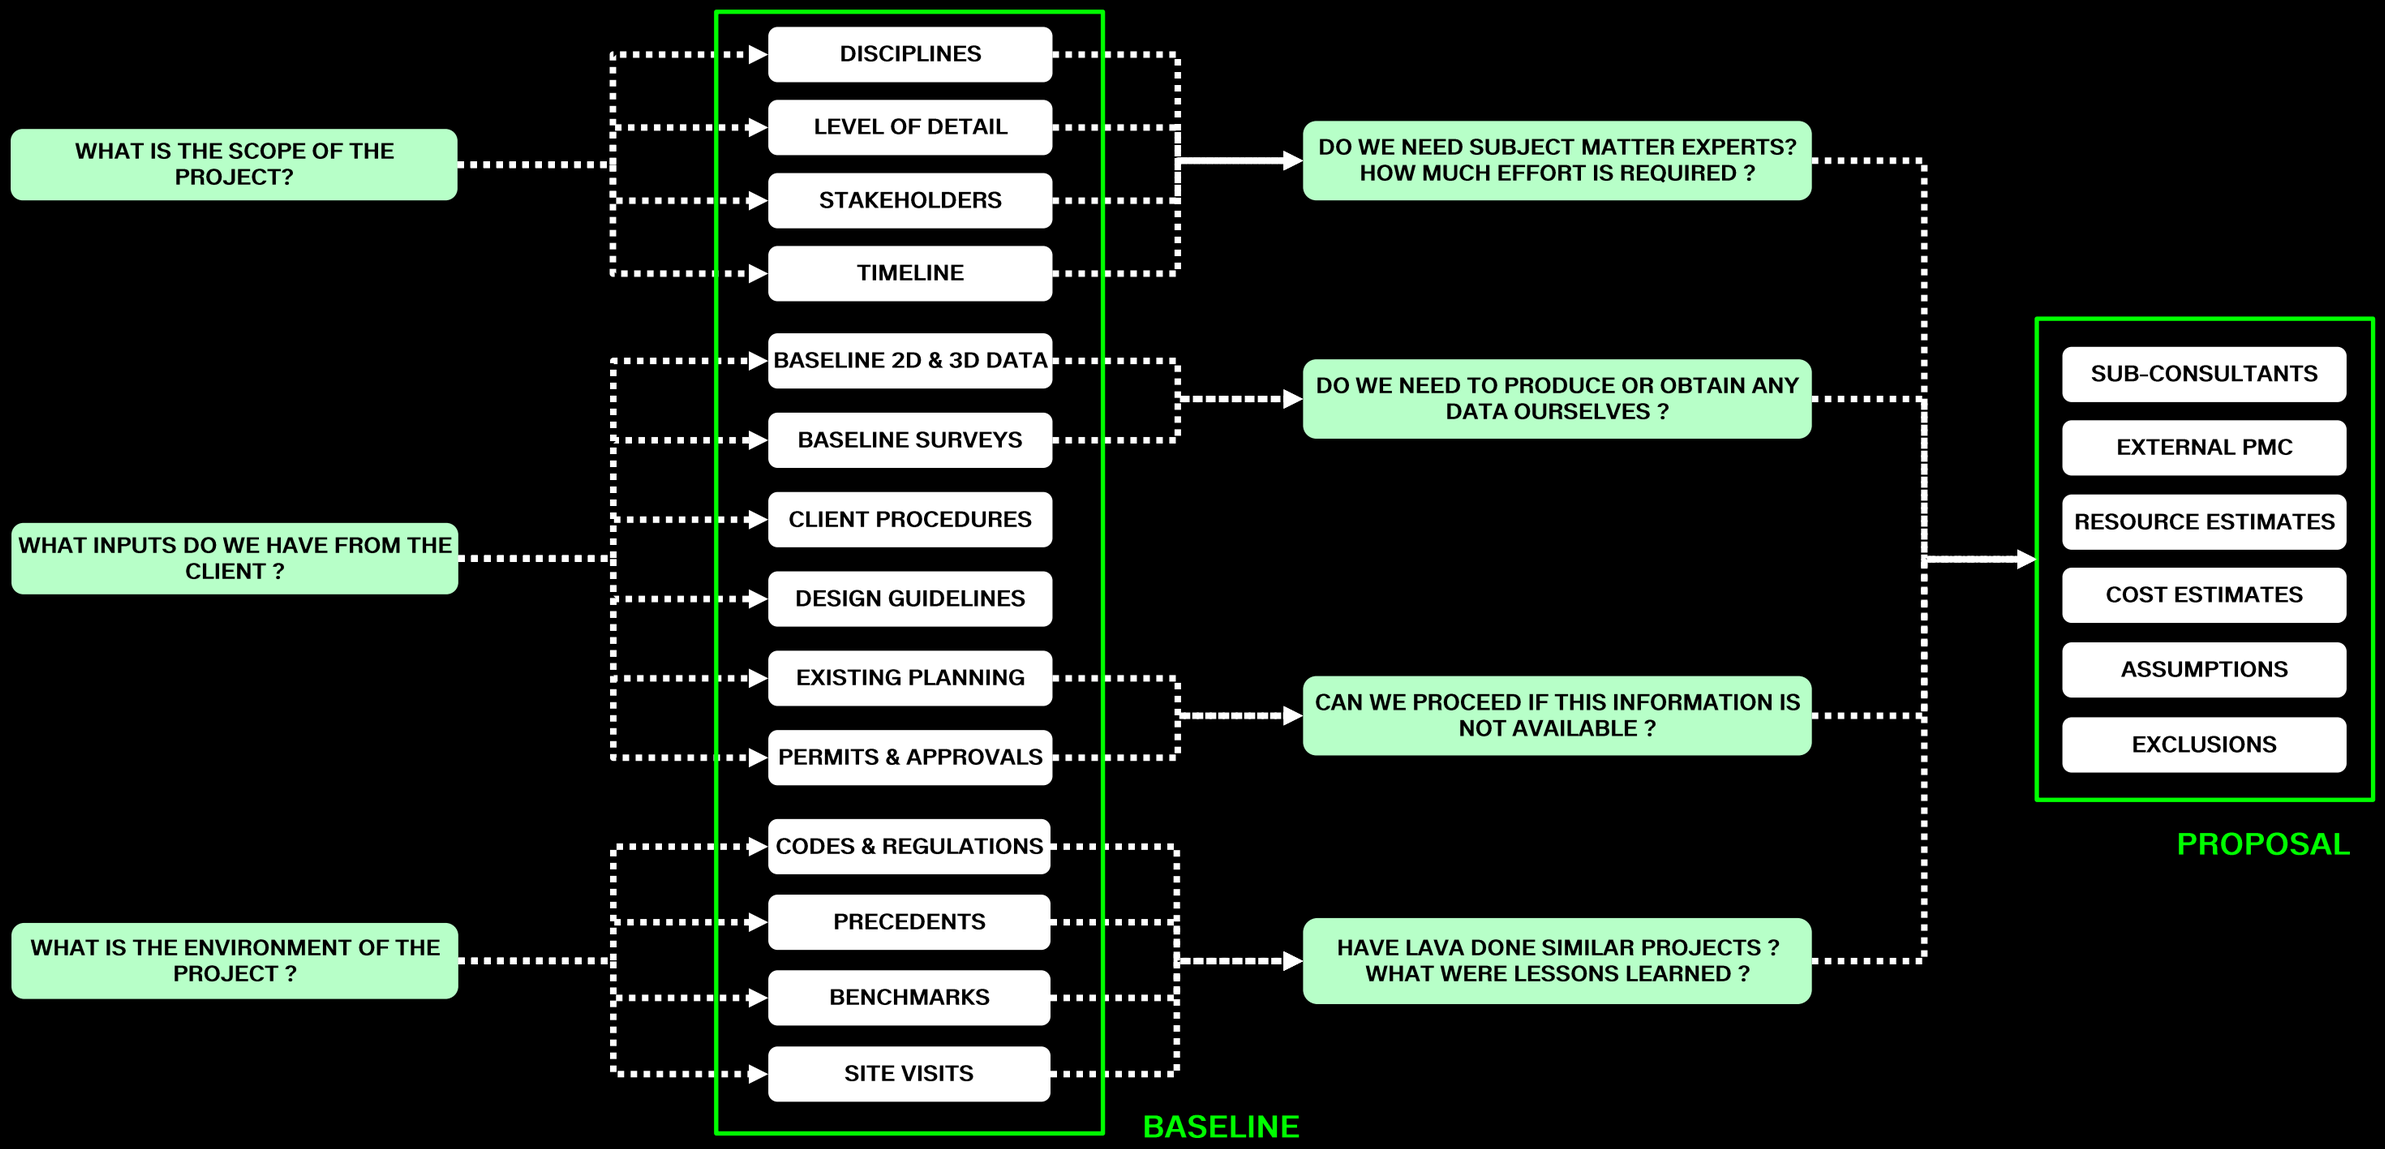

2.2.2 DOCUMENT CHECKLIST

WHAT IS THE DOCUMENT CHECKLIST?

The Document Checklist is one half of the Project Checklist, which can support LAVA and the Client to align on tracking known information and identifying gaps/unknowns in order to develop a Baseline for the project and deal with changes if required down the line.

Baseline Information section is intended for documents received during the Bidding phase. It reflects the constraints LAVA was aware of when we made our proposal.

Project Execution section is intended to include documents received after our offer was made. **This separation can help support Change Management** if required later (i.e. Variations to the contract to receive more time, fees, etc.)

Sub-Sections organize the documents based on topics. Not all projects need all information listed in the template :

e.g. **Contractual Documents** are always needed, however project might not involve Sub-Consultants

e.g. **Site & Project Context** is always needed, however not all projects involve Traffic Impact Studies (TIS)

Date, Source and Time are very important to track to maintain accurate knowledge.

Link must be accessible to the Project Team (e.g. Sharepoint, Server, etc.)

Status is adjusted based on a drop-down function to track if the information is available, has been requested/will be provided, is missing, or not relevant for the project.

Comments provide additional context related to the same.

		No.	Description	Title	Date	Source	Location	Status	Comments
BASELINE INFORMATION Before the Project	CONTRACTUAL DOCUMENTS	1	Scope of Works	250425_NMDMP_SoW	1/1/2025	Client	LINK	Available	
		2	Services Agreement	250425_NMDMP_ServicesAgreement	1/1/2025	Client	LINK	In Progress	Client Signature pending - ensure appendices are included
		3	Appendices to Services Agreement		1/1/2025	Client	LINK	In Progress	Appendices provided - updates to be confirmed upon final issue
		4	Notice to Proceed			Client	-	In Progress	Client confirmation pending - refer to Project Director
		5	Non-Disclosure Agreement (Client)		31/11/2024	Client	LINK	Available	
		6	Non-Disclosure Agreements (Sub-Consultants)		10/12/2024	LAVA	LINK	Available	
		7	Sub-Consultancy Agreements		21/12/2024	LAVA		In Progress	LAVA Signatures pending - to follow Services Agreement
		8	Appendices to Sub-Consultancy Agreements		21/12/2024	Sub-Consultants / LAVA	LINK	In Progress	Technical & Commercial Proposals by Sub-Consultants - check against final terms of Services Agreement
	PROJECT INFORMATION	9	Project Objectives	250425_NMDMP_SoW	1/1/2025	Client	-	Available	Refer to Scope of Works
		10	Project Stage (e.g. Pre-Concept, Concept,etc.)	250425_NMDMP_SoW	1/1/2025	Client	-	Available	Refer to Scope of Works
		11	Project Type (e.g. Commercial, Residential, etc.)	250425_NMDMP_SoW	1/1/2025	Client	-	Available	Refer to Scope of Works
		12	Project Stakeholders	250425_NMDMP_SoW	1/1/2025	Client	-	In Progress	Partially identified in Scope of Works - to be further assessed
		13	Project Timeline	250425_NMDMP_SoW		Client	-	Available	Refer to Scope of Works
		14	Project Budget			Client	-	Missing	Expected to be shared upon execution of Service Agreement
		15	Area Requirements	250425_NMDMP_SoW	1/1/2025	Client	-	In Progress	High-level figures provided in Scope of Works, breakdown not included
		16	Existing Design	250425_NMDMP_SoW	1/1/2025	Client	-	In Progress	Indicative visuals as part of Masterplan - refer to images in Scope of Works
	SITE & PROJECT CONTEXT	17	Project Report(s)	250425_DMP_Book1 & Book2	3/4/2023	Client	LINK	Available	Detailed Masterplan 100% submision documents
		18	Site Topography / Contours	250425_NMDMP_LiDAR-Survey	4/25/2025	Client	LINK	Available	1m Resolution
		19	Site 2D Drawing	250425_Jeddah-Masterplan	4/25/2025	Open Source	-	Available	
		20	Site 3D Model	250425_Jeddah-City-Model	3/16/2014	Open Source	LINK	In Progress	Outdated model missing new developments
		21	BIM / GIS Files				-		
		22	Zoning / Land Use Map			Authorities	-	Missing	To be obtained from available documentation by authorities
		23	Legal Cadastral Maps			Authorities	-	Missing	
		24	Environmental Surveys			Client		Missing	If not provided, Environmental Reports will be incomplete
		25	Geotechnical Reports / Data			Client		Missing	Surveys to be conducted by client - if not provided, might result in abortive work
		26	Weather Data	Tabuk-weather-station	2/5/2013	Open Source	LINK	In Progress	Closest open source weather station EPW file is within 1000 kilometers distance from site
		27	Traffic Impact Study (TIS)			Client		Missing	If not provided, Mobility Subconsultant cannot execute services
		28	Plot Boundary & Tie-In / Access Points	3/4/2023_DMP_Plotsheet013	1/1/2025	Client	LINK	Available	Appendix to Scope of Works
		29	Maximum Heights, Setbacks, envelope, etc.	3/4/2023_DMP_Plotsheet013	1/1/2025	Client	LINK	Available	Refer to Plotsheet in Scope of Works
		30	Utility Provisions (Power, Water, Telecom, etc.)			Client	LINK	Missing	Data has not been provided yet
		31	Hydrological Surveys / Flood Maps				LINK	In Progress	Low fidelity information available - surveys to be conducted by client - delay in inputs might result in abortive work
		32	Heritage / Conservation Status				-	Missing	To be clarified in environmental surveys
		33	Site Images				-	Missing	Site images to be captured during site visit once project kicks off
		34	Sustainability Goals			LEED		Available	Sustainability goals defined in Scope of Works- refer to LEED pathways
	COMPLIANCE	35	Client Procedures - Stage Gate Deliverables	250425_PRC01_xxxx	3/4/2023	Client	LINK	Available	
		36	Client Procedures - Quality	250425_PRC015_xxxx	3/4/2023	Client	LINK	Available	
		37	Client Procedures - GIS & BIM	250425_PRC22_xxxx	3/4/2023	Client	LINK	Available	
		38	Client Procedures - Document Numbering	250425_PRC25_xxxx	3/4/2023	Client	LINK	Available	
		39	Client Procedures - Change Management	250425_PRC31_xxxx	3/4/2023	Client	LINK	Available	
		40	Client Procedures - Design Guidelines			Client		Missing	Information has not been provided yet
		41	Client Procedures - Development Control Regulations			Client		Missing	Information has not been provided yet
		42	Client Procedures - Reporting Template			Client		Missing	No template has been provided as part of briefing
		43	Client Procedures - Drawing Template			Client		Missing	No template has been provided as part of briefing
		44	Germany - HOAI Phase Requirements			Authorities	LINK	Available	Refer to LAVA Library
		45	UK - RIBA Stage Requirements				-		
		[illegible]	[illegible]			Authorities		In Progress	Obtain and archive from public records
		47	International - Local Building Code Regulations			Authorities		In Progress	Obtain and archive from public records
PROJECT EXECUTION During the Project	PROJECT MANAGEMENT	47	Project Management Plan			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		48	Initial Timeline			LAVA	LINK	Available	Prepared as part of RfP response
		49	Detailed Route Map / Schedule			LAVA		In Progress	To be prepared after Notice to Proceed during Mobilization
		50	Deliverables List			LAVA		In Progress	To be prepared after Notice to Proceed during Mobilization
		51	Project Directory			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		52	Reporting Template & Dashboard			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		53	MoMs Template			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		54	RFI Register			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		55	Risk Register			LAVA		Not Required	Not required at this stage
		56	Resource Tracker			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		[illegible]	[illegible]			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		58	Responsibility Matrix			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		59	Stakeholders List			LAVA		Missing	To be prepared after Notice to Proceed during Mobilization
		60	Project Delivery Platform	Aconex		Client		Available	Aconex account is set up
	CONTRACTUAL DOCUMENTS	61	Instructions						
		62	Variation Order						
		63	Termination Order						
		64	Notice of Completion						
	3RD PARTY INPUTS	65	Neighboring Context 01	240205_NMSSV_Masterplan	5/2/2025	Consultant X	LINK	In Progress	Information shared informally by consultant - Client has not reviewed
		66	Neighboring Context 02	240205_Lake_Concept Design	5/3/2025	Consultant Z	LINK	In Progress	Information shared informally by consultant - Client has not reviewed

2.2.3 PROCESS CHECKLIST

WHAT IS THE PROCESS CHECKLIST?

The Quality Checklist is the other half of the Project Checklist, allowing LAVA to keep track of the main Project processes which need to be executed from start to finish, starting from Bidding before the Project, and ending with the Project Close-out after the Project. Project Leadership is responsible to monitor, control and verify the implementation of these steps.

	No.	Processes	Completed	Date	Checked by
BIDDING	A1	**Partner(s) confirm interest** in Bidding on the Project	N		
	A2	**Bidding Code** is assigned by Office Management and activated on Poolarserver	N		
	A3	**Director and/or Project Manager are assigned** on Technical and Commercial Proposals	N		
	A4	**Bidding Documents** (e.g. RfP, Appendices, etc.) are accessible on the Server and reviewed by the team	N		
	A5	**Confirm Project details** such as location, size, scope, time, type and LAVA's role in the Project	N		
	A6	**Baseline Information** provided by the Client is reviewed, and gaps/risks are identified	N		
	A7	Identify potential **external consultants** which might be required to complete the Project	N		
	A8	Contact consultants to confirm interest, and share Bid documents after confirming their **NDA signatures**	N		
	A9	Request technical and commercial proposal **inputs from subconsultants**	N		
	A10	**Resourcing** requirements are estimated	N		
	A11	Compile a **Technical Proposal** including Company Information, Portfolio, CVs and any other requirements	N		
	A12	Prepare a **Commercial Proposal** separate from the Technical Proposal	N		
	A13	**Archive all Bidding material** in their respective locations on the Server	N		
MOBILIZATION	B1	**Notice to Proceed** is received from the Client	N		
	B2	**Form of Agreement with client** is signed and executed	N		
	B3	**Project Kick-Off Date and Milestones** are agreed with Client	N		
	B4	**Client Review periods** are agreed with Client	N		
	B5	**Sub-Consultancy Agreements with Subconsultants** are signed and executed	N		
	B6	**Project Code** is assigned by Office Management and activated on Poolarserver	N		
	B7	**Project Leadership Team** is appointed	N		
	B8	**Folder Structure** is created on the Server	N		
	B9	**Digital Collaboration tools** are identified and access is granted by Directors if necessary	N		
	B10	**Planning - Timeline** including key milestones and review periods is drafted	N		
	B11	**Planning - Resourcing** availability of Project Team is confirmed	N		
	B12	**Planning - Project Directory** list with Project Team members and Key Persons contact details is created	N		
	B13	**Planning - List of Deliverables** or Work Breakdown Structure is defined	N		
	B14	**Templates and Standards** are available to the Project Team	N		
	B15	**Workstations, licenses and IT requirements** are assigned to all Project Staff	N		
	B16	**2D & 3D site information** is collected from the best available sources	N		
	B17	**Regulations procedures, guidelines and compliance requirements** relevant for the Project are confirmed	N		
	B18	**Internal LAVA Kick-Off meeting** between Project Team and Partner(s) is arranged	N		
	B19	**Objectives and Strategic Framing** for Project including relevant Themes and Questions are defined	N		

	No.	Processes	Completed	Date	Checked by
PROJECT EXECUTION	C1	**Project Kick-off with Client** is scheduled and presentation is prepared accordingly	N		
	C2	**Roles and Responsibilities** within Project Team are assigned	N		
	C3	**Communication methods** with Client, Consultants and others are defined	N		
	C4	**Information gaps** are documented, **RFIs** are issued and **assumptions** are defined if necessary	N		
	C5	**Benchmarking, references and research** is completed	N		
	C6	**Design processes and outputs** align with LAVA quality standards	N		
	C7	**Project Timeline is updated** accordingly throughout Project	N		
	C8	Production and services align with **Cost, Scope and Time constraints**	N		
	C9	**Team Performance** is monitored, feedback for improvement is communicated	N		
	C10	**Progress Reporting** is prepared and shared with relevant parties	N		
COMMERCIAL CONDITIONS	D1	Main Contract and sub-contract **appendices** are fully accounted for	N		
	D2	Main Contract and sub-contract **terms and conditions** fullfilled	N		
	D3	Legal issues support available	N		
	D4	Liabilities can be controlled	N		
	D5	**Invoicing policy** and **payment milestones** agreed	N		
	D6	**Payments** are received and issued in regular time according to contractual terms	N		
	D7	Contractual conflicts identified, Early Warnings formally notified to Client if necessary	N		
	D8	**Change Procedures** are agreed and **Change Management** is executed in collaboration with Client	N		
	D9	Contracts and appendices are **updated per client instructions** if necessary	N		
PROJECT CLOSE-OUT	E1	Deliverables and services align with **Stage Gate requirements, Approval or Quality Criteria**	N		
	E2	**Final Presentations** to Client Representatives, Stakeholders and/or Authorities are scheduled and completed	N		
	E3	**Client comments** are addressed to ensure approvals	N		
	E4	**Revisions to Deliverables or Addenda** are issued if necessary	N		
	E5	Project Sponsor or Client Representatives are provided a formal **Notice of Completition**	N		
	E6	**LAVA Finance Team** is notified of Completiton to initiate **Invoicing**	N		
	E7	All Project Documentation is **archived on Server**	N		
	E8	**Project Fact Sheet** is filled with key information and data to support PR functions	N		
	E9	**PR Quicklinks Sheet** is filled with links to key graphics, render and images to support PR functions	N		
	E10	**Lessons Learned** are shared by Project Team	N		
	E11	**Feedback** is provided by Project Manager/Team Lead to Project Team	N		
	E12	**Resourcing is demobilized**, Project Team is adjourned	N		
	E13	**Workstations, licenses and IT requirements** are made available to the organization	N		

Processes are pre-defined and cannot be modified on a project basis.

Completition Status can be marked as Y, N or N/A (Non-Applicable).

Project Leadership (i.e. Director, Lead and Project Management) responsible for checking that each process is completed during the respective phase of a Project (e.g. Bidding processes to be checked during or no later than the end of the Bidding phase)

03

DURING THE PROJECT

3 DURING THE PROJECT

WHEN AND HOW DO LAVA START A PROJECT ?


1. **Notice to Proceed is formally issued by client** – *green light to start the Project is communicated by the Partner(s)*
2. **Project Code is set up** – *Directors Determine Code and Kickoff the Project*
3. **Project Leadership Team is assigned** – Director + Project Lead + Project Management *responsibilities are defined at a high-level*
4. **Standardized Folder Structure is set up on Server** – *Project Leadership Ensures Projects are Set Up*
5. **Online Platform(s) are set up for digital collaboration and files exchange**– *Directors with Head of Digital Collaboration.*
6. **General Project Planning by Project Lead / Manager** – *Timeline, Deliverables List, Resourcing, Templates, etc.*
7. **Project Checklist is maintained** – *Has any new information become available after we made our offer?*
8. **LAVA Internal Kick-Off** – *The Vision is set – what are the applicable LAVA Themes ? What are our aspirations ?*

3 DURING THE PROJECT


WHAT TAKES PLACE **DURING** THE PROJECT ?

As soon as a Project is confirmed to start, the Project Leadership and Team must ensure that a set of process groups are implemented consistently beginning from mobilization to kick-off through to the scheduled end dates. These process groups are defined accordingly :


1. **Knowledge Management** – A set of rules for systematically capturing, organizing, maintaining, updating and sharing data and/or documentation to ensure design teams are informed and empowered, and that Projects are run efficiently and accurately.
2. **Planning** – Development of a structured roadmap defining schedules and milestones, listing out deliverables, delineating roles and responsibilities, to ensure LAVA delivers on client expectations per scope, time and cost constraints as agreed beforehand.
3. **Execution** – Once a project kicks off, Execution in the context of Project Management is centered on monitoring the progress of tasks and activities and updating the Planning as required, facilitating coordination, assuring and controlling the quality of our work and ensuring that we deliver.

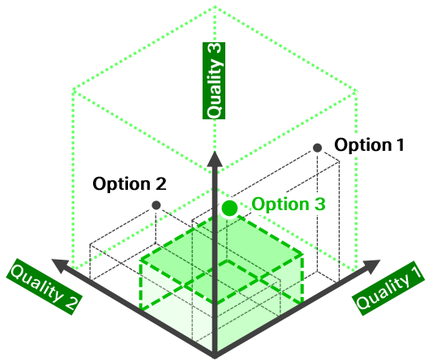

1. **Inquire, Imagine, Invent –** LAVA's project management processes to support our research and design methodology step-by-step

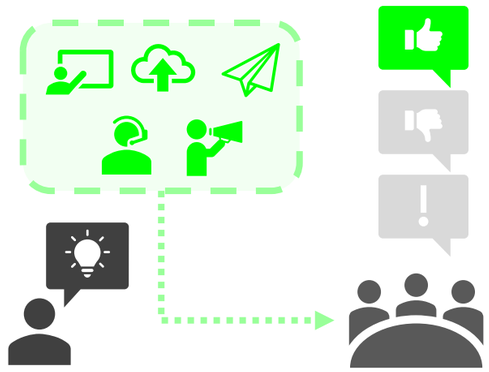

2. **Communication –** Ensure all parties have access to the right information at the right time to make an impact on the project

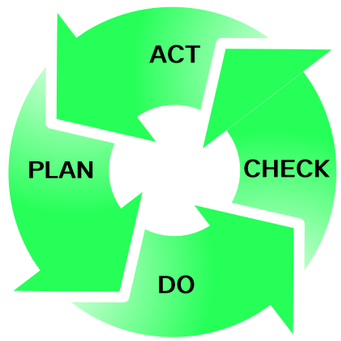

3. **Plan, Do, Check, Act –** the PDCA cycle as a continuous improvement model for agile and iterative work balanced with preparation


3 DURING THE PROJECT

WHO IS RESPONSIBLE FOR WHAT DURING THE PROJECT ?

	PARTNERS	DIRECTORS	PROJECT MANAGEMENT	OFFICE MANAGEMENT	IT & TECHNICAL SUPPORT	PROJECT LEAD
1. Administration	Confirm that Project is ready to commence after client notice (Notice to Proceed, Contract is signed, etc.)	**Responsible.** Define **Project Leadership** and Assign **Resourcing** to Project Team.		**Responsible.** Create a **Project Code** for use on Poolarserver upon confirmation.		
		Confirmation to start Project		Confirmation to create Project Code		
2. Knowledge Management	**Consulted.** Confirm purchases to IT & Technical Support according to Digital Collaboration needs.	**Informed.** Given access to all platforms after set-up by Project Management.	**Responsible.** Create Project Folders on Server using Project Code. Coordinate with others to set-up Digital Collaboration for Project.		**Responsible.** Set-up **Digital Collaboration** channels and platforms if required by Project Management (e.g. Sharepoint, Miro Board, etc.)	**Consulted.** Provide feedback to Project Management during Planning on necessary software, tools, etc.
			Confirmation to set-up Digital Collaboration			
					Consult	
3. Planning	**Informed.** Given access to all of the initial and the latest Project Management documents, if updated during the Project.	**Consulted.** Provide feedback and advise on Project Management documents. Address project risks, reporting them to Partners if necessary.	**Responsible.** Provide the Project Lead with all initial Project Management documents (e.g. Timeline, Deliverables List, etc.). Flag **risks** to Director.		**Informed.** Support Project Team with **technical issues** if needed (e.g. software licenses, data storage, communication channels, etc.).	**Responsible.** Follows Project Management documents and updates Planning during the Project as needed (PDCA cycle : Plan Do Check Act)
			Provide initial Planning at Project Kickoff			
					Update Planning during the Project	
4. Execution	**Consulted.** Review Bi-Weekly Reporting and provide feedback on progress. Make decisions on design studies as required.	**Accountable.** Ensure **Design Direction** is aligned with LAVA ethos and themes. Report to Partners on progress.	**Informed. Monitor and control** implementation of Project Processes. **Flag potential issues to Director** (e.g. scope, time, cost, quality)			**Responsible.** Ensure production of **Design, Coordination, Reporting,** and **Deliverables.** Delegate tasks to Project Team. Ensure Team follows Project Processes.
	Review & Confirm				Document Progress in Bi-Weekly Reports	

SET-UP DURING THE PROJECT

1. **Planning** – *Use existing LAVA templates as required*
2. **Digital Collaboration Platforms** – *Identify tools which will be used and set up access for the team*
3. **Kick-Off Presentation** – *Preliminary Research, Reverse Brief, Sketches, Design Direction etc.*
4. **LAVA Motivation & Objectives** – *Workshopped through Internal Kick-Off Presentation with Partner*

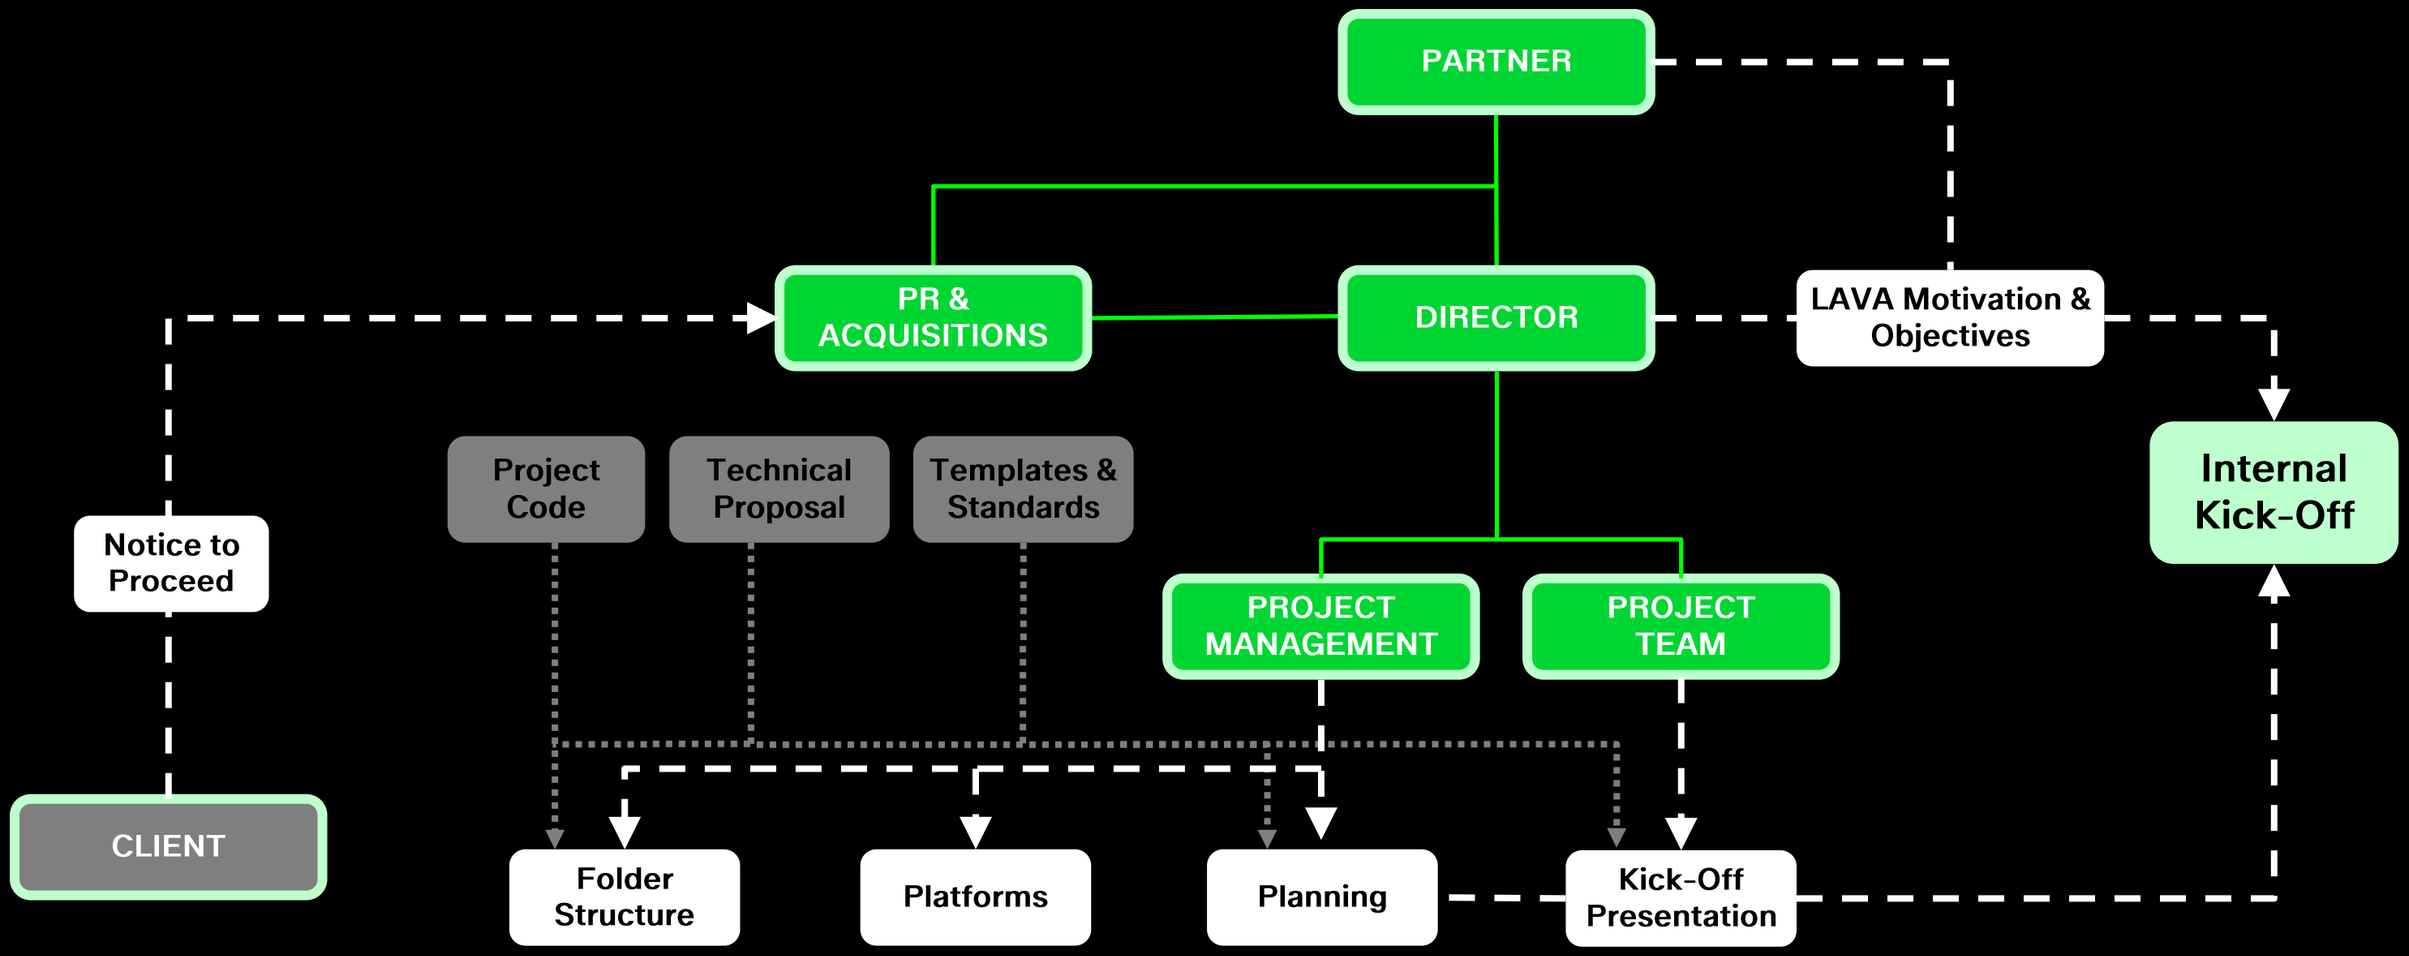


3.1 KNOWLEDGE MANAGEMENT

WHAT ARE PRINCIPLES OF KNOWLEDGE MANAGEMENT ?


Knowledge Management is a systematic approach for collecting, sharing and storing data, information or documents as part of Project activities.

This can improve team performance by empowering different individuals to be self-dependent and ensures continuity across different stages irrespective of which specific person is available or not, by making sure that tacit knowledge becomes explicit in being properly recorded. At a minimum the following are applications of Knowledge Management at LAVA :

- **Project Code** – Every Project at LAVA receives a code when it is started. The same code should be used for different stages.
- **Folder Structure** – A standardized system for organization information on the server is to be followed.
- **Digital Collaboration** – Tools and platforms which might be required to collaborate internally or externally.
- **File Naming Conventions** – In addition to folder structures, ensuring a unified system for labeling documents is followed .

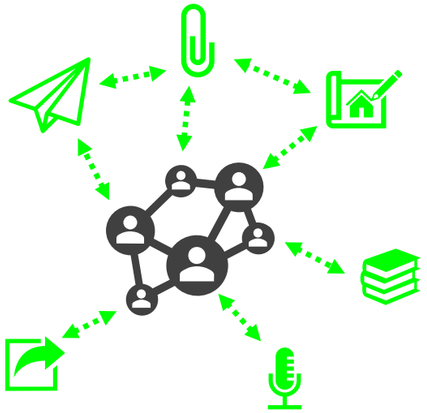

1. **Capture and Share** – Facilitate collaboration and keep a record of communications with internal and external parties

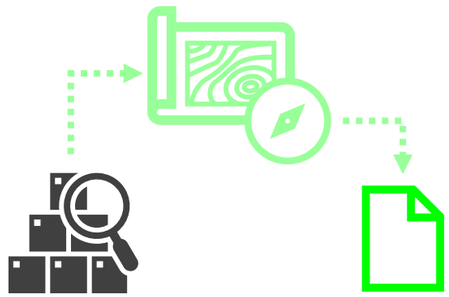

2. **Ease of Accessibility** – Applying a clear logic for organizing and labeling information, which allows for intuitive navigation and traceability



3. **Consistent Implementation** – Ensure that the system is not only set up at the beginning, but is routinely maintained

3.1.1 PROJECT CODE

PROJECT CODE DURING THE PROJECT

Project Names and Numbers are set up by Project Leadership according to the template below.

Upon availability of a Project Code, workhours can be recorded under the respective phase of this project. Having a Project Code set up during Bidding can ensure that any work outside of billable hours may also be monitored by LAVA.


0000_xxx_Project

- 4-digit sequential number
- 3 to 5 character short name
- In standard projects, 3 digits are used. For nested projects, up to 5 digits could be used to be more clearly indicate the relationship between the projects (e.g. For NEOM projects, first letter can be N, second letter can be the Cluster, etc.)
- The Project name, recognizable addition to the short name, which must also be kept brief.

3.1.2 FOLDER STRUCTURE

SET-UP FOLDER STRUCTURE DURING THE PROJECT

Sub-Folders are structured and numbered to group categories together accordingly.
Additional folders can be created under each Subfolder and labeled accordingly (e.g, Date and Topic)

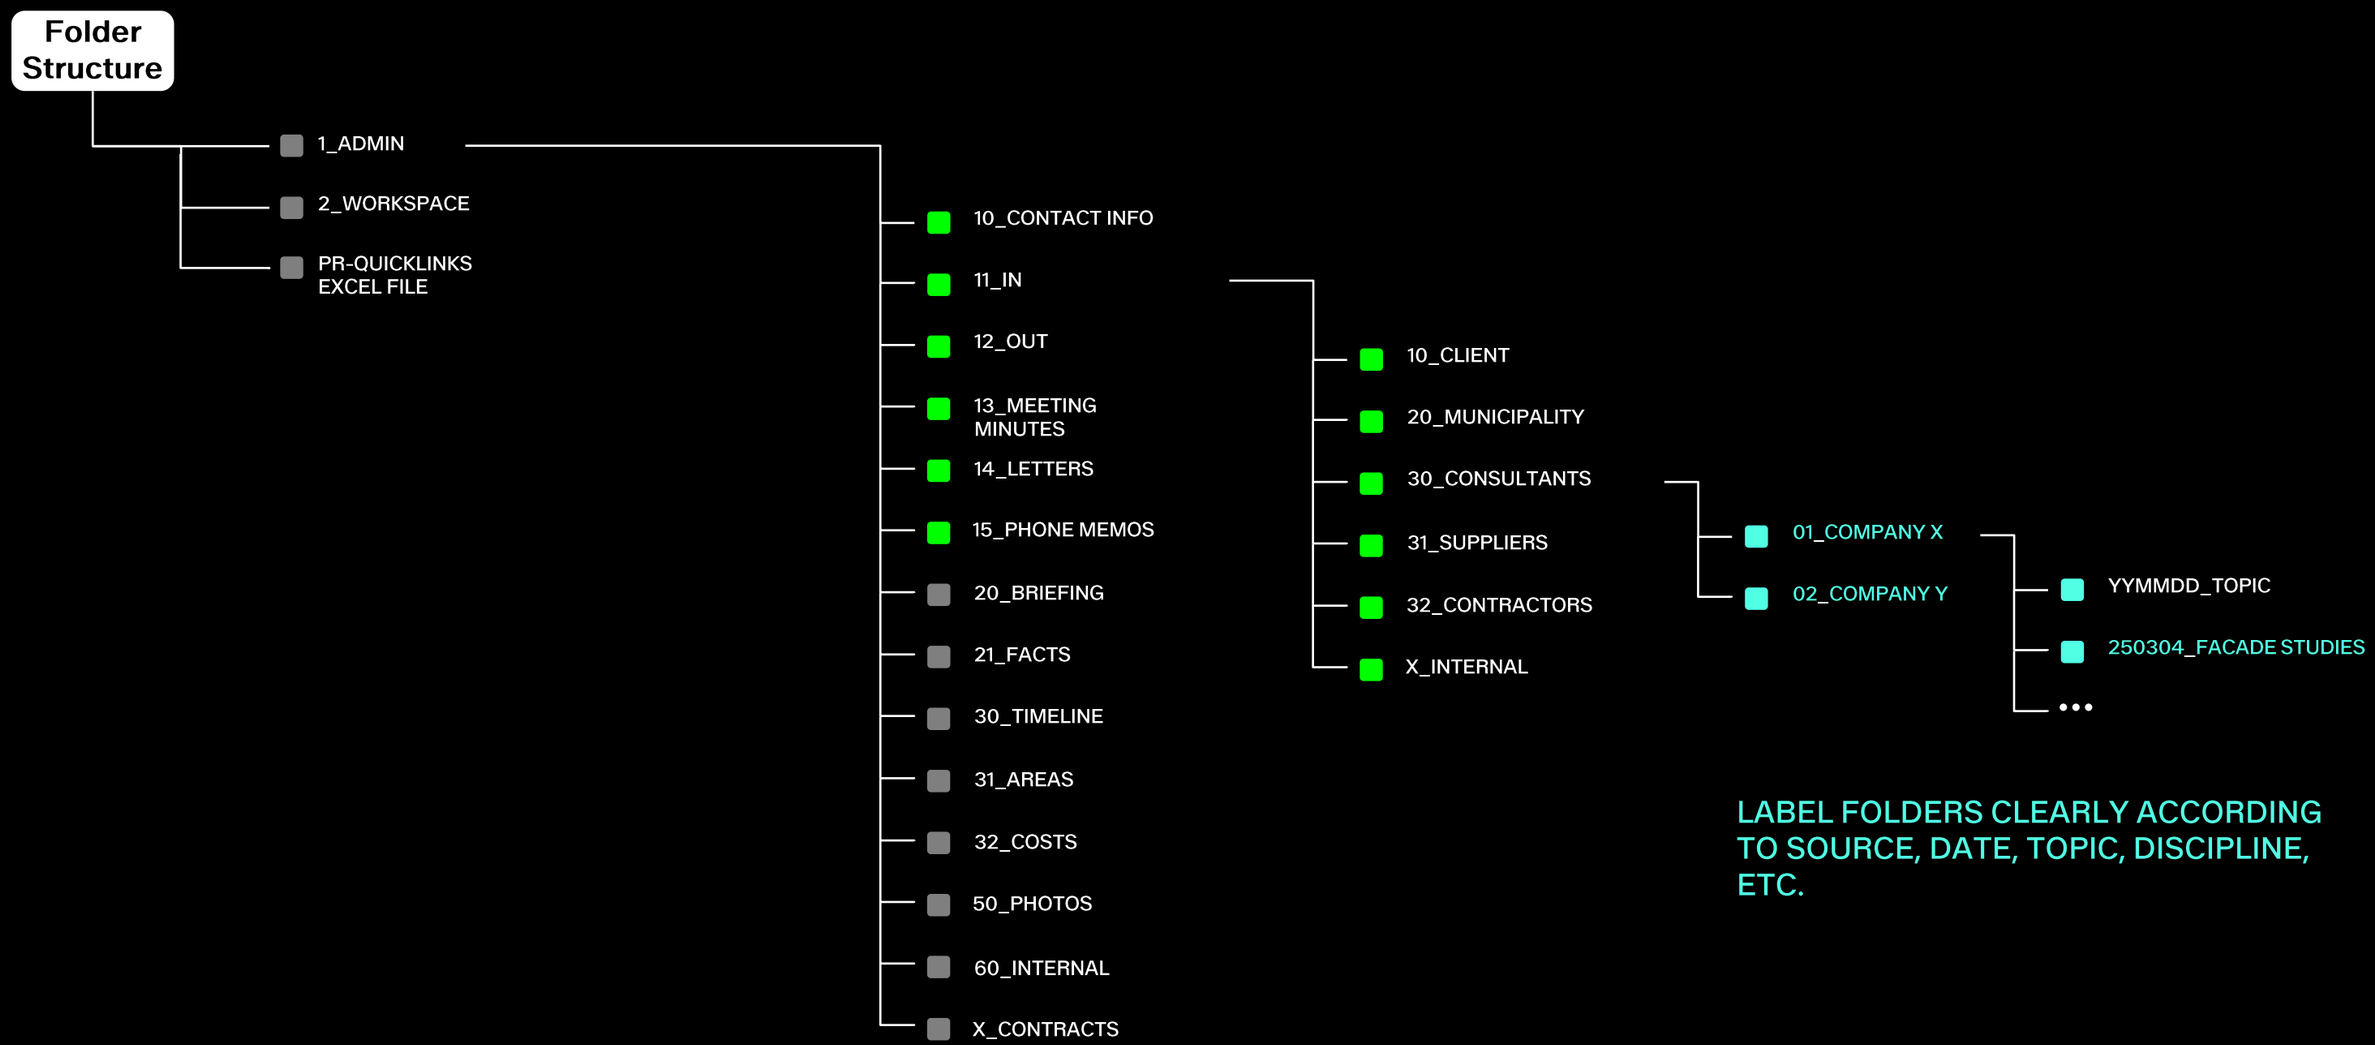


LABEL FOLDERS CLEARLY ACCORDING TO SOURCE, DATE, TOPIC, DISCIPLINE, ETC.

3.1.2 FOLDER STRUCTURE

SET-UP FOLDER STRUCTURE DURING THE PROJECT

Under Workspace, **Sub-Folder Structures** are also standardized and must be copied according to location (Germany, or General for International projects) under the respective phase of a project.

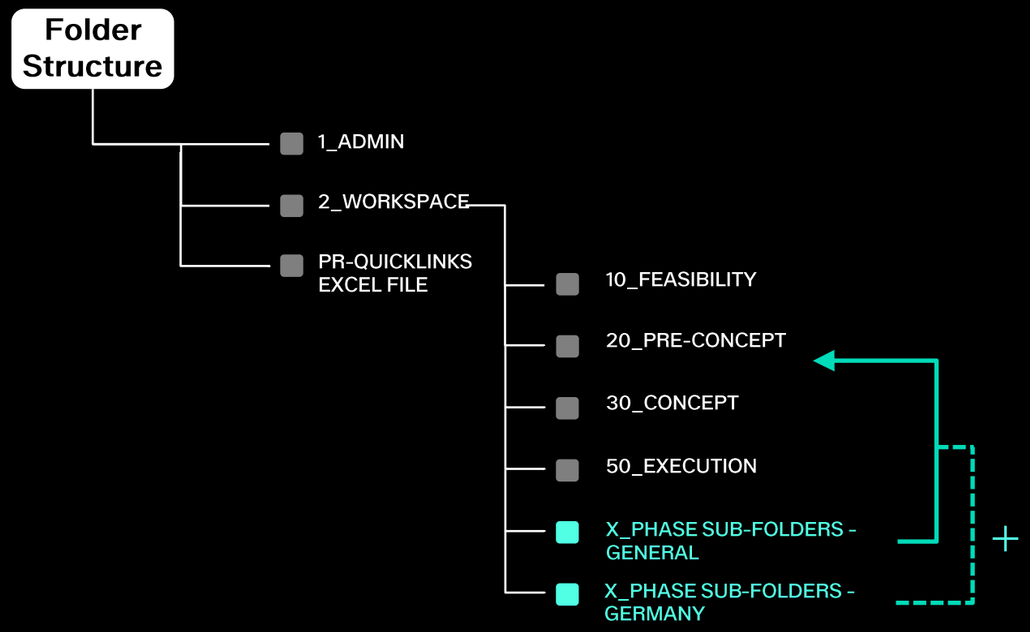


COPY GENERAL FOLDER STRUCTURE AND DELETE ANY UNNECESSARY SUB-FOLDERS WHICH MIGHT NOT BE REQUIRED.

IN THE CASE OF GERMAN PROJECTS, ADD ADDITIONAL SUBFOLDERS UNDER THEIR RESPECTIVE LOCATIONS UNDER THE GENERAL FOLDER STRUCTURE.

3.1.2 FOLDER STRUCTURE

SET-UP FOLDER STRUCTURE DURING THE PROJECT

Under Workspace, **Sub-Folder Structures** are also standardized and must be copied according to location (Germany, or General for International projects) under the respective phase of a project.

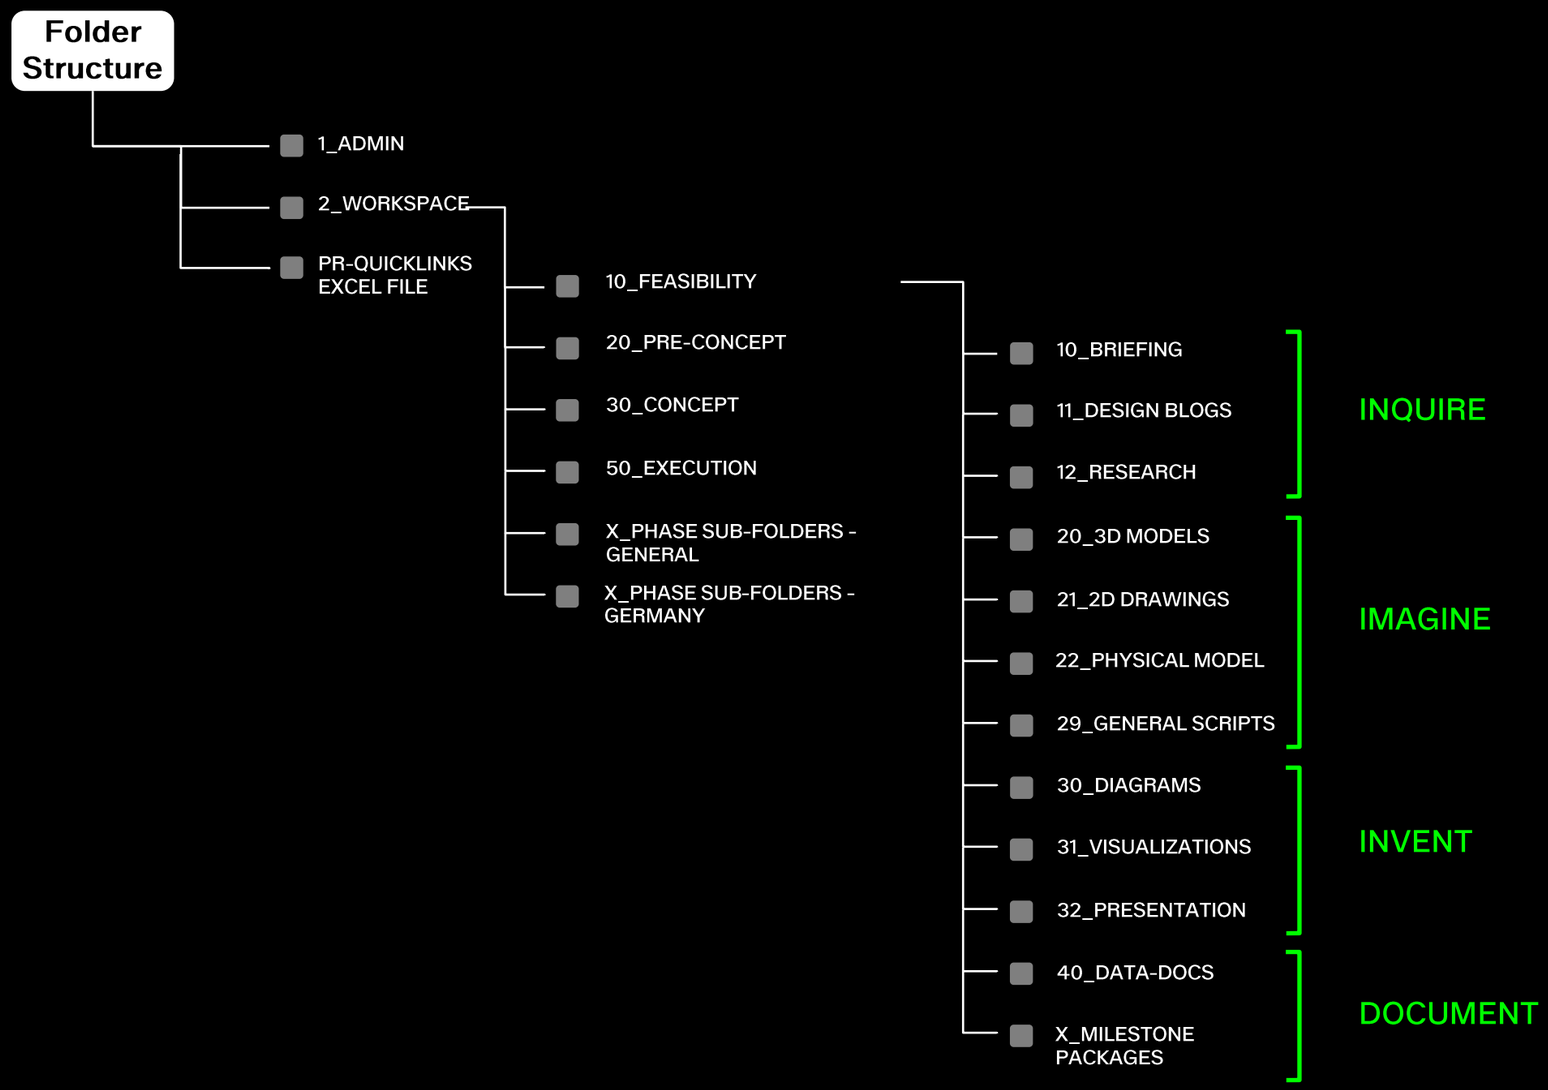

3.1.3 DIGITAL COLLABORATION

SET-UP DIGITAL COLLAB DURING THE PROJECT

During the project, different needs might arise, and the project lead needs to ensure in time that the tools needed are accessible to the right people/

More available

Less Available

Provided by Default

Provided to everyone directly when they join and are freely available to all fulltime employees (some variations may exist depending on employment contract)

- Computer & Peripheries
- Local File Storage Server
- Microsoft 365
- Poolarserver Access
- Rhino 3D
- Adobe Creative Cloud

Free/Included in Existing Subscriptions

Available by request, and have no limits or high enough practical limits for our usage

- MiroBoard
- Twinmotion
- Midjourney

Limited Licenses / Credits Available

Available by request, but have limited licenses, credits or storage space

- SharePoint
- Enscape
- V-ray
- Runway AI
- Lumion
- Planen und Bauen

Provisioned per Project / User Needs

Available by request, have limited licenses, and require approval from project lead and customized needs assessment.

Requests should be submitted at least 1 week in advance for software and at least 2 weeks in advance for hardware.

Autodesk

- Revit
- Navisworks
- Construction Cloud
- Revit Cloud Collab
- AutoCAD
- Others

Additional Software

Additional Hardware

3.1.3 DIGITAL COLLABORATION

SET-UP DIGITAL COLLAB DURING THE PROJECT

Depending on the LAVA office, different persons might need to be contacted to set up access to the various platforms and digital resources which might be needed by the Project Team.

The digital tools that are **PROVIDED BY DEFAULT**:

Computer & Peripheries

Windows PC, screen, mouse, keyboard, headset, webcam

- BER: Harry McClendon, Sibel Ruge
- STR: Fadel Makhzoum, Angela Lempelius

LOCAL FILE STORAGE SERVER ACCESS

- BER: Harry McClendon, Sibel Ruge
- STR: Fadel Makhzoum, Angela Lempelius

MICROSOFT 365

- BER: Harry McClendon, Sibel Ruge
- STR: Fadel Makhzoum, Angela Lempelius

POOLARSERVER ACCESS

- BER: Harry McClendon, Sibel Ruge
- STR: Fadel Makhzoum, Angela Lempelius

RHINO 3D (v6, v7,v8)

- BER: Harry McClendon
- STR: Fadel Makhzoum, Hossem Elseffy

ADOBE CREATIVE CLOUD

- BER: Harry McClendon
- STR: Fadel Makhzoum, Hossem Elseffy

3.1.3 DIGITAL COLLABORATION

SET-UP DIGITAL COLLAB DURING THE PROJECT

Depending on the LAVA office, different persons might need to be contacted to set up access to the various platforms and digital resources which might be needed by the Project Team.

The digital tools that are **FREE OR INCLUDED IN EXISTING SUBSCRIPTIONS**:

TWINMOTION

- BER: Harry McClendon
- STR: Fadel Makhzoum

MIDJOURNEY

- BER: Harry McClendon
- STR: Fadel Makhzoum

MIROBOARD

- BER: Laurent Dubuis, Lukas Kronawitter, Lukas Utzig
- STR: Fadel Makhzoum

3.1.3 DIGITAL COLLABORATION

SET-UP DIGITAL COLLAB DURING THE PROJECT

Depending on the LAVA office, different persons might need to be contacted to set up access to the various platforms and digital resources which might be needed by the Project Team.

The digital tools that are SHARED ACCESS, BUT LIMITED LICENSES / CREDITS AVAILABLE:

SharePoint Cloud File Storage
- Directors/Project Lead
- If permission is missing → Fadel Makhzoum

Enscape
- Fadel Makhzoum
- Hossam Elseffy

V-Ray
- Fadel Makhzoum
- Hossam Elseffy

Runway AI Access / Additional Credits
- Fadel Makhzoum
- LAVAi Team

Lumion
- Fadel Makhzoum

Planen und Bauen (German building codes and norms online database)
- Valerie Kerz
- Fadel Makhzoum
- Sibel Ruge

3.1.3 DIGITAL COLLABORATION

SET-UP DIGITAL COLLAB DURING THE PROJECT

Depending on the LAVA office, different persons might need to be contacted to set up access to the various platforms and digital resources which might be needed by the Project Team.

The digital tools that are **PROVISIONED PER PROJECT OR USER NEEDS**:

AUTODESK

Revit, Navisworks, AutoCAD, Revit Cloud Collaboration, Autodesk Construction Cloud / Cloud Docs

- Fadel Makhzoum
- Zuhair Baluch

Additional Software

- Fadel Makhzoum
- Harry McClendon


Additional Hardware

- BER: Harry McClendon
- STR: Fadel Makhzoum, Hossam Elseffy

3.1.3 DIGITAL COLLABORATION

SET-UP DIGITAL COLLAB DURING THE PROJECT with LAVAi

Team LAVAi provides support for AI usage across offices. This includes supporting project teams with workflows integration, troubleshooting and consultancy on GenAI (Generative AI) for case-specific applications. Requests for support can be posted on the **LAVAi Teams channel** or sent directly to the **LAVAi emails.**



LAVAi Team

AI - Support | LAVA Germany | Microsoft Teams

ai@l-a-v-a.com
lavai@l-a-v-a.com

Jan Kovaricek:
j.kovaricek@l-a-v-a.com

Hossein Maghami:
h.maghami@l-a-v-a.com

Benedikt Schambeck:
b.schambeck@l-a-v-a.com

Fadel Makhzoum:
f.makhzoum@l-a-v-a.com

3.1.3 DIGITAL COLLABORATION

HOW TO USE SHAREPOINT ON ANY PROJECT

4. Weekly back up / Clean up file

4.1 Weekly back up

1. Download the previous file / Important file.
2. Place it in the relevant folder on LAVA Network Server.
3. Delete those file from the SharePoint what is no longer need.

4.2 Weekly Clean Up

Steps

1. Go to site storage metrics
2. Find the largest folders *(PowerPoint presentations take up a lot of space due to their many copies in the version history)*
3. Delete all versions in the version history
4. Empty recycle bin


Note:


** Every Team should have one person take responsible to back up / clean up the file twice per week.

3.1.3 DIGITAL COLLABORATION

HOW TO USE SHAREPOINT ON ANY PROJECT

1. Go to site storage metrics

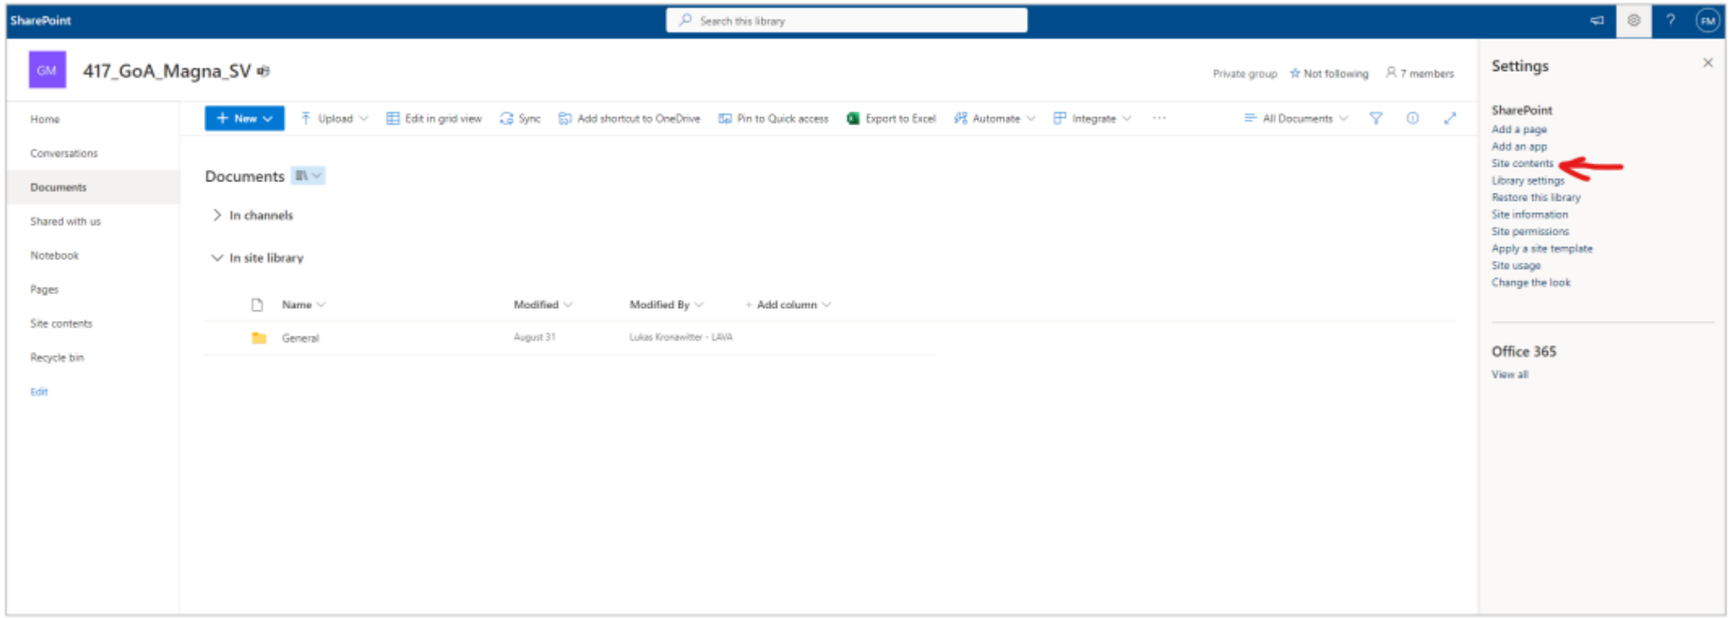

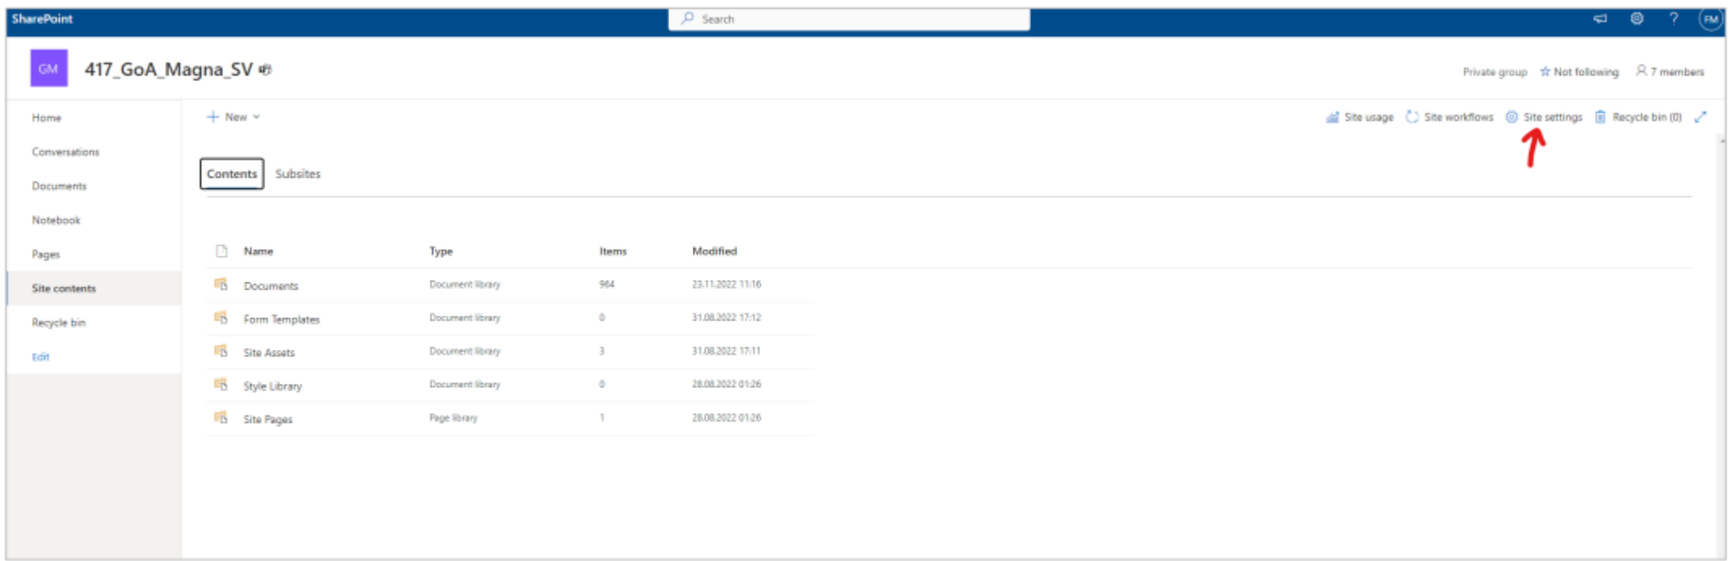



3.1.3 DIGITAL COLLABORATION

HOW TO USE SHAREPOINT ON ANY PROJECT

4. Weekly back up / Clean up file

1. Go to site storage metrics

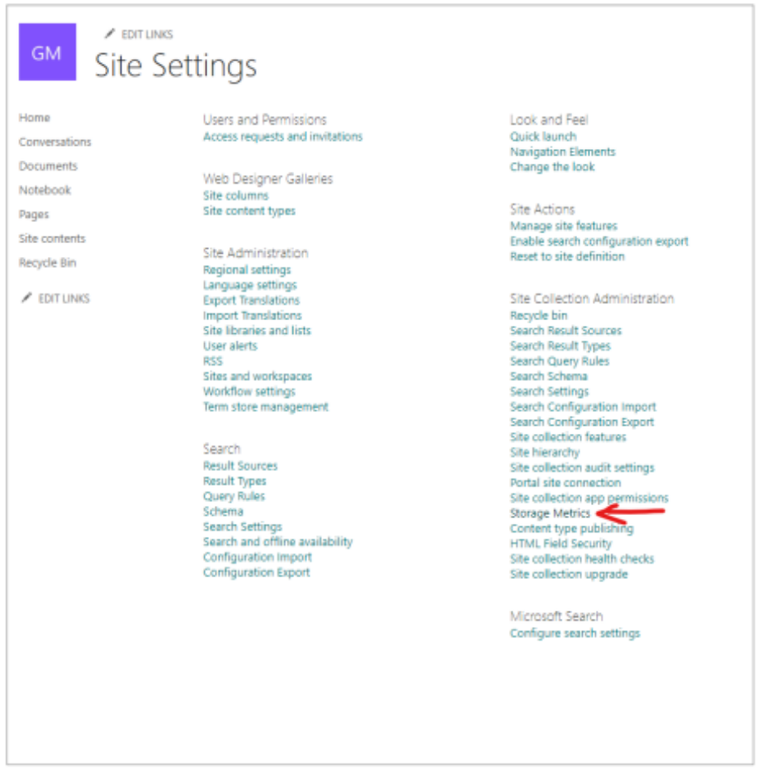

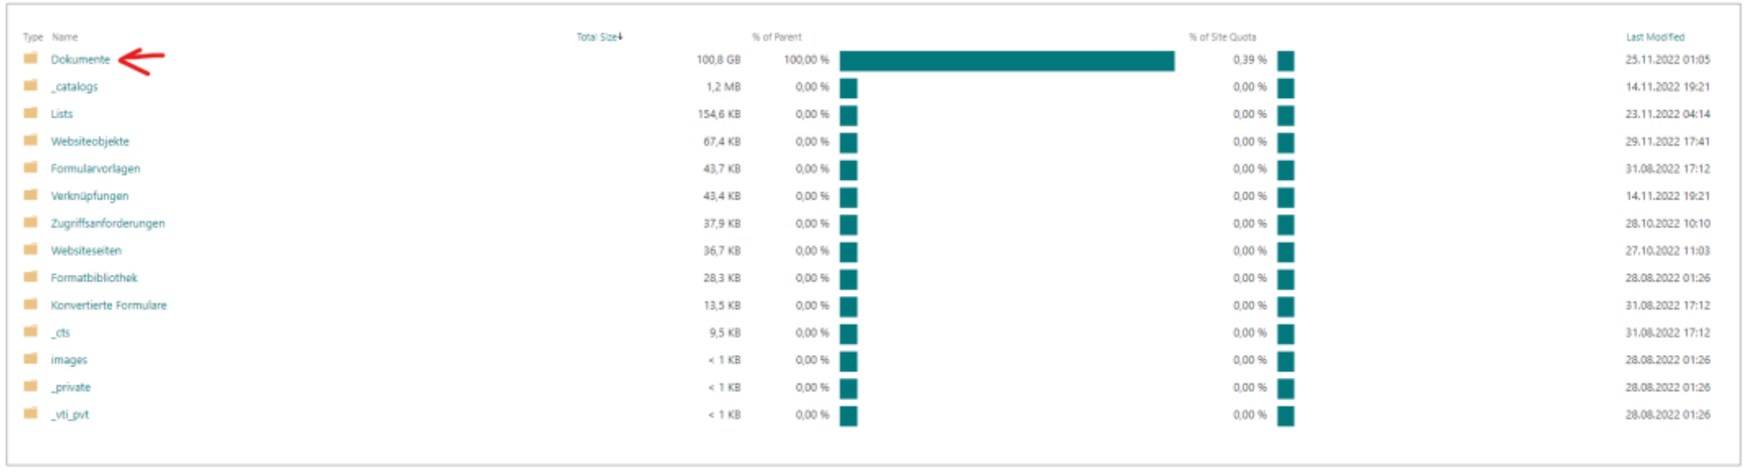


3.1.3 DIGITAL COLLABORATION


HOW TO USE SHAREPOINT ON ANY PROJECT

4. Weekly back up / Clean up file

2. Find the largest folders

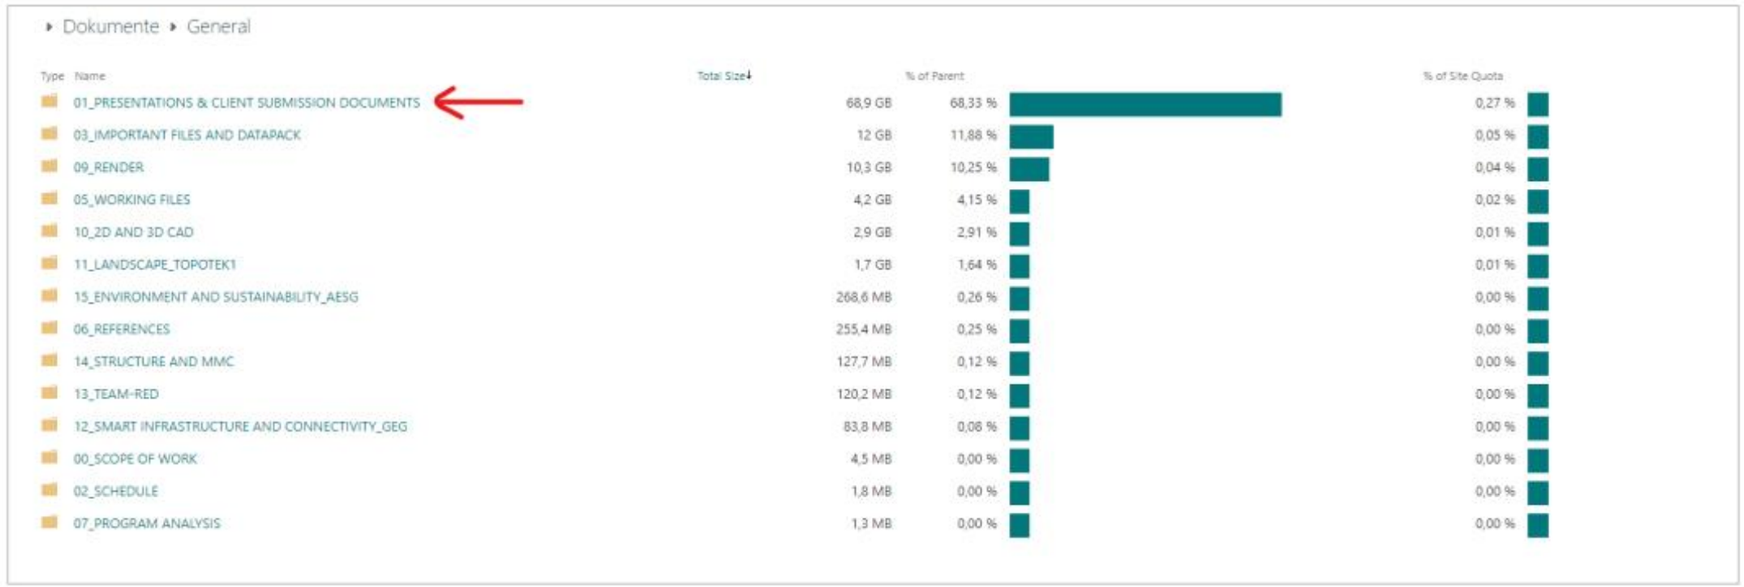

PowerPoint presentations take up a lot of space due to their many copies in the version history

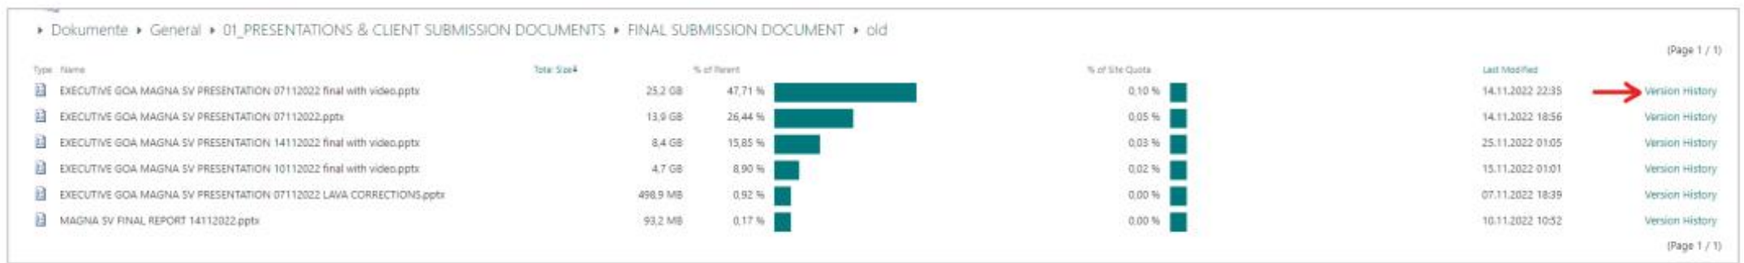

3.1.3 DIGITAL COLLABORATION

HOW TO USE SHAREPOINT ON ANY PROJECT

4. Weekly back up / Clean up file

3. Delete all versions in the version history.

EDIT LINKS

Versions saved for EXECUTIVE GOA MAGNA SV PRESENTATION 07112022 final with video.pptx

Delete All Versions


No.	Modified	Modified By	Size
79.0	10.11.2022 13:15	Nadh Ha Naseer - LAVA	297 MB
78.0	10.11.2022 13:10	Nadh Ha Naseer - LAVA	297 MB
77.0	10.11.2022 12:59	Nadh Ha Naseer - LAVA	297 MB
76.0	10.11.2022 12:44	Nadh Ha Naseer - LAVA	297 MB
75.0	10.11.2022 12:36	Nadh Ha Naseer - LAVA	300,5 MB
74.0	10.11.2022 12:26	Nadh Ha Naseer - LAVA	300,5 MB
73.0	10.11.2022 12:16	Nadh Ha Naseer - LAVA	300,5 MB
72.0	10.11.2022 12:06	Nadh Ha Naseer - LAVA	300,5 MB
71.0	10.11.2022 11:56	Nadh Ha Naseer - LAVA	300,5 MB
70.0	10.11.2022 11:45	Nadh Ha Naseer - LAVA	300,5 MB
69.0	10.11.2022 11:31	Nadh Ha Naseer - LAVA	300,5 MB
68.0	10.11.2022 11:17	Nadh Ha Naseer - LAVA	300,5 MB
67.0	10.11.2022 11:08	Nadh Ha Naseer - LAVA	304,4 MB
66.0	10.11.2022 10:56	Nadh Ha Naseer - LAVA	303,7 MB
65.0	10.11.2022 10:48	Nadh Ha Naseer - LAVA	303,7 MB
64.0	10.11.2022 10:35	Nadh Ha Naseer - LAVA	312,2 MB
63.0	10.11.2022 10:24	Nadh Ha Naseer - LAVA	318,5 MB
62.0	10.11.2022 10:09	Nadh Ha Naseer - LAVA	318,7 MB
61.0	10.11.2022 09:49	Nadh Ha Naseer - LAVA	319,9 MB
60.0	09.11.2022 18:37	Nadh Ha Naseer - LAVA	318,7 MB
59.0	09.11.2022 18:30	Nadh Ha Naseer - LAVA	318,7 MB
58.0	09.11.2022 17:51	Nadh Ha Naseer - LAVA	317,8 MB
57.0	09.11.2022 16:51	Nadh Ha Naseer - LAVA	317,6 MB
56.0	09.11.2022 16:49	Nadh Ha Naseer - LAVA	317,6 MB
55.0	09.11.2022 16:28	Nadh Ha Naseer - LAVA	317,6 MB
54.0	09.11.2022 16:23	Nadh Ha Naseer - LAVA	317,6 MB
53.0	09.11.2022 16:01	Nadh Ha Naseer - LAVA	317,6 MB
52.0	09.11.2022 15:57	Nadh Ha Naseer - LAVA	317,6 MB

3.1.3 DIGITAL COLLABORATION

HOW TO USE SHAREPOINT ON ANY PROJECT

4. Weekly back up / Clean up file

4. Empty recycle bin

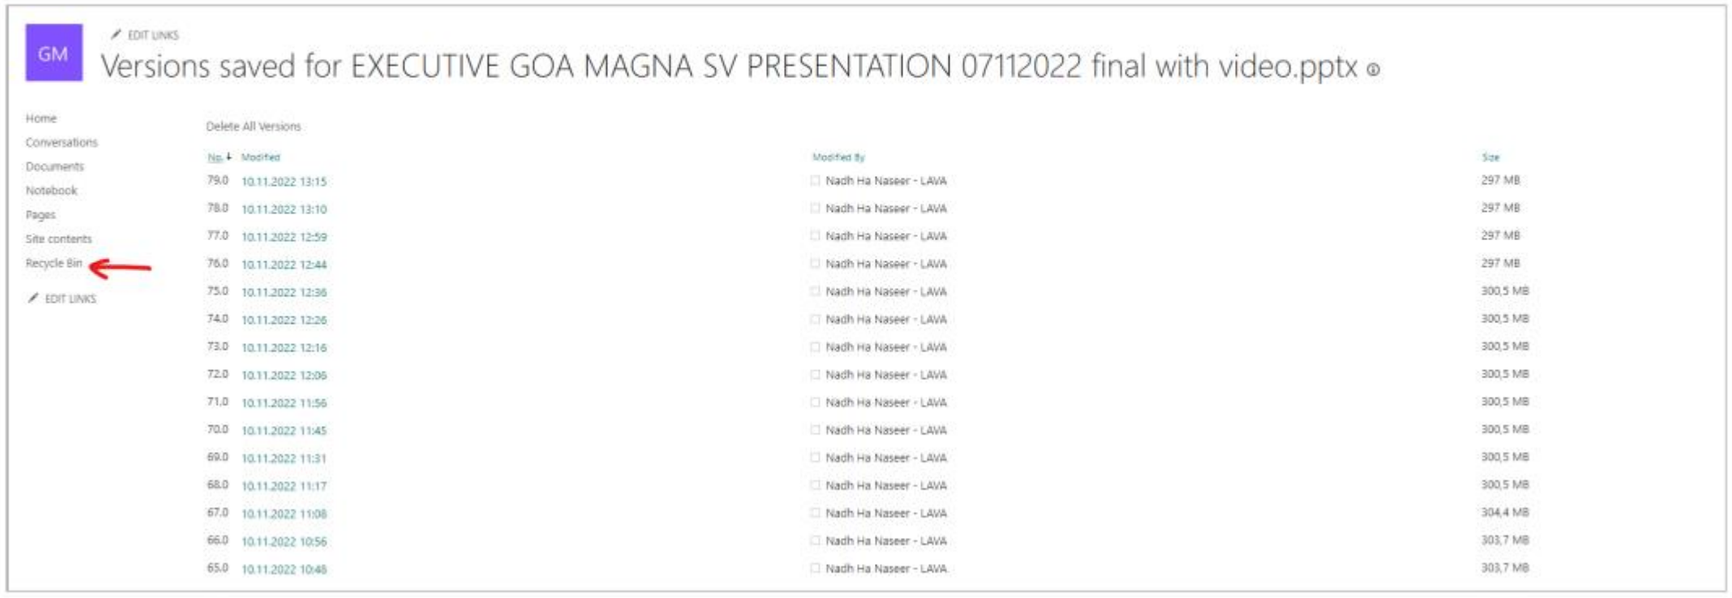

3.1.4 FILE NAMING CONVENTIONS

FILE NAMING CONVENTIONS FOR ANY PROJECT

Issue Document

Neom – Trojena – Signature Assets

Date_ NTSA_0000_XXX_Title of the file.

- Date that you are working on the file
- Project Number
- Project Initial

Working File

Your Initial

Date_ Title of the file_XX

Date that you are working on the file

3.1.4 FILE NAMING CONVENTIONS

FILE NAMING CONVENTIONS FOR ANY PROJECT

Main Combine File

Neom – Trojena – Signature Assets

Drawing Number

NTSA_0000_XXX_DWG 000_Title

Project Initial

Project Number

Worksession FIle

Neom – Trojena – Signature Assets

NTSA_0000_XXX_2D_Title

Project Initial

Project Number

Working File

Your Initial

Date_ Title of the file_XX


Date that you are working on the file

3.2 PLANNING

WHAT ARE THE KEY PRINCIPLES OF PLANNING ?


Time, Scope and Resource(Cost) are the **triple constraints** of Project Management which are interrelated. By default it is required to adhere to all three during a Project, however **trade-offs** are also possible if required by the Client or if determined necessary by Senior Leadership. Reducing or increasing one parameter will affect at least another (e.g. increase resourcing to achieve increased scope requirements, reducing scope to achieve a faster timeline, etc.)

SCOPE

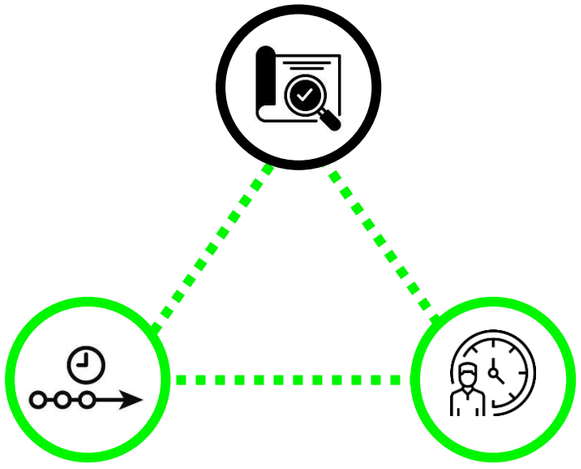


- **Breakdown & Delineation** – Eliminate ambiguities and gaps by ensuring scope items are subdivided into tasks and activities, and responsibilities are fully covered.
- **Quality** – The integrity of the design and deliverables to meet expectations and compliance needs identified by the Client and LAVA
- **Minimize Scope Creep** – Deliver exactly what is required, and escalate potential deviations to Project Leadership (e.g. requests for more work)

TIME

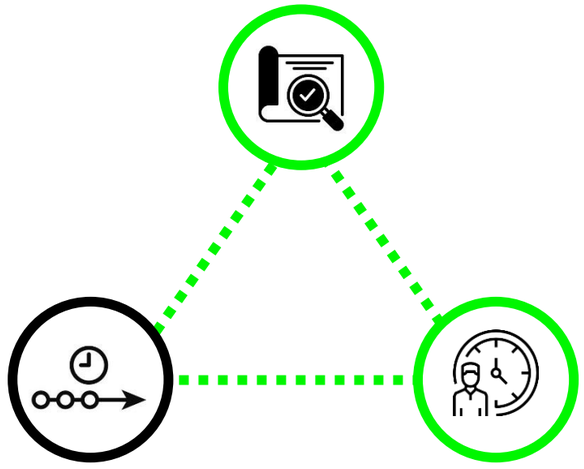

- **Interdependencies & Critical Paths** – Keep in mind pre-requisites when sequencing and scheduling activities. Consider the longest sequential chain of tasks as the critical path and prioritize it.
- **Milestones and Reviews** – Consider the time required to review internally work by LAVA or others, as well as external feedback from the Client and its impact.
- **Minimize Delay Risks** – Plan for early engagement with Stakeholders and regular check-ins, consider buffer periods for Quality Control, and set key decision points to reduce chances of downstream pressure.


RESOURCING

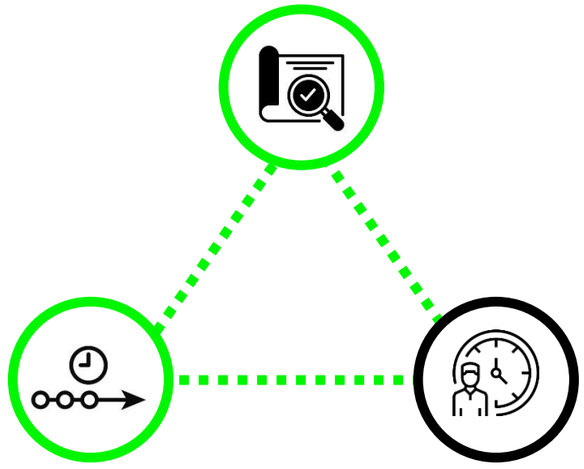

- **Resource = Cost** – Hours/days of work are assigned according to fees which are proposed and approved by the Client.
- **Parkinson's Law**– Work expands to fill the available time. Ensure tasks are not overstaffed or overestimated in time, and adjust planning if this becomes apparent.
- **Resource Crashing** – Certain tasks can be achieved faster by assigning more staff to them. On the other hand, some tasks take a certain amount of time no matter how many resources thrown at them.

3.2 PLANNING

WHAT ARE THE KEY PRINCIPLES OF PLANNING ?

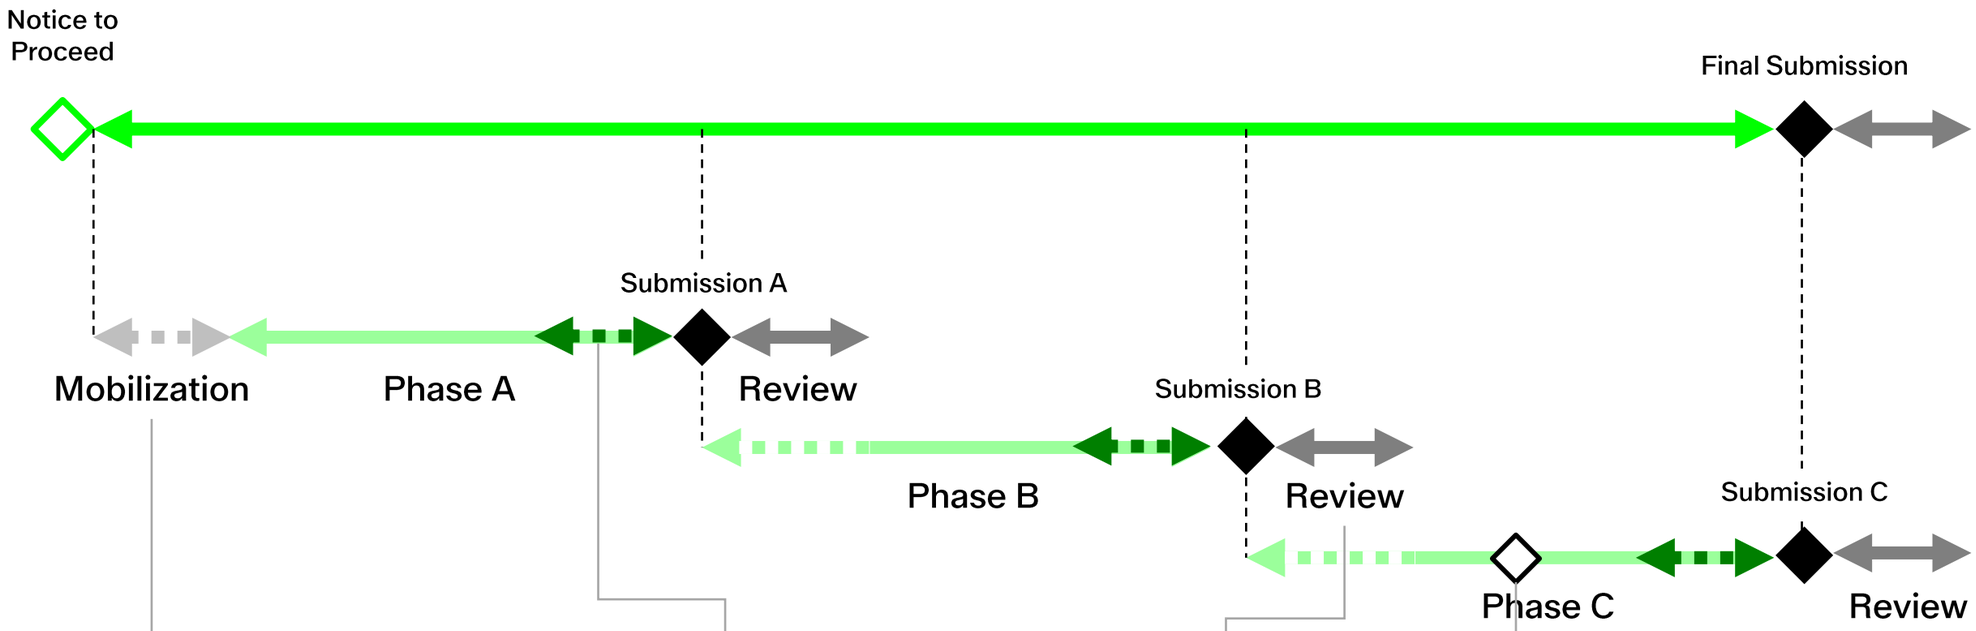

Early Planning Reduces Late Pressure

The majority of Project Management Planning efforts is front-loaded and happens during the mobilization period or early stages of a project. By ensuring the Project Team has access to the necessary tools to self-organize, track and monitor their progress, we assure quality and empower them to focus on the design.

Quality Control Buffers

Before a submission date, plan for internal Quality Checks according to the Project requirements, e.g. Sub-Consultants to submit to LAVA for internal review and adjustments before finalization and submissions to the Client.

As a rule of thumb, consider at least 25% of a certain phase duration for quality control, internal comments, and subsequent adjustments.

Client Reviews & Feedback

Following milestones, a Client Review period with a specific duration is either already defined in the agreement, or must be agreed during the Project. As a rule of thumb, review periods are between 1-2 weeks, but can be shorter or longer relative to the overall timeline.

It is important to keep in mind the impact that comments may have on the team's ability to deliver according to Planning. Therefore comments received outside of the review period which might be problematic should be flagged to Project Leadership.


Design Freeze

Design Freeze dates are set as a 'pencils-down' internal milestone for LAVA and Subconsultants to work off of the same version.

This assures quality in our work, so that deliverables are aligned, and that enough time is left for execution.

3.2 PLANNING

WHAT ARE THE KEY PRINCIPLES OF PLANNING ?

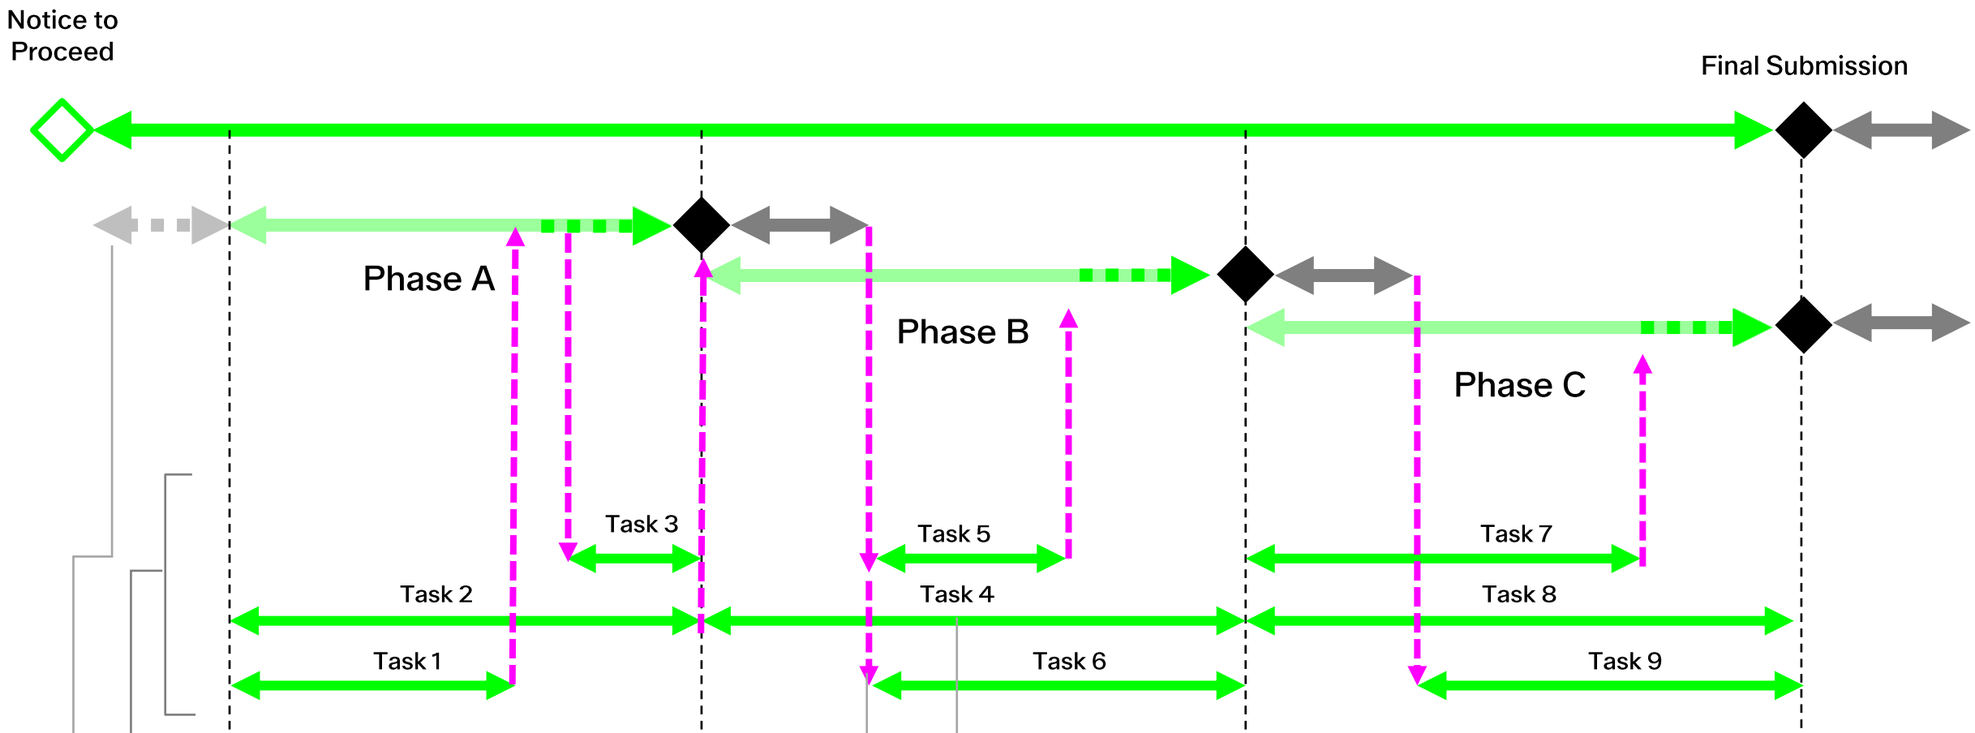

Tracking Deliverables and assigning Responsibilities

Based on the Scope of Work or on regulatory requirements, a list of intended Deliverables should be prepared during Mobilization.

Additionally, scope delineations (e.g. Scope Responsibility Matrix) with subconsultants should be clear as soon as possible, to ensure there are no scope gaps which appear later during the Project.

Scope Breakdown

Based on the List of Deliverables and assigned responsibilities, tasks and activities emerge which must be planned accordingly and assigned to responsible individuals within LAVA or as applicable.

Scope Interdependencies


It is good practice to identify which scope items need be prioritized first, to ensure that others can be progressed accordingly.

Critical Paths

Once tasks are identified and sequenced, it will become clear which sequence of activities takes the longest time to complete from start to finish. These must be prioritized to ensure timely production and delivery by responsible parties.

3.2 PLANNING

WHAT ARE THE KEY PRINCIPLES OF PLANNING ?

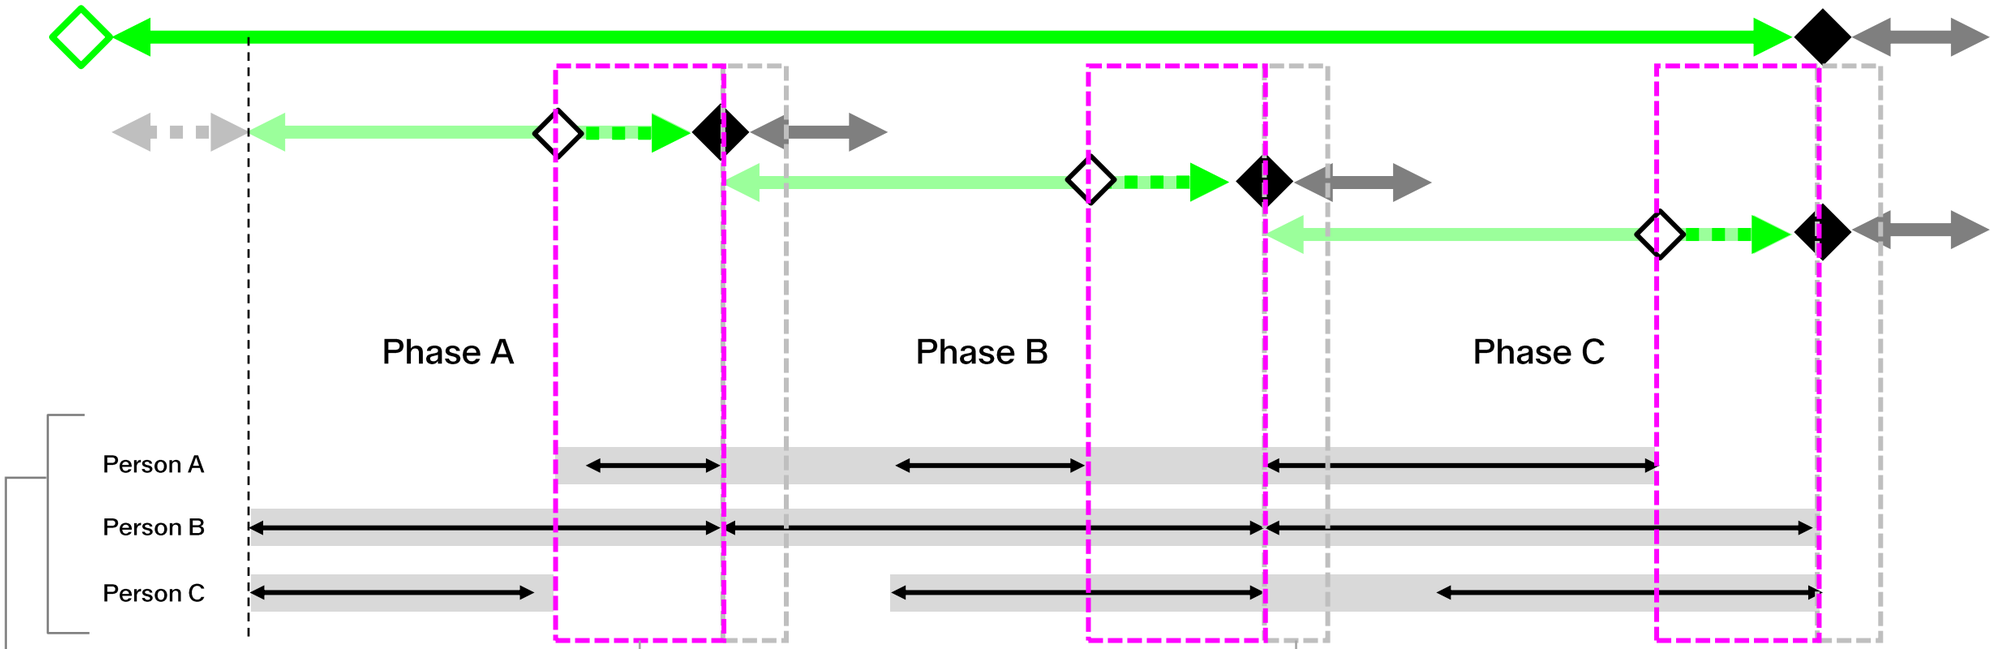

Distribute Tasks based on Skills, Roles, Availabilities

Ensure the right personnel are given the right tasks based on experience and technical requirements. This might mean having preliminary discussions with the team to confirm their abilities. Assignment of tasks should also consider Resource Availability based on the Team's degree of project participation (full-time vs. part-time) and the potential annual leaves which might be scheduled.

Complexity vs. Number of Personnel

Not all tasks are equal. Certain tasks require multiple people to achieve objectives within time constraints due to scale, difficulty or other parameters related to the work. Do not hesitate to update the Planning and re-assign personnel based on feedback from the team regarding this.

Monitoring Overhours

In general it is required to ensure that the Project Team delivers according to the resources (cost) estimated before the Project. Should certain personnel invest significantly more time than anticipated, seek to rebalance workloads within the Team, and/or alternatively escalate to Project Leadership to troubleshoot and find solutions if the entire team is under pressure.

Debriefs, Accountability & Continuous Improvements


Every milestone provides an opportunity to reflect on how the Project Team's performance can be improved to achieve more with less, how to minimize risks and avoid errors in next phase.

3.2.1 PROJECT LEADERSHIP & ROLES

WHAT ARE THE RESPONSIBILITIES WITHIN OUR TEAM ?

As part of Planning, it is important to define roles within a team, which will vary from one Project to another. It is recommended to produce an **Org Chart** at a minimum to clarify the individuals that define Project Leadership, and their inherent responsibilities.

In general, a **Project or Senior Architect** would be assigned as Project Lead responsible for the execution of design and deliverables, while a **Project or Design Manager** would be responsible for the Planning and other associated activities.

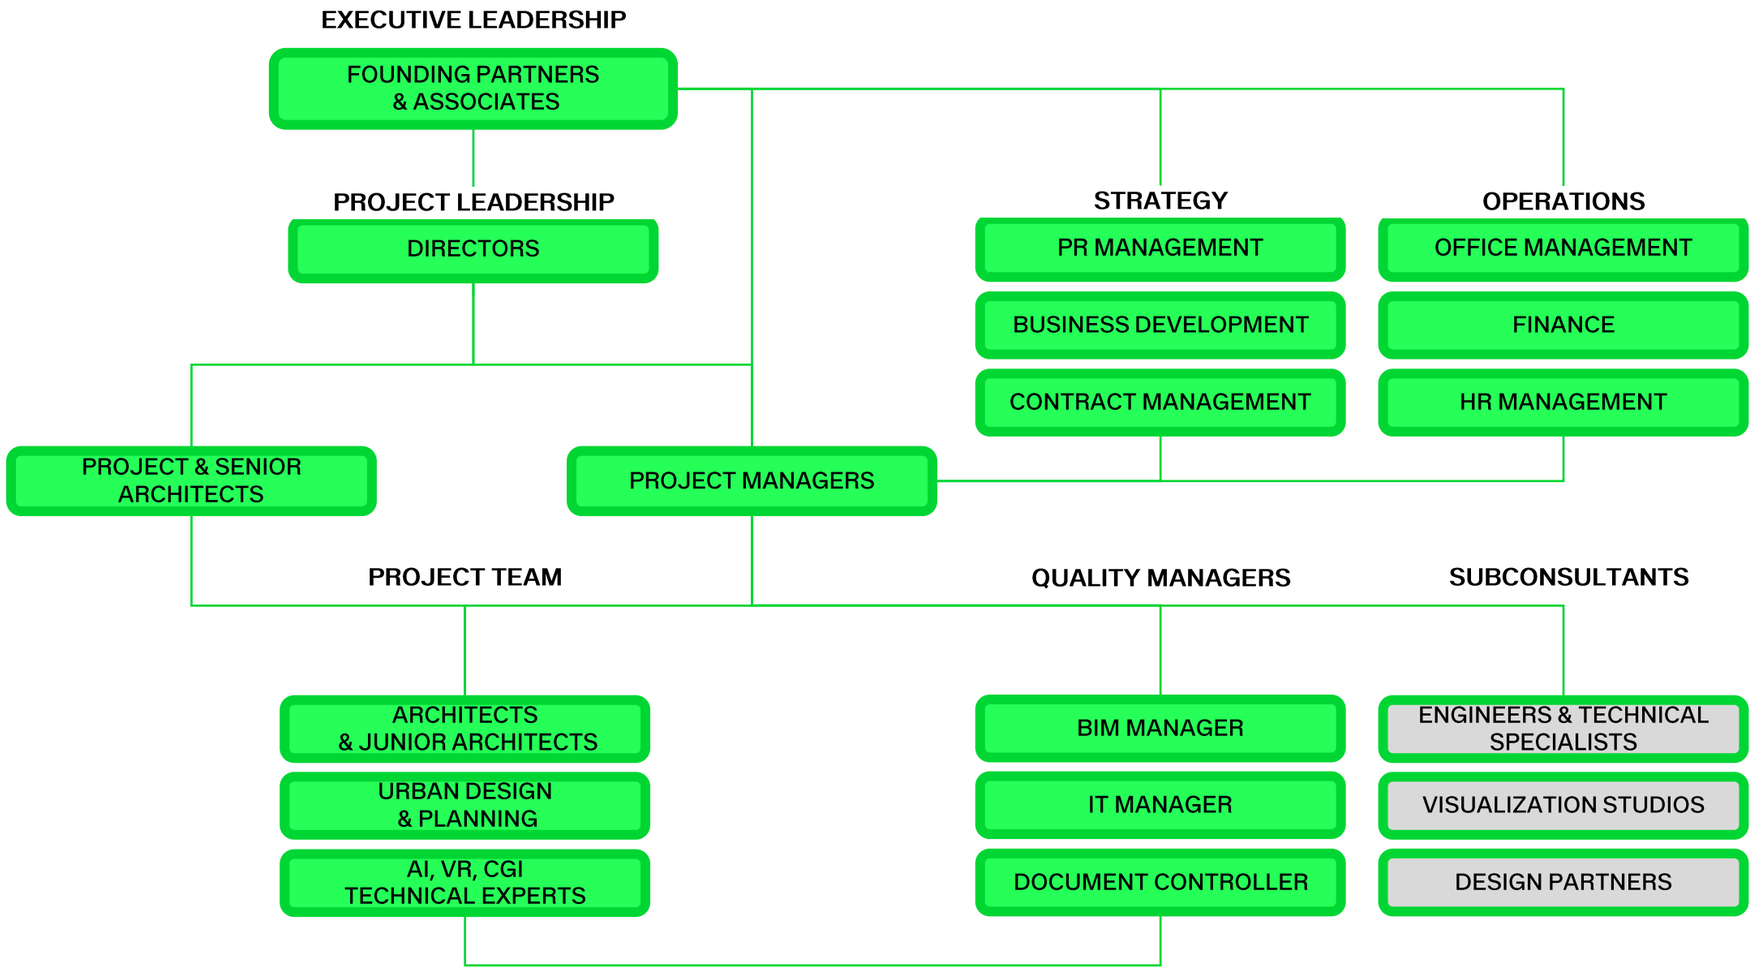


3.2.2 TIMELINE


HOW DO WE SCHEDULE OUR PROJECTS ?

Scheduling is the most common Project Management tool at LAVA. We use **Timelines** primarily to **schedule, monitor and control** our projects which are different in their **complexity and duration**. Additionally, we use Timelines to **communicate** on what will be done by when with **different participants** that have **varying roles, level of involvement and appetite for details** in the Project.

As a result, **three different templates** are given as potential starting points for all Projects. Ideally only one template is used in a Project, however it is likely two different templates might be required, and are subject to be **tailored, modified and used creatively** by teams to empower them in achieving their objectives :

- **High-Level Schedule** – weekly cadence with minimal details, suitable for overviews and communications with executive or senior leadership.
- **Daily Schedule** – detail-oriented breakdowns on daily basis, additionally allowing for resource tracking. Suitable for use by the Project Team internally.
- **Master Schedule** – weekly cadence for very large and complex projects, involving multiple stages across large periods.

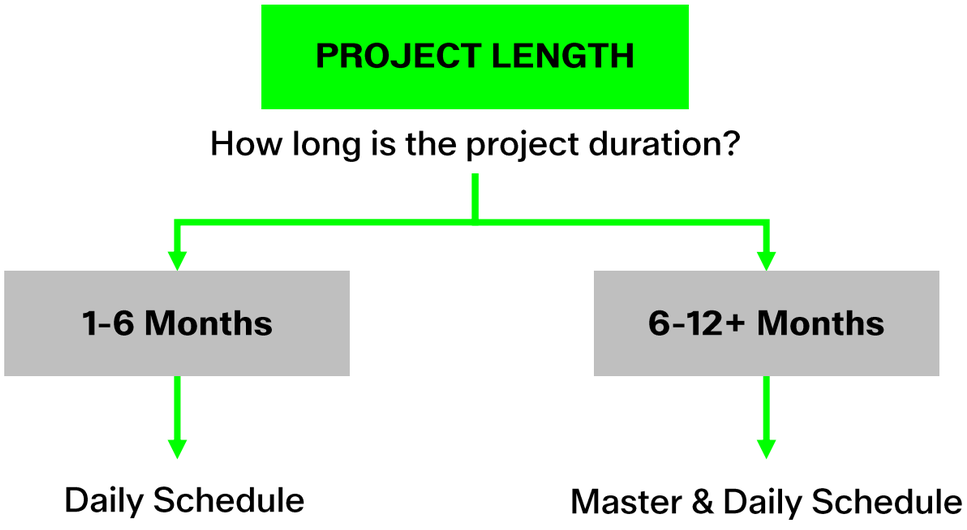

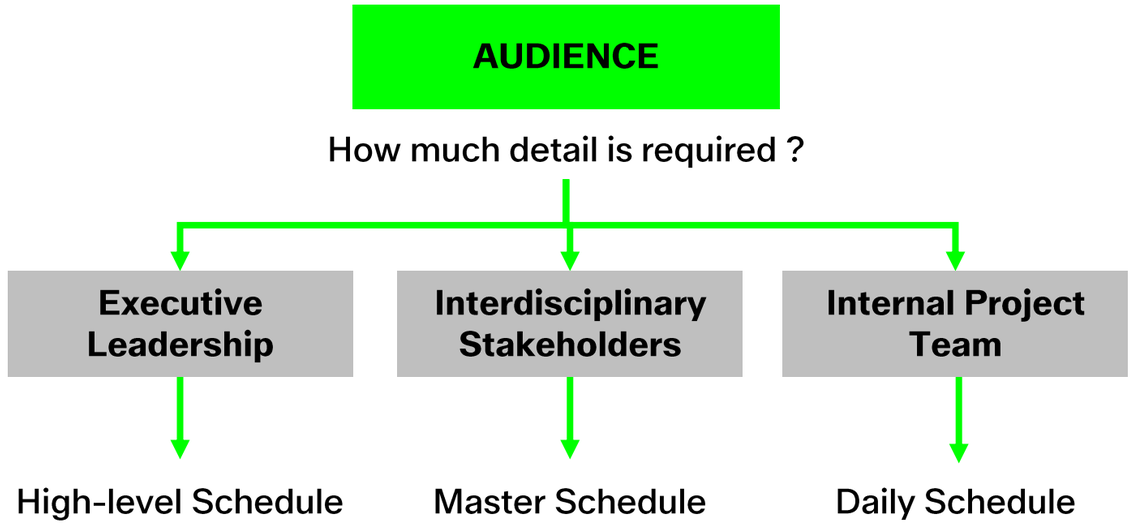

3.2.2 TIMELINE

HOW DO WE SCHEDULE OUR PROJECTS ?

OVERVIEW → DETAIL

HIGH LEVEL SCHEDULE

- Weekly cadence – suitable for projects ranging from weeks to a few months.
- Simple bar chart for streamlined communications to/from senior management.
- Can be used as a client-facing schedule to communicate big picture without details.
- Can be used as a project dashboard for weekly or bi-weekly reporting updates.

Key Features

- Timeline Overview
- Simple breakdown of phases or general tasks (e.g. Research, Design, Modelling, Rendering, etc.)

MASTER SCHEDULE

- Weekly cadence – suitable for projects over 6+ months and potentially over multiple years.
- Detailed Gantt chart
- Ideal for Framework Projects or Programs involving multiple sub-projects running in parallel (e.g. Masterplan + Assets + Infrastructure & Public Realm)
- Can be used as both team-facing (LAVA + External Sub-Consultants) and client-facing to provide an overview on overall program.

Key Features

- Timeline Overview + Detailed Breakdown of Scope
- Multi-year outlook
- Multi-disciplinary Scopes
- Suitable for mapping of Interdependencies

DAILY SCHEDULE

- Daily cadence – suitable for projects under 6 months.
- Detailed Gantt chart
- Ideal for internal team task distribution and tracking
- Primarily used as a team-facing schedule (LAVA + Sub-Consultant)
- Can be used as a client-facing schedule, however Project Team to ensure internal information is hidden (e.g. Resource Availability, Responsibility assignments)

Key Features

- Timeline Overview + Detailed Breakdown of Scope
- Daily Milestone Tracking
- Activities & Tasks
- Resource Availability


3.2.2 TIMELINE

HIGH-LEVEL TIMELINE

For smaller projects, early planning during Bidding, or to simplify communications with leadership, a **High-Level Timeline** can be used which is easy to produce and update. For more complex planning on a weekly or daily cadence, the following pages include alternative templates.

Project Start Date input automates the months, weeks and years to save time

Key Timeline Overview to sequentially highlight key activities and milestones

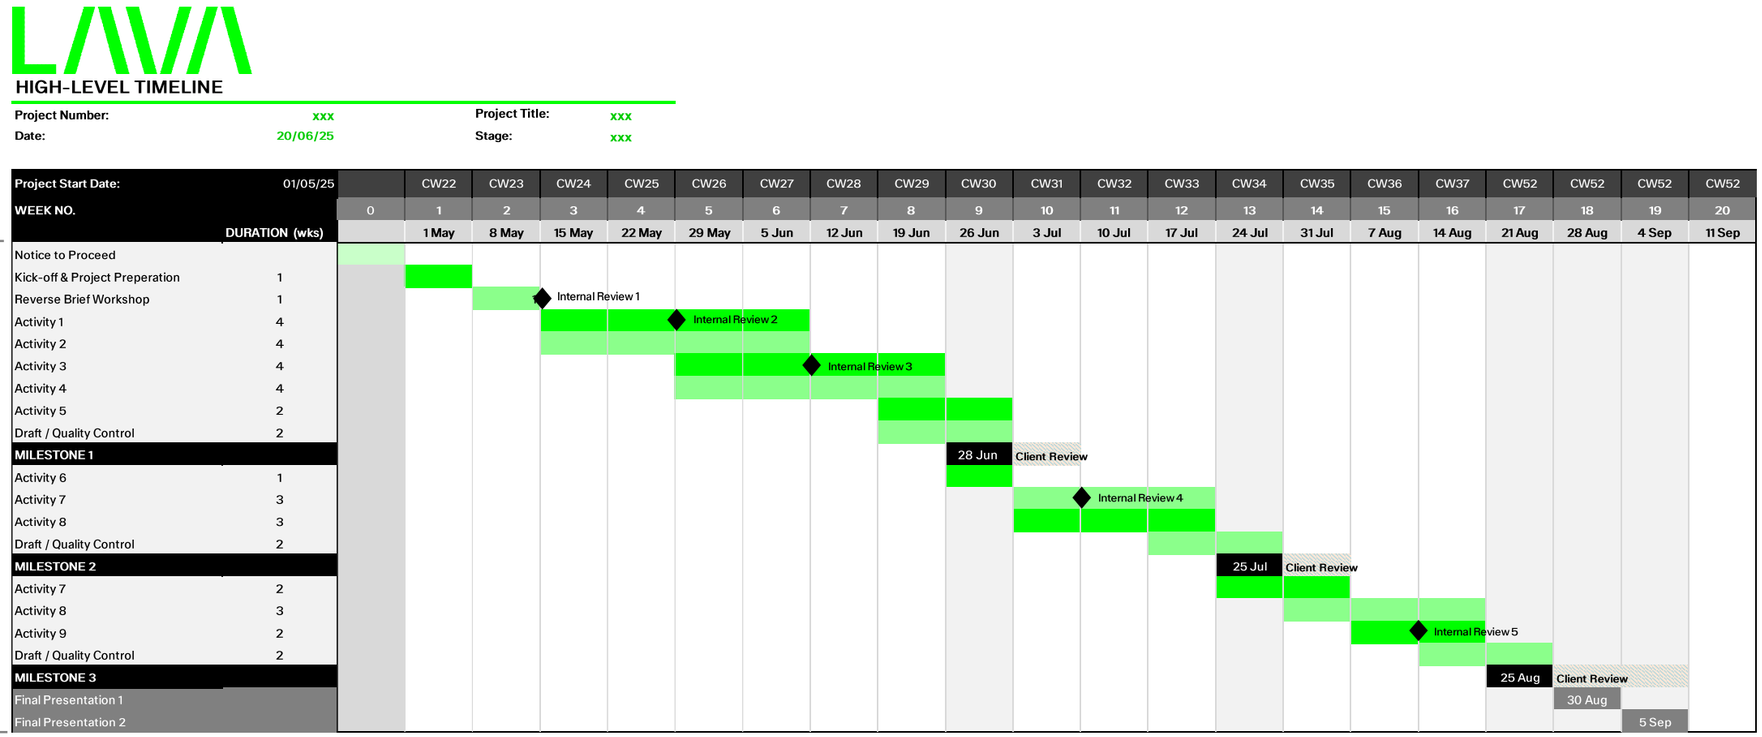

3.2.2 TIMELINE

TIMELINE WITH WEEKLY CADENCE

Project Start Date input automates the months, weeks and years to save time


Timeline Overview to track separate stages from a longer-term complex project

Interdependencies between scope items or deliverables can be manually illustrated with arrows

Scope Overview to track individual deliverables, disciplines, etc.

Key Meetings are called out at the bottom to reduce clutter in the timeline

Current Date is automatically highlighted

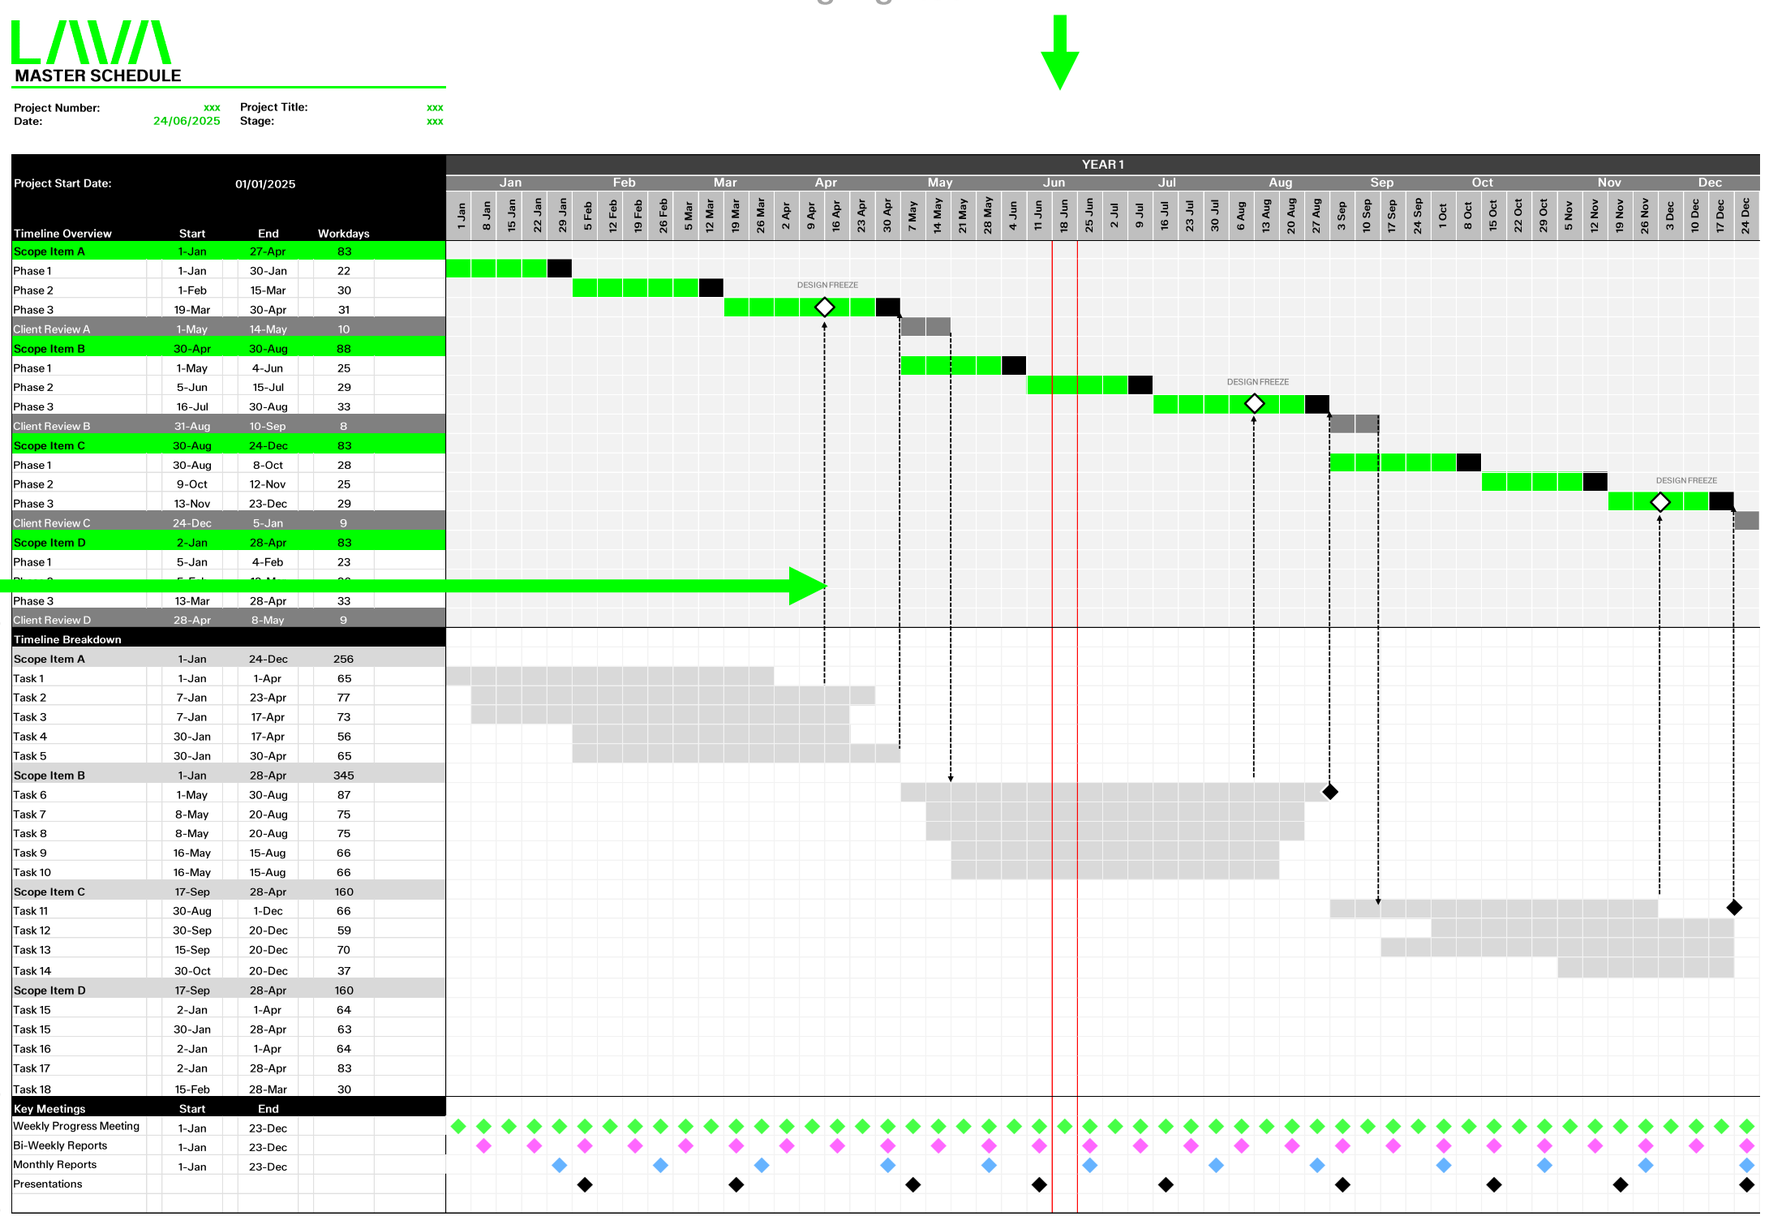

Timeline Overview	Start	End	Workdays
Scope Item A	1-Jan	27-Apr	83
Phase 1	1-Jan	30-Jan	22
Phase 2	1-Feb	15-Mar	30
Phase 3	19-Mar	30-Apr	31
Client Review A	1-May	14-May	10
Scope Item B	30-Apr	30-Aug	88
Phase 1	1-May	4-Jun	25
Phase 2	5-Jun	15-Jul	29
Phase 3	16-Jul	30-Aug	33
Client Review B	31-Aug	10-Sep	8
Scope Item C	30-Aug	24-Dec	83
Phase 1	30-Aug	8-Oct	28
Phase 2	9-Oct	12-Nov	25
Phase 3	13-Nov	23-Dec	29
Client Review C	24-Dec	5-Jan	9
Scope Item D	2-Jan	28-Apr	83
Phase 1	5-Jan	4-Feb	23
Phase 3	13-Mar	28-Apr	33
Client Review D	28-Apr	8-May	9

Timeline Breakdown			
Scope Item A	1-Jan	24-Dec	256
Task 1	1-Jan	1-Apr	65
Task 2	7-Jan	23-Apr	77
Task 3	7-Jan	17-Apr	73
Task 4	30-Jan	17-Apr	56
Task 5	30-Jan	30-Apr	65
Scope Item B	1-Jan	28-Apr	345
Task 6	1-May	30-Aug	87
Task 7	8-May	20-Aug	75
Task 8	8-May	20-Aug	75
Task 9	16-May	15-Aug	66
Task 10	16-May	15-Aug	66
Scope Item C	17-Sep	28-Apr	160
Task 11	30-Aug	1-Dec	66
Task 12	30-Sep	20-Dec	59
Task 13	15-Sep	20-Dec	70
Task 14	30-Oct	20-Dec	37
Scope Item D	17-Sep	28-Apr	160
Task 15	2-Jan	1-Apr	64
Task 15	30-Jan	28-Apr	63
Task 16	2-Jan	1-Apr	64
Task 17	2-Jan	28-Apr	83
Task 18	15-Feb	28-Mar	30

Key Meetings	Start	End
Weekly Progress Meeting	1-Jan	23-Dec
Bi-Weekly Reports	1-Jan	23-Dec
Monthly Reports	1-Jan	23-Dec
Presentations		

3.2.2 TIMELINE

TIMELINE WITH DAILY CADENCE

Project Start Date input automates the months, weeks and days to save time


Timeline Overview summarizes the phases or scope categories, as well as review periods. Start and End Dates inputs automate how cells are filled.

Key Milestones summarizes the key meetings and submissions. Start and End Dates inputs automate how cells are filled.

Timeline Breakdown is used to track individual items, categorized based on discipline, deliverables, etc. Start and End Dates inputs automate how cells are filled. Bars in green can be used to track planned resourcing, bars underneath in grey can track the actual resourcing.

Team Availability is often used in LAVA projects to track project resourcing

Current Date is automatically highlighted

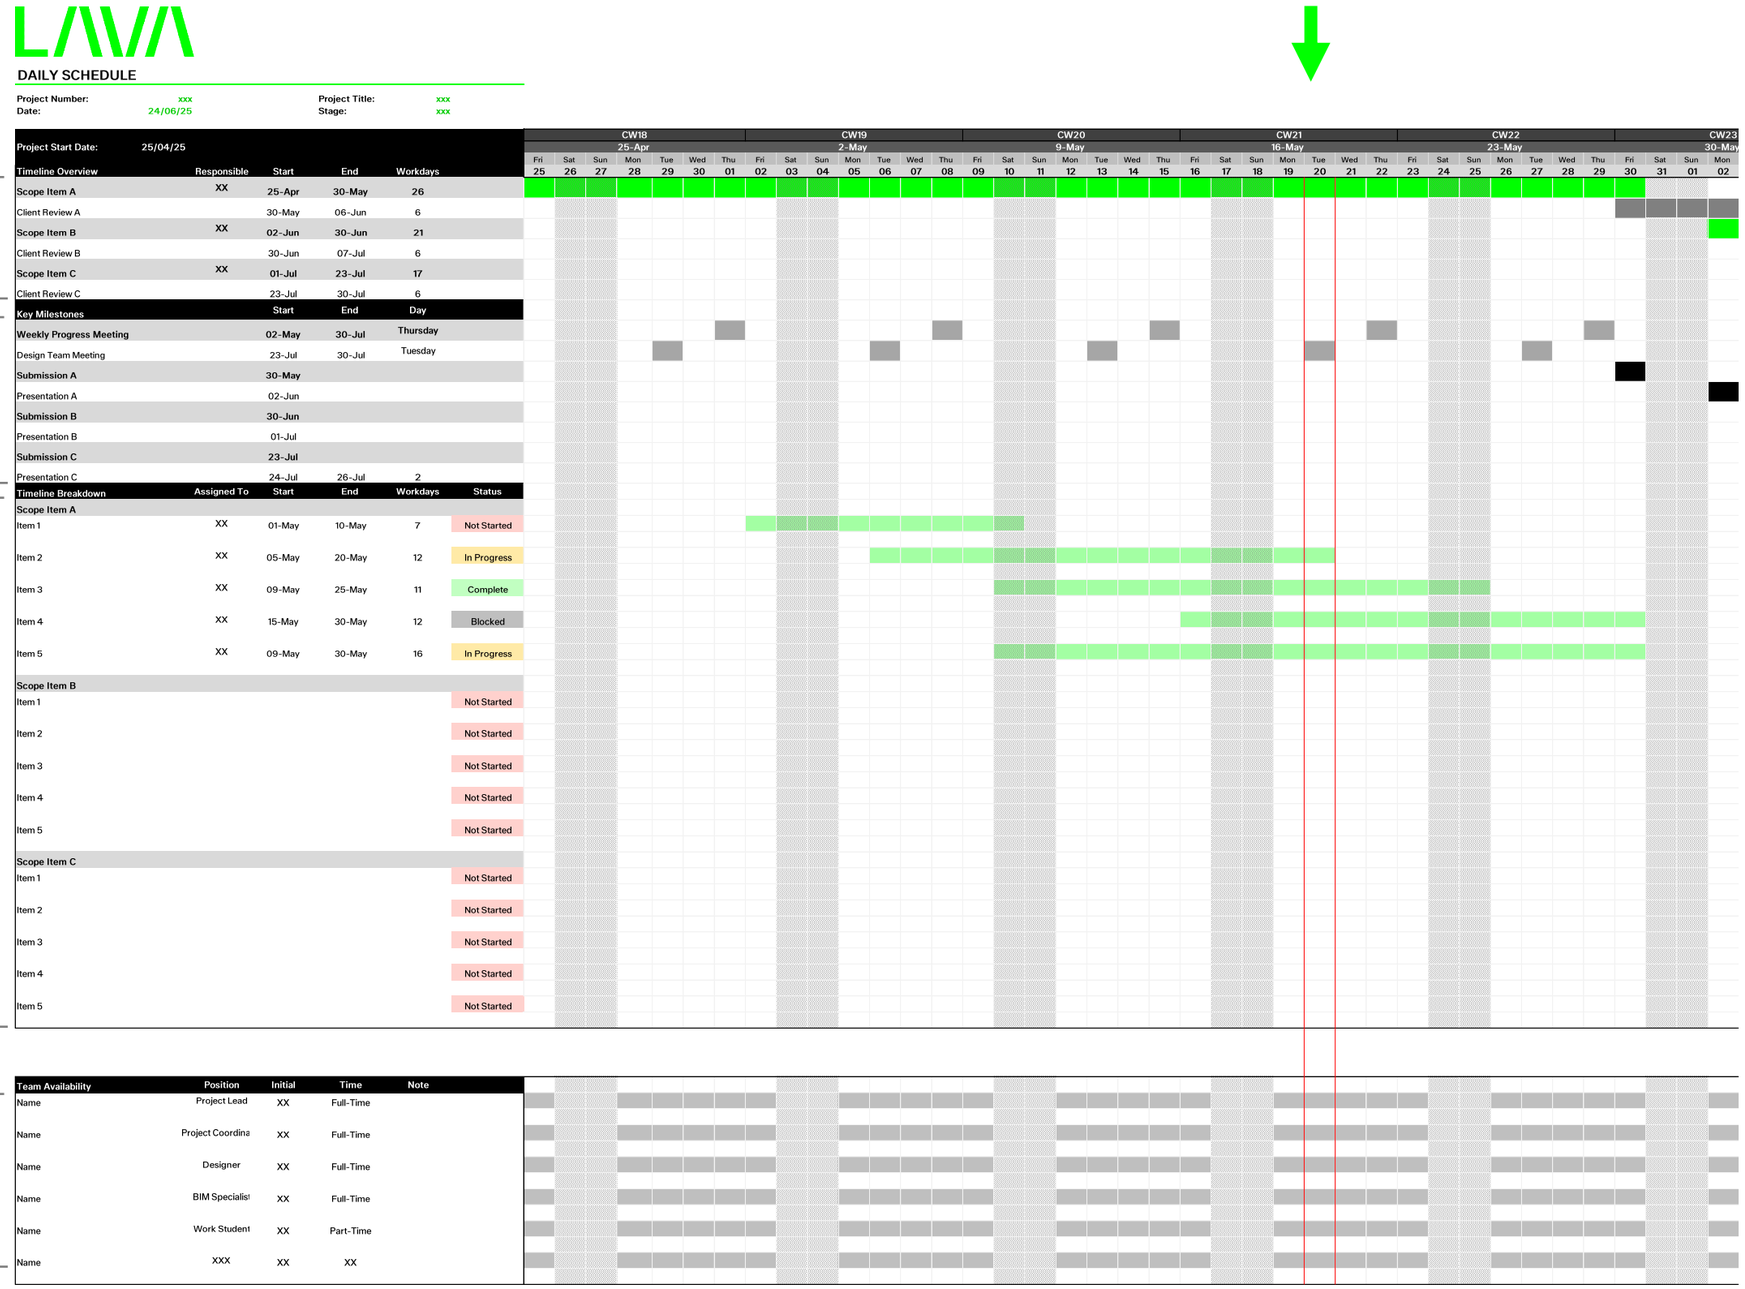

DAILY SCHEDULE

Project Number: xxx
Date: 24/06/25
Project Title: xxx
Stage: xxx

Project Start Date: 25/04/25

Timeline Overview	Responsible	Start	End	Workdays
Scope Item A	XX	25-Apr	30-May	26
Client Review A		30-May	06-Jun	6
Scope Item B	XX	02-Jun	30-Jun	21
Client Review B		30-Jun	07-Jul	6
Scope Item C	XX	01-Jul	23-Jul	17
Client Review C		23-Jul	30-Jul	6

Key Milestones	Start	End	Day
Weekly Progress Meeting	02-May	30-Jul	Thursday
Design Team Meeting	23-Jul	30-Jul	Tuesday
Submission A	30-May		
Presentation A	02-Jun		
Submission B	30-Jun		
Presentation B	01-Jul		
Submission C	23-Jul		
Presentation C	24-Jul	26-Jul	2

Timeline Breakdown	Assigned To	Start	End	Workdays	Status
Scope Item A					
Item 1	XX	01-May	10-May	7	Not Started
Item 2	XX	05-May	20-May	12	In Progress
Item 3	XX	09-May	25-May	11	Complete
Item 4	XX	15-May	30-May	12	Blocked
Item 5	XX	09-May	30-May	16	In Progress
Scope Item B					
Item 1					Not Started
Item 2					Not Started
Item 3					Not Started
Item 4					Not Started
Item 5					Not Started
Scope Item C					
Item 1					Not Started
Item 2					Not Started
Item 3					Not Started
Item 4					Not Started
Item 5					Not Started

Team Availability	Position	Initial	Time	Note
Name	Project Lead	XX	Full-Time	
Name	Project Coordina	XX	Full-Time	
Name	Designer	XX	Full-Time	
Name	BIM Specialist	XX	Full-Time	
Name	Work Student	XX	Part-Time	
Name	XXX	XX	XX	

CW18 25-Apr: Fri 25, Sat 26, Sun 27, Mon 28, Tue 29, Wed 30, Thu 01
CW19 2-May: Fri 02, Sat 03, Sun 04, Mon 05, Tue 06, Wed 07, Thu 08
CW20 9-May: Fri 09, Sat 10, Sun 11, Mon 12, Tue 13, Wed 14, Thu 15
CW21 16-May: Fri 16, Sat 17, Sun 18, Mon 19, Tue 20, Wed 21, Thu 22
CW22 23-May: Fri 23, Sat 24, Sun 25, Mon 26, Tue 27, Wed 28, Thu 29
CW23 30-May: Fri 30, Sat 31, Sun 01, Mon 02

3.2.3 RESOURCING

WIP

HOW DO WE MANAGE OUR RESOURCING ?

OVERVIEW ON MONITORING & CONTROLLING PLANNED HOURS VS. ACTUAL HOURS SPENT:

1. RESOURCE BREAKDOWN SCHEDULE DERIVED FROM COST PROPOSALS AS PLANNED (HOURS PER WEEK PER ROLE)

2. POOLARSERVER RESOURCE DATA (HOURS LOGGED BY PROJECT TEAM) AS ACTUAL

TOOL / TEMPLATE FOR STREAMLINING PROCESS UNDER DEVELOPMENT – MIDTERM GOAL (3-6 MONTHS)

3.2.4 DELIVERABLES LIST

HOW DO WE TRACK PROJECT DELIVERABLES ?

Based on the Scope of Works and any relevant procedures, a Project Manager should list out all requirements for submission. For more complex projects, a **Work Breakdown Structure** might be required to track deliverables using a hierarchical numbering system. For simpler projects, this information could be hidden.

Level sets the hierarchy of the row (e.g. 1.1.1 or 1.1). Adjust it to ensure the WBS formula works accordingly.

WBS stands for Work Breakdown Structure. The count is automated based on a formula, depending on the Level. Copy and paste the formula to trigger the count.

Deliverables List

Level	WBS	Discipline	Content	Responsibility	Phase	Format / Scale	Status	Revision	Date	Link	Comments
1	1	Discipline 1		Consultant 1							
2	1.1	Deliverables Type 1									
3	1.1.1	Discipline 1	Deliverable Name	Consultant 1			To-Do	1	DD/MM/YYYY	LINK	
3	1.1.2	Discipline 1	Deliverable Name	Consultant 1			To-Do	1	DD/MM/YYYY	LINK	
3	1.1.3	Discipline 1	Deliverable Name	Consultant 1			To-Do	1	DD/MM/YYYY	LINK	
3	1.1.4	Discipline 1	Deliverable Name	Consultant 1			To-Do	1	DD/MM/YYYY	LINK	
2	1.2	Deliverables Type 1									
3	1.2.1	Discipline 1	Deliverable Name	Consultant 1			WIP	1	DD/MM/YYYY		
3	1.2.2	Discipline 1	Deliverable Name	Consultant 1			WIP	1	DD/MM/YYYY		
3	1.2.3	Discipline 1	Deliverable Name	Consultant 1			WIP	1	DD/MM/YYYY		
3	1.2.4	Discipline 1	Deliverable Name	Consultant 1			WIP	1	DD/MM/YYYY		
2	1.3	Deliverables Type 1									
3	1.3.1	Discipline 1	Deliverable Name	Consultant 1			Completed	1	DD/MM/YYYY		
3	1.3.2	Discipline 1	Deliverable Name	Consultant 1			Completed	1	DD/MM/YYYY		
3	1.3.3	Discipline 1	Deliverable Name	Consultant 1			Completed	1	DD/MM/YYYY		
3	1.3.4	Discipline 1	Deliverable Name	Consultant 1			Completed	1	DD/MM/YYYY		
1	2	Discipline 2		Consultant 2							
2	2.1	Deliverables Type 1									
3	2.1.1	Discipline 2	Deliverable Name	Consultant 2			To-Do	1	DD/MM/YYYY		
3	2.1.2	Discipline 2	Deliverable Name	Consultant 2			To-Do	1	DD/MM/YYYY		
3	2.1.3	Discipline 2	Deliverable Name	Consultant 2			To-Do	1	DD/MM/YYYY		
3	2.1.4	Discipline 2	Deliverable Name	Consultant 2			To-Do	1	DD/MM/YYYY		
2	2.2	Deliverables Type 1									
3	2.2.1	Discipline 2	Deliverable Name	Consultant 2			WIP	1	DD/MM/YYYY		
3	2.2.2	Discipline 2	Deliverable Name	Consultant 2			WIP	1	DD/MM/YYYY		
3	2.2.3	Discipline 2	Deliverable Name	Consultant 2			WIP	1	DD/MM/YYYY		
3	2.2.4	Discipline 2	Deliverable Name	Consultant 2			WIP	1	DD/MM/YYYY		
2	2.3	Deliverables Type 1									
3	2.3.1	Discipline 2	Deliverable Name	Consultant 2			Completed	1	DD/MM/YYYY		
3	2.3.2	Discipline 2	Deliverable Name	Consultant 2			Completed	1	DD/MM/YYYY		
3	2.3.3	Discipline 2	Deliverable Name	Consultant 2			Completed	1	DD/MM/YYYY		
3	2.3.4	Discipline 2	Deliverable Name	Consultant 2			Completed	1	DD/MM/YYYY		
1	3	Discipline 3		Consultant 3							
2	3.1	Deliverables Type 1									
3	3.1.1	Discipline 3	Deliverable Name	Consultant 3			To-Do	1	DD/MM/YYYY		
3	3.1.2	Discipline 3	Deliverable Name	Consultant 3			To-Do	1	DD/MM/YYYY		
3	3.1.3	Discipline 3	Deliverable Name	Consultant 3			To-Do	1	DD/MM/YYYY		
3	3.1.4	Discipline 3	Deliverable Name	Consultant 3			To-Do	1	DD/MM/YYYY		
2	3.2	Deliverables Type 1									
3	3.2.1	Discipline 3	Deliverable Name	Consultant 3			WIP	1	DD/MM/YYYY		
3	3.2.2	Discipline 3	Deliverable Name	Consultant 3			WIP	1	DD/MM/YYYY		
3	3.2.3	Discipline 3	Deliverable Name	Consultant 3			WIP	1	DD/MM/YYYY		
3	3.2.4	Discipline 3	Deliverable Name	Consultant 3			WIP	1	DD/MM/YYYY		
2	3.3	Deliverables Type 1									
3	3.3.1	Discipline 3	Deliverable Name	Consultant 3			Completed	1	DD/MM/YYYY		
3	3.3.2	Discipline 3	Deliverable Name	Consultant 3			Completed	1	DD/MM/YYYY		
3	3.3.3	Discipline 3	Deliverable Name	Consultant 3			Completed	1	DD/MM/YYYY		
3	3.3.4	Discipline 3	Deliverable Name	Consultant 3			Completed	1	DD/MM/YYYY		

Status has built-in conditional formatting with a pull-down list.

Revision, Date, Links and Comments may be filled by the team to track our deliverables

3.2.5 SCOPE & RESPONSIBILITIES

HOW DO WE MANAGE SCOPE RESPONSIBILITIES ?

Scope Responsibilities are usually defined when working with multiple sub-consultants as part of a consortium, to ensure that there are no scope gaps or duplication of work. There are various ways this can be planned and documented should this be required for a specific Project. One example would be **using the Deliverables List** in combination with a **RACI Matrix (Responsible – Accountable – Consulted – Informed)**

Responsible – Develops and completes the deliverable. Ensures others are consulted or informed accordingly.

Accountable – Provides ultimate sign-off on the work that the Responsible party provides. LAVA is always accountable for sub-consultants.

Consulted – Their feedback on the deliverable needs to be considered.

Informed – Kept in the loop of communications on how and when a deliverable progresses.

Project Team parties can be configured manually depending on the configuration of each Project.

Responsibility can be assigned using a RACI pulldown for each deliverable depending on each party listed above

Level	WBS	Discipline	Content	Project Team						
				LAVA	Sub-Consultant 1	Sub-Consultant 2	Sub-Consultant 3	Sub-Consultant 4	Sub-Consultant 5	Sub-Consultant 6
1	1	Discipline 1								
2	1.1	Deliverables Type 1								
3	1.1.1	Discipline 1	Deliverable Name	R	I	I	I	I	I	I
3	1.1.2	Discipline 1	Deliverable Name	R	I	I	I	I	I	I
3	1.1.3	Discipline 1	Deliverable Name	R	I	I	I	I	I	I
3	1.1.4	Discipline 1	Deliverable Name	R	I	I	I	I	I	I
2	1.2	Deliverables Type 1								
3	1.2.1	Discipline 1	Deliverable Name	R	C	C	I	I	I	I
3	1.2.2	Discipline 1	Deliverable Name	R	C	C	I	I	I	I
3	1.2.3	Discipline 1	Deliverable Name	R	C	C	I	I	I	I
3	1.2.4	Discipline 1	Deliverable Name	R	C	C	I	I	I	I
2	1.3	Deliverables Type 1								
3	1.3.1	Discipline 1	Deliverable Name	A	C	R	I	I	I	I
3	1.3.2	Discipline 1	Deliverable Name	A	C	R	I	I	I	I
3	1.3.3	Discipline 1	Deliverable Name	A	C	R	I	I	I	I
3	1.3.4	Discipline 1	Deliverable Name	A	C	R	I	I	I	I
1	2	Discipline 2								
2	2.1	Deliverables Type 1								
3	2.1.1	Discipline 2	Deliverable Name	A	R	C	I	C	C	C
3	2.1.2	Discipline 2	Deliverable Name	A	R	C	I	C	C	C
3	2.1.3	Discipline 2	Deliverable Name	A	R	C	I	C	C	C
3	2.1.4	Discipline 2	Deliverable Name	A	R	C	I	C	C	C
2	2.2	Deliverables Type 1								
3	2.2.1	Discipline 2	Deliverable Name	A	R	C	I	C	I	I
3	2.2.2	Discipline 2	Deliverable Name	A	R	C	I	C	I	I
3	2.2.3	Discipline 2	Deliverable Name	A	R	C	I	C	I	I
3	2.2.4	Discipline 2	Deliverable Name	A	R	C	I	C	I	I
2	2.3	Deliverables Type 1								
3	2.3.1	Discipline 2	Deliverable Name	A	R	I	I	I	I	I
3	2.3.2	Discipline 2	Deliverable Name	A	R	I	I	I	I	I
3	2.3.3	Discipline 2	Deliverable Name	A	R	I	I	I	I	I
3	2.3.4	Discipline 2	Deliverable Name	A	R	I	I	I	I	I

3.2.6 PROJECT DIRECTORY

WHAT IS THE PROJECT DIRECTORY?

In all cases, it is required to simply list out the **team members and key points-of-contact** from a Client Team or Sub-Consultants in a project. For more complex projects, the Project Directory can also serve as a **Stakeholder Register**, keeping track of relevant parties such as Authorities. The template is extensive and certain columns may also be hidden when not required (e.g. Title, Location, etc.)

The template below is extensive as a start, and includes **many columns which can be hidden** on a project-basis, subject to the Project Leadership's decision.

Name column for **LAVA** includes a drop-down list which uses data inputs which are manually copied into the **Poolarserver Staff tab**. Every so often, the Data must be manually updated by the Project Management team to align with the latest list of staff at LAVA.

Location and Work Email are automatically filled once the name is selected

Organization	Discipline	Project Role	Position	Title	Name	Location	Work Email	Phone Number	Comments
NEOM	Trojena	Client							
NEOM	Trojena	Client Representative	Project Manager	Mr.			-		
NEOM	Trojena	Procurements	Senior Manager	Mr.			-		
NEOM	Trojena	Leadership	Executive Director	Mr.					
NEOM	Trojena	Infrastructure	Senior Design Manager	Mrs.					
LAVA	Architecture	Lead Consultant							
LAVA	Architecture	Leadership	Partner	Mr.	Tobias Wallisser	Berlin	t.wallisser@l-a-v-a.com		
					Lukas Kronawitter	Berlin	l.Kronawitter@l-a-v-a.com		
LAVA	Architecture	Technical Lead	Senior Architect	Mr.	Hessamedin Fana	Stuttgart	h.fana@l-a-v-a.com		
LAVA	Architecture	Design Lead	Senior Architect	Ms.	Veronika Volkova	Berlin	v.volkova@l-a-v-a.com		
LAVA	Architecture	Coordination	Senior Architect	Mr.	Tarak Mehta	Berlin	t.mehta@l-a-v-a.com		
LAVA	Architecture	Invoicing / Contracts	Head of Finance	Mrs.	Greshma Babu	Berlin	g.babu@l-a-v-a.com		
Consultant 1	Engineering	Sub-Consultant							
Consultant 1	Engineering	Leadership	Partner	Mrs.					
Consultant 1	Engineering	Leadership	Director	Mr.					
Consultant 1	Engineering	Management	Design Manager	Mr.					
Consultant 1	Engineering	MEP	Senior Engineer	Mrs.					
Consultant 1	Engineering	Structure	Senior Engineer	Mr.					
Consultant 1	Engineering	Geotechnical	Senior Engineer	Mr.					
Consultant 1	Engineering	Invoicing / Contracts	Administration	Mr.					
Consultant 2	Landscape Design	Sub-Consultant							
Consultant 2	Landscape Design	Leadership	Partner	Mrs.					
Consultant 2	Landscape Design	Leadership	Director	Mr.					
Consultant 2	Landscape Design	Management	Design Manager	Mr.					
Consultant 2	Landscape Design	Design Lead	Senior Designer	Mrs.					
Consultant 2	Landscape Design		Administration	Mr.					

Information for other parties must be filled manually by Project Leadership, including the Organization, Discipline and individual details.


In the future, there is potential for building a **Consultant Database** using information filled for other parties, which can become another tab that automates information using drop-down bars.

3.3 EXECUTION

WHAT IS THE EXECUTION STAGE?

The Execution phase is when the Project Planning is put into action :

- **Inquire, Imagine, Invent** - LAVA starts the Project by asking the right questions, researching and analyzing, investigating alternatives and making decisions based on careful evaluation;
- Resources are deployed to **execute tasks and activities** and deliver the outputs within the agreed timeframe;
- **Progress is reported** and **Coordination** is conducted both internally (Project Team, Leadership, Sub-Consultants) and externally (Client, Stakeholders, Authorities, etc.)

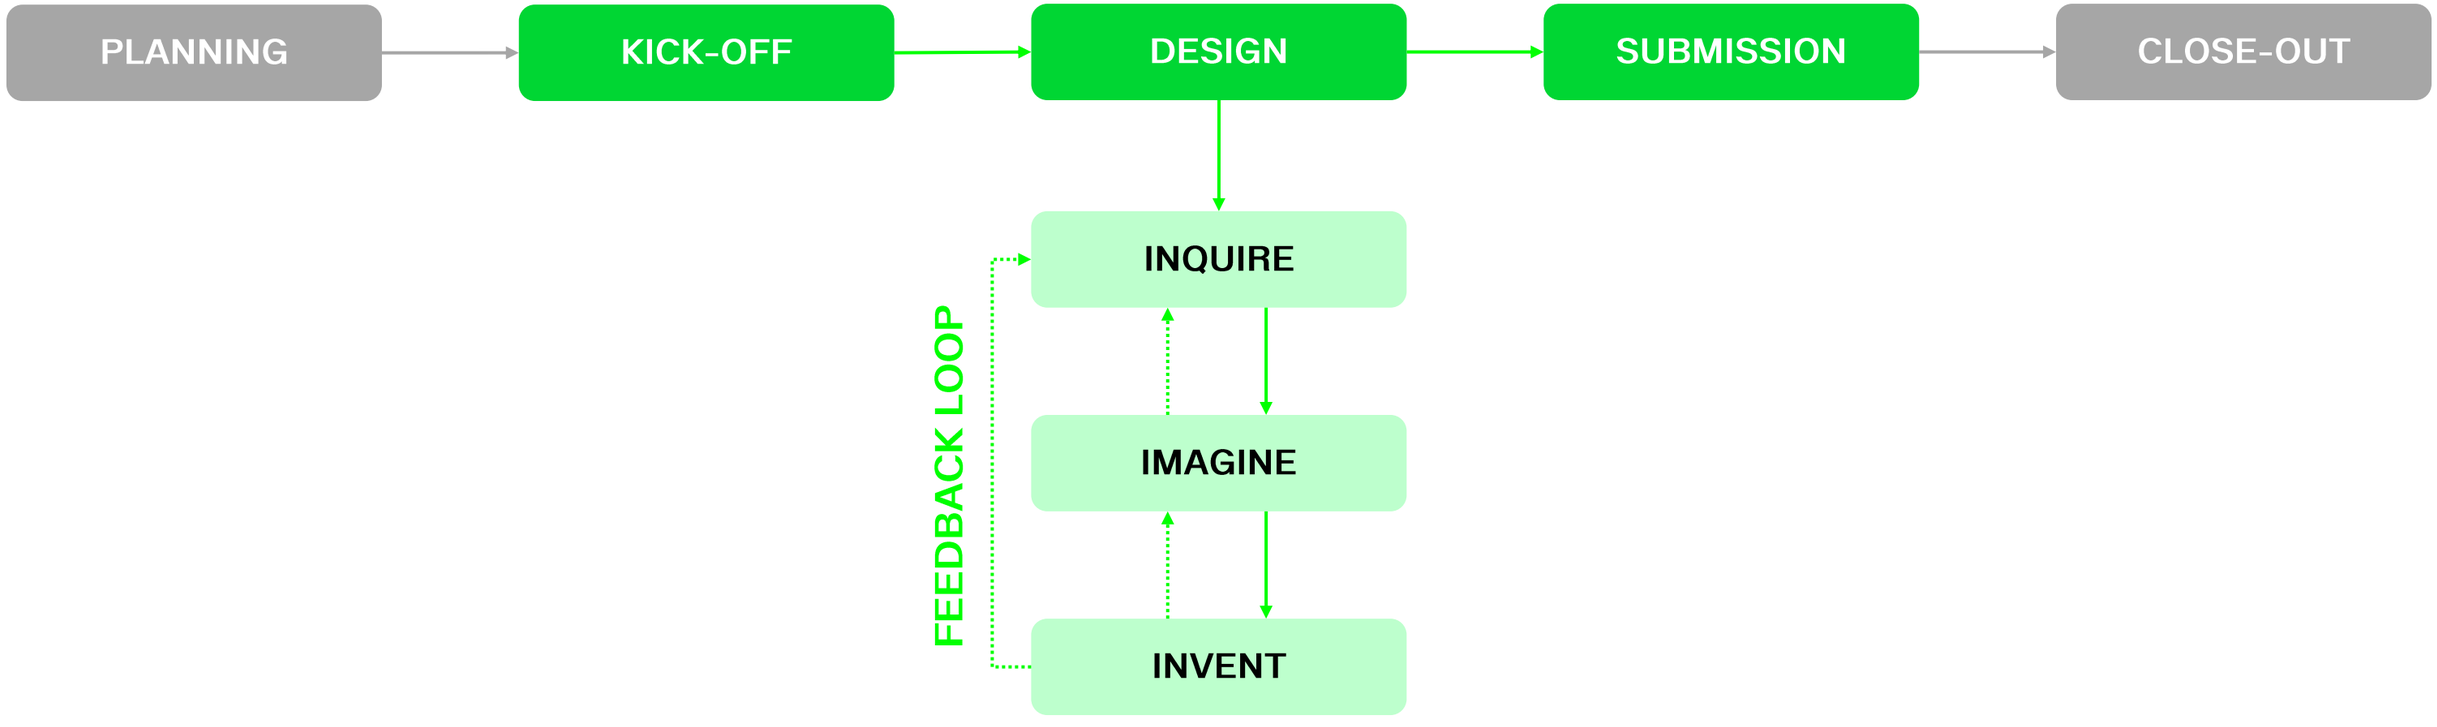

3.3.1 INTERNAL KICK-OFF

HOW DOES LAVA KICK-OFF PROJECTS ?

During the Mobilization period, a project does not start with the involvement of external parties until LAVA have defined the **Design Direction** for the Team.

It is required to organize an Internal Kick-Off meeting in which the Project Team presents **bottom-up information** and receive **top-down strategies** from Partner and/or Director. Following this, the Project Team may initiate engagement with other parties and start the execution.

	PARTNERS	DIRECTORS	PROJECT MANAGEMENT	PROJECT LEAD	PROJECT TEAM
1. Preparation for Internal Kick-Off	**Informed.** Given high-level briefing by Director on the project ahead of the internal Kick-Off.	**Accountable.** Schedule Internal Kick-Off meeting, prepare Agenda, and ensure Preparation by all responsible parties.	**Consulted.** Provide Project Planning documents to Project Lead and Director ahead of Internal Kick-off.	**Responsible.** Prepare a Presentation with summary of project information, initial ideas, site analysis, research and benchmarks, etc.	**Consulted.** Support Project Lead with preparation of Internal Kick-Off Presentation if required.
			Presentation		
2. Internal Kick-Off	**Consulted.** Communicate to Project Team what the initial thoughts, inquiries and ambitions are towards the Project.	**Accountable.** Ensure that Project Team has received briefing on LAVA motivation, applicable Themes and strategic framing before Project starts.	**Informed.** Provided briefing during meeting or afterwards regarding inquiry, design direction to study, LAVA Themes, strategic framing, etc.	**Responsible.** Conduct presentation and take note of any feedback received from Project Leadership on design direction and strategy to start the project.	**Informed.** Provided briefing during meeting or afterwards regarding inquiry, design direction to study, LAVA Themes, strategic framing, etc.
			Briefing & Design Direction		
3. External Kick-Off	**Informed.** Project Lead and PM to align scheduling of Kick-Off meetings with Partner(s) availability if possible.	**Informed.** Project Lead and PM to align scheduling of Kick-Off meetings with Director availability if possible.	**Accountable.** Ensure Project Lead has necessary Planning information to organize external Kick-Off meetings.	**Responsible.** Organize and schedule initial Kick-Off meeting(s) between LAVA, Sub-Consultants, Client and/or other Stakeholders.	
			Planning Documents		

3.3.1 INTERNAL KICK-OFF

LAVA THEMES & STRATEGIES

Our previous and future work is strategically framed through the lens of 8 key themes. When starting a project, it is important to determine the following :

- **Which LAVA Themes** relate the project and how ? Multiple themes can be applicable.
- **What is the envisioned lab approach ?** What are the tools and workflows we would like to explore and use ?
- **Which previous LAVA projects** can be studied and benchmarked ? Are there any precedents or approaches which we have learned from in the past ?

As the Project Team execute the work, Project Leadership controls that the above is integrated in the design.



Architecture driven by technology, data, and AI revolutionizes both design and production.	Reimagining healthy and intelligent urban landscapes.	Private environments that supercharge health, happiness, comfort, and well-being through design.	Holistic, architectural ecosystems that replenish and enhance the earth beyond sustainability.	When explorative ideas animate architectural concepts, imaginations become agents of innovation.	When typologies and functions fuse, architecture forms multifaceted spaces beyond mix-use.	Creative energy thrives in connections and collaboration at the workplace of the future.	Public spaces and buildings designed for dynamic interactions and close-knit communities.
Digital Workflows	**Urban**	**Private**	**Sustainability**	**Experimental**	**Mixed-use**	**Workspace**	**Public Spaces**
• Technology • Data • AI • Digital Fabrication • etc.	• Healthy • Intelligent • Urban • Landscapes	• Private • Living • Health • Comfort • Well-being	• Ecosystems • Holistic • Sustainable • Earth	• Explorative • Conceptual • Imaginative	• Typologies & Functions fuse • Multifaceted • Multifunctional	• Collaborations • Workspace • Connectivity	• Public • Interactions • Dynamic • Communities


3.3.2 TASKS & ACTIVITIES

FROM PLANNING TO **IMPLEMENTING** TASKS & ACTIVITIES

During Execution, the Team must implement Project Planning in detail :

- Subdivide the scope into **smaller manageable parts** (e.g. Façade, Structure, Program Distribution)
- **Define and sequence** the activities to achieve the parts – in what order should they be tackled?
- Identify **pre-requisites and interdependencies** between different disciplines and/or parts.
- **Prioritize critical paths** as the consecutive activities which take the longest time

The flowchart below is an example illustrating this methodology. Project Teams may decide on a **case-by-case basis** what the best approach is to clarifying the tasks and activities (e.g. using the Timeline, Kan Ban board, etc.)

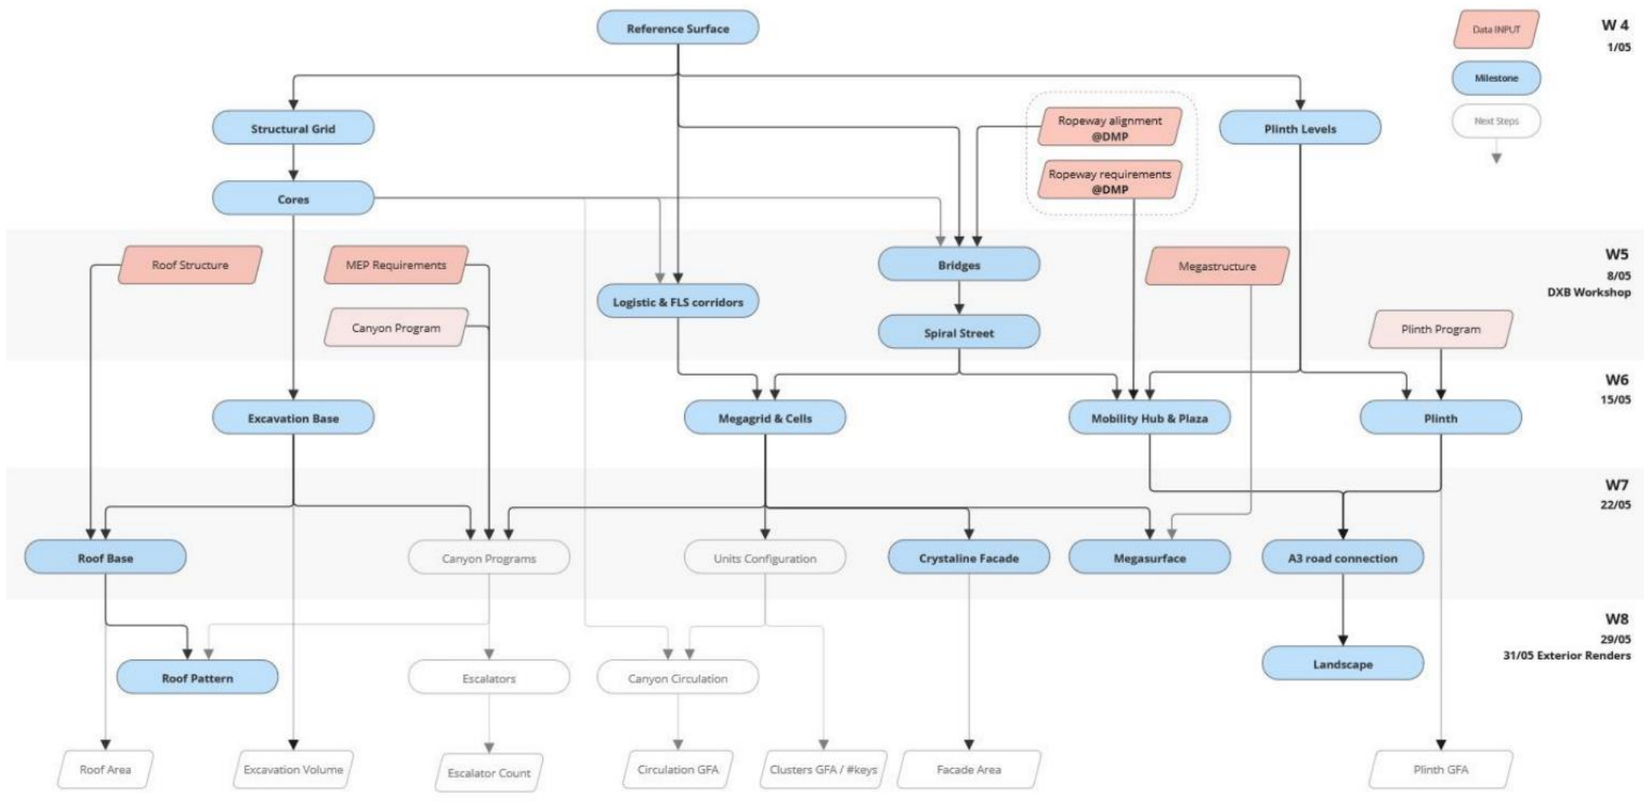

Critical Path diagram for Vault Value Engineering phase

3.3.3 DESIGN DIRECTION

HOW DO WE MANAGE DESIGN AT LAVA ?

INQUIRE


- Review the objectives and ask the right questions.
- Conduct bottom-up empirical analysis and review available data.
- Research precedents and relevant benchmarks.

IMAGINE

- Define a clear vision and guiding principles for the project.
- Develop strong diagrams that communicate the design intent.
- Test and evaluate alternative design options and variants.

INVENT

- Define a clear vision and guiding principles for the project.
- Develop strong diagrams that communicate the design intent.
- Test and evaluate alternative design options and variants.

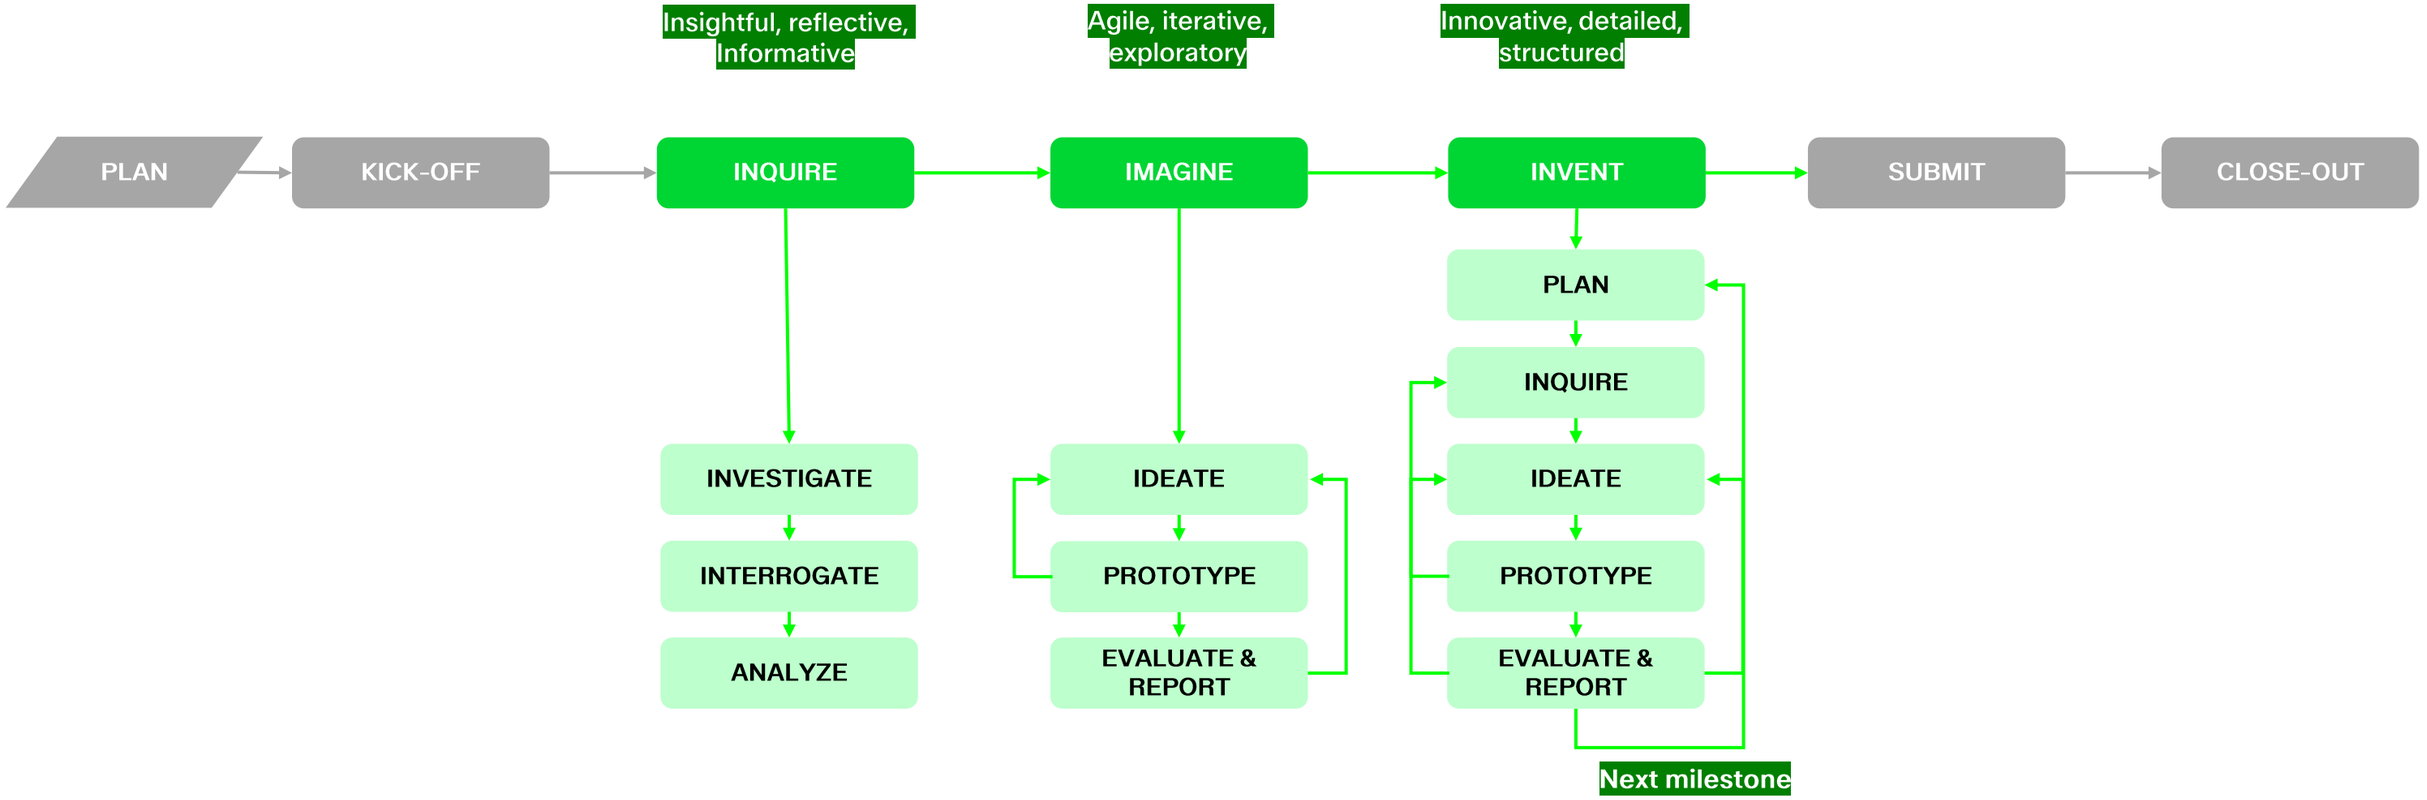

3.3.3 DESIGN DIRECTION

INQUIRE ROADMAP

Inquire :to investigate; look into

Project Management controls that the Project Team conduct project activities and tasks such as :

- Collect and analyse data, identify gaps, define assumptions if needed to proceed as per scope and time requirements;
- Ask the right questions based on LAVA motivation and strategic framing;
- Define project objectives, requirements, opportunities and constraints.
- Research precedents, identify potential tools and techniques which support initial ideation.

From Client

PROJECT DATA

From LAVA

DESIGN DIRECTION

PLANNING & TEAM

COLLECT

1. **Project Information**
   1. Project SoW
   2. Baseline Data
   3. Previous Stage (when applicable)
   4. Site Context
   5. Environment etc.
2. **Design Direction**
   1. Direction from Leadership
   2. LAVA Themes
   3. Client Guidelines, etc.
3. **Research**
   1. Topics, Technology, Emerging Trends
   2. Architecture & Built Environment
   3. Culture, etc.
4. **Compliance**
   1. Codes and Standards
   2. Specific Procedures
   3. Stage Requirements, etc.

REVIEW

1. Update Project Checklist
2. Confirm objectives
3. Identify opportunities, constraints, strengths/weaknesses, etc.
4. Flag & fill knowledge gaps

BENCHMARK

1. Relevant LAVA Projects
2. External Precedents (scale / typology / theme / environment)
3. Examples of deliverables
4. Tools & Techniques

OUTPUT

1. Formulate the Vision
2. Define design parameters (quantitative and/or qualitative)
3. Elaborate tasks and activities
4. Identify paths for ideation
5. Assign responsibilities
6. Initiate design studies

IMAGINE


3.3.3 DESIGN DIRECTION

IMAGINE ROADMAP

Imagine :to form a mental image of (something not present)

Project Management controls that the Project Team conduct project activities and tasks such as :

- Design parameters form the framework for iterative methodologies centered on fast ideation, prototyping and optimization;
- Project Team identifies and utilizes a workflow which facilitates brainstorming, sketching, collaboration and feedback;
- Exploration of different options, testing alternatives and documenting the processes and outcomes;
- Close communication between internal LAVA Team and Leadership, with sub-consultant experts and with the client team;
- Decision-making via deadlines and presentations of illustrated concepts, options, evaluation and recommendations.

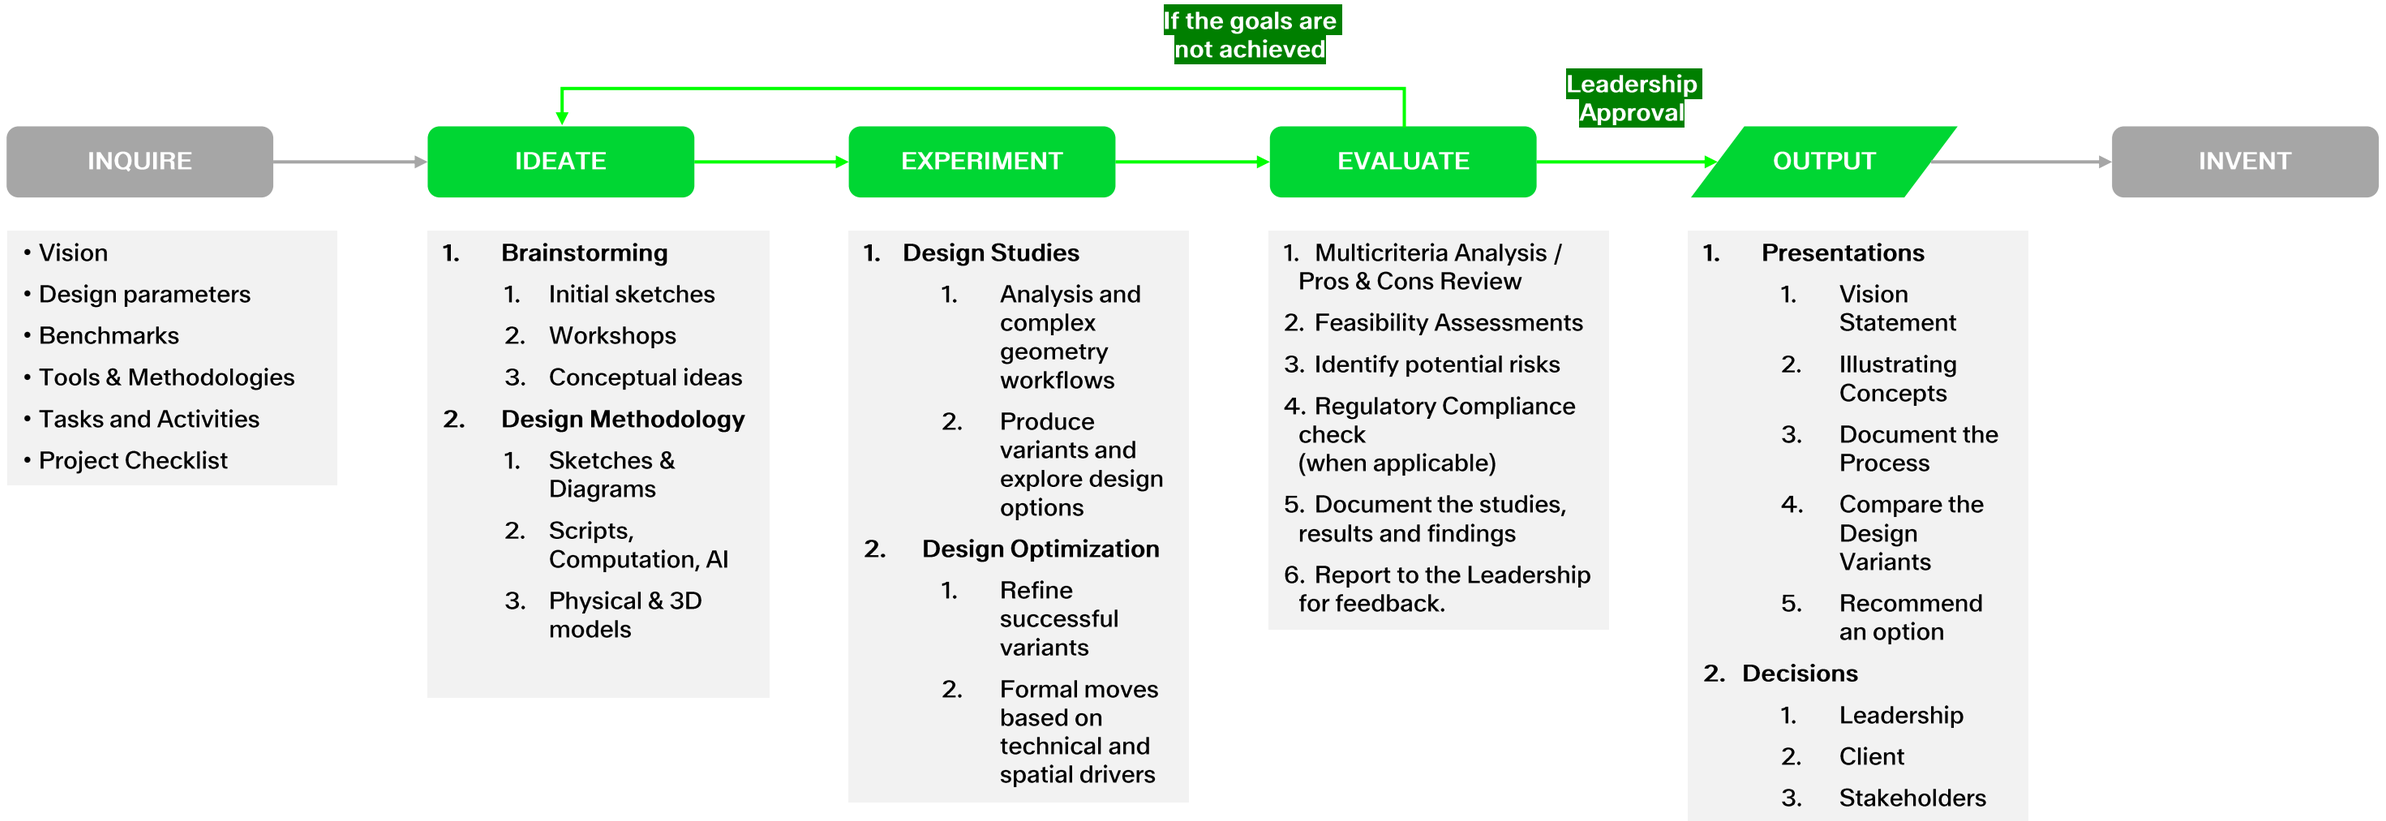

3.3.3 DESIGN DIRECTION

HOW CAN WE EVALUATE OPTIONS ?

To support **decision-making** and justify our proposals, it is important to document and compare the options which were produced as part of our design studies before making a recommendation. There are various ways this can be achieved, however it is always recommended to present **visuals and sketches** supported by an assessment of **how each option performs against the design criteria** (e.g. multicriteria analysis, pros and cons, etc.)

	THUMBNAIL 01 OPTION	THUMBNAIL 02 OPTION	THUMBNAIL 03 OPTION
	Option Description	Option Description	Option Description
CRITERIA 1	Simple explanation of the option's performance	Simple explanation of the option's performance	Simple explanation of the option's performance
CRITERIA 2	Simple explanation of the option's performance	Simple explanation of the option's performance	Simple explanation of the option's performance
CRITERIA 3	Simple explanation of the option's performance	Simple explanation of the option's performance	Simple explanation of the option's performance
CRITERIA 4	Simple explanation of the option's performance	Simple explanation of the option's performance	Simple explanation of the option's performance
		RECOMMENDED	

EXAMPLE : MULTICRITERIA ANALYSIS


3.3.3 DESIGN DIRECTION

INVENT ROADMAP

Invent :to produce (something, such as a useful device or process) for the first time through the use of the imagination or of ingenious thinking and experiment

Project Management controls that the Project Team conduct project activities and tasks such as :

- Tasks and Activities are defined according to milestones, and Planning is monitored and updated against team's progress;
- Innovative solutions are applied to resolve macro and micro issues and maximize the performance and efficiency of design;
- Comments and feedback from Client and LAVA Leadership is continuously considered and implemented;
- Production of all deliverables in accordance to not only LAVA's vision, but also to the scope requirements.

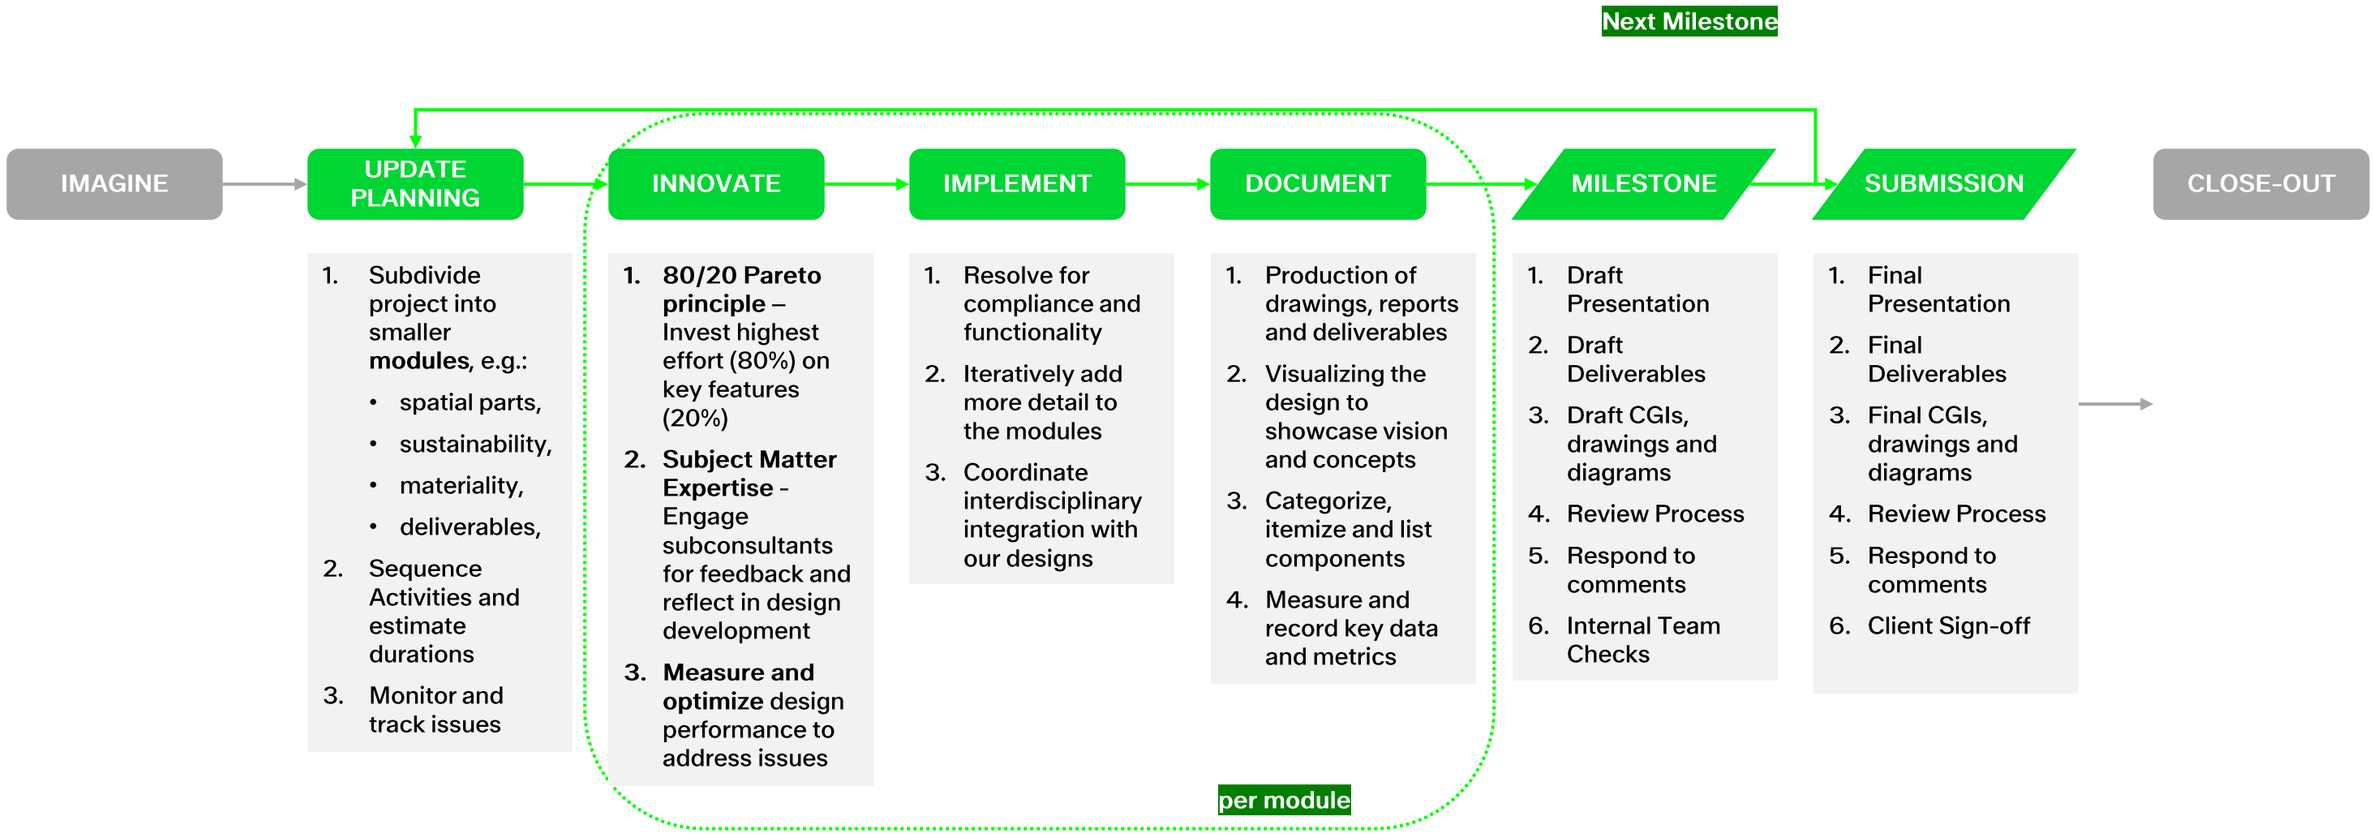

3.3.4 COORDINATION

HOW DO WE COMMUNICATE AND COLLABORATE IN PROJECTS ?

Communications must be tailored to suit the intended audience and anticipated purpose. When in doubt, Project Leadership can determine the most suitable form of communication based on the scope, project planning and specific circumstances :

- **Informal vs. Formal –** Internal coordination is light and agile, while external exchanges might need to be recorded in detail.
- **Cadence and Style –** While Internal Team reports can be transparent and flag issues for resolution, external stakeholder reports must show clarity and demonstrate confidence in LAVA. Weekly reports can be detailed, bi-weekly or milestone reports must be more overarching instead.

TEAM COLLABORATION

1. **Internal LAVA Stand-Ups**
    1. Weekly in-person / online meeting
    2. Distribution of tasks and activities
    3. Project Planning updates
    4. Q&A, resolution of issues
2. **Design Team Meetings (DTMs)**
    1. Weekly online meeting
    2. Deliverables progress
    3. Interdisciplinary alignment
    4. Q&A, resolution of issues
3. **Ad-Hoc Coordination**
    1. Daily and ongoing / via Digital Collaboration platforms
    2. Interactive and bottom-up initiative by Project Team
    3. Project Leadership supports with guidance as required

REGULAR REPORTING

1. **Regular Client Reports**
    1. Cadence as per contract (i.e. Weekly, Biweekly or Monthly)
    2. Project Dashboard, Lookback & Lookahead
    3. Demonstrate adherence to timeline and scope
    4. Build consensus on design decisions and enable decision making by client team
    5. Receive feedback, address comments and facilitate approvals
2. **Bi-Weekly Internal LAVA Reports**
    1. Project Dashboard, Lookback & Lookahead
    2. High-level progress summary to Partners and Directors
    3. Design direction and studies, analysis, options assessments and recommendation
    4. Flag project risks and open issues requiring senior leadership awareness

STAKEHOLDER MEETINGS

1. **Authorities & Key Stakeholder Engagement**
    1. Agenda drafted and shared before the meeting
    2. Slide Deck demonstrating how LAVA understands and addresses stakeholder requirements
    3. MoMs recorded and shared after the meeting
    4. Receive feedback, address comments and facilitate approvals
2. **3rd Parties Coordination**
    1. Agenda drafted and shared before the meeting
    2. Slide deck addressing agenda (optional – as required)
    3. Scope responsibilities and timeline constraints of all parties are noted
    4. Baseline information is noted (e.g. Highlight data gaps and assumptions if necessary)
    5. Actionable items, responsibilities and dates assigned in MoMs

COMMUNICATION CHANNELS

1. **Cloud / Repository**
    1. Push / Pull access to dedicated project folders via Digital Collaboration platforms
    2. Access to working documents for Project Team
    3. Access to draft or final deliverables for Client Team
2. **Formal Communication**
    1. Via e-mail or Project Delivery Platform if applicable
    2. Deliverables at Milestones
    3. Technical Letter (LAVA Letterhead) signed by Project Leadership
    4. Client Instructions (e.g. Variation Notice)
3. **Informal Communication**
    1. Via e-mail or chats / phone
    2. Preferably limited to ad-hoc communications with team.
    3. Take note and report to Project Leadership. Request formal communications from client.

3.3.5 REPORTING

HOW DO WE REPORT OUR PROGRESS AND SERVICES ?

INTERNAL ⟷ EXTERNAL

	LAVA LEADERSHIP	LAVA CONSULTANTS	STAKEHOLDERS	CLIENT
PARTY ENGAGED	Partners, Directors	Subject Matter Experts, Discipline Leads	Authorities, Key Stakeholders, 3rd Parties	Client Representative Team
REGULARITY	Bi-Weekly	Weekly Ad-Hoc / As Required	Schedule Milestones Ad-Hoc / As Required	Weekly / Monthly (as per scope)
GOAL	• Design Direction • Progress overview • Facilitate decision-making • Issues escalation	• Interdisciplinary coordination • Focused updates • Schedule / Responsibility Alignment • Quality Control	• Present LAVA design • Seek pre-Approvals / Approvals or alignment • Clarify Baseline information, fill data gaps and/or agree on assumptions	• Scope/timeline adherence • Progress overview • Achievement-driven • Facilitate decision-making • Address feedback
SPECIAL CONTENT	• Project Dashboard • Vision Statement • Design parameters • Project Methodology • Design Sketches and evaluation • Decision Pages	• Vision Statement • Design parameters • Issues Tracker • Project Checklist, Data Gaps & Assumptions • Risk Management	• Vision Statement • Approvals Roadmap • Project Checklist, Data Gaps & Assumptions • Content depending on Stakeholder focus	• Project Dashboard • Lookback / Lookahead • Design Sketches and evaluation • Decision Pages


3.3.5 REPORTING

HOW DO WE REPORT OUR PROGRESS AND SERVICES ?


* Optional pages




01 | Cover




02 | ToC

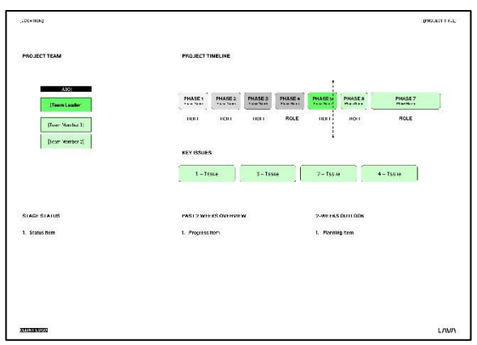


03 | Dashboard

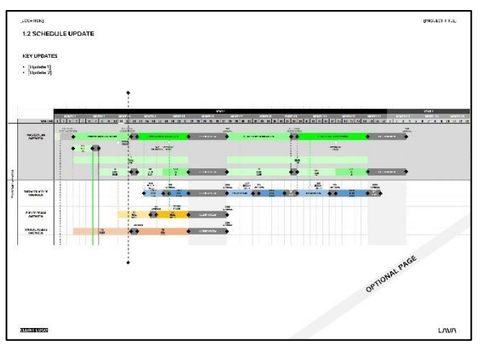


04 | Schedule Update*



05 | Chapter Page & ToC




06 | Items Thumbnails*

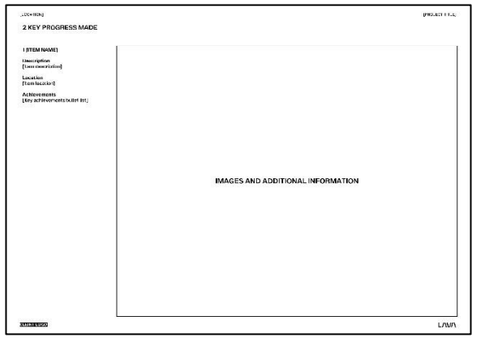


05 | Item Page



06 | Decision Page*




06 | Chapter Page*



07 | Optional Content*

(e.g. 4-weeks overlook, risks, logs, etc.)



09 | Previous Reports Links*



10 | Back Cover

3.3.5 REPORTING


PERIODIC REPORT: DASHBOARD

Dashboard can be adapted for different recipients:

- **LAVA Leadership |** comprehensive and realistic overview of the project progress.
- **Consultants |** focused overview of the relevant matters only.
- **Client |** comprehensive overview; focused on **positive framing and achievement-oriented communications**

CONTENT

1. **Project Team –** fill with key personnel.
2. **Project Timeline –** timeline editable on Slide Master. Adjust based on applicable procedures (e.g. HOAI, RIBA)
3. **Key Issues –** optional if any critical issues present.
4. **Stage Status –**big milestone achieved / upcoming.
5. **Past 2 Weeks Overview –** summarize key achievements.
6. **2-Weeks Outlook –** summarize key planned items.

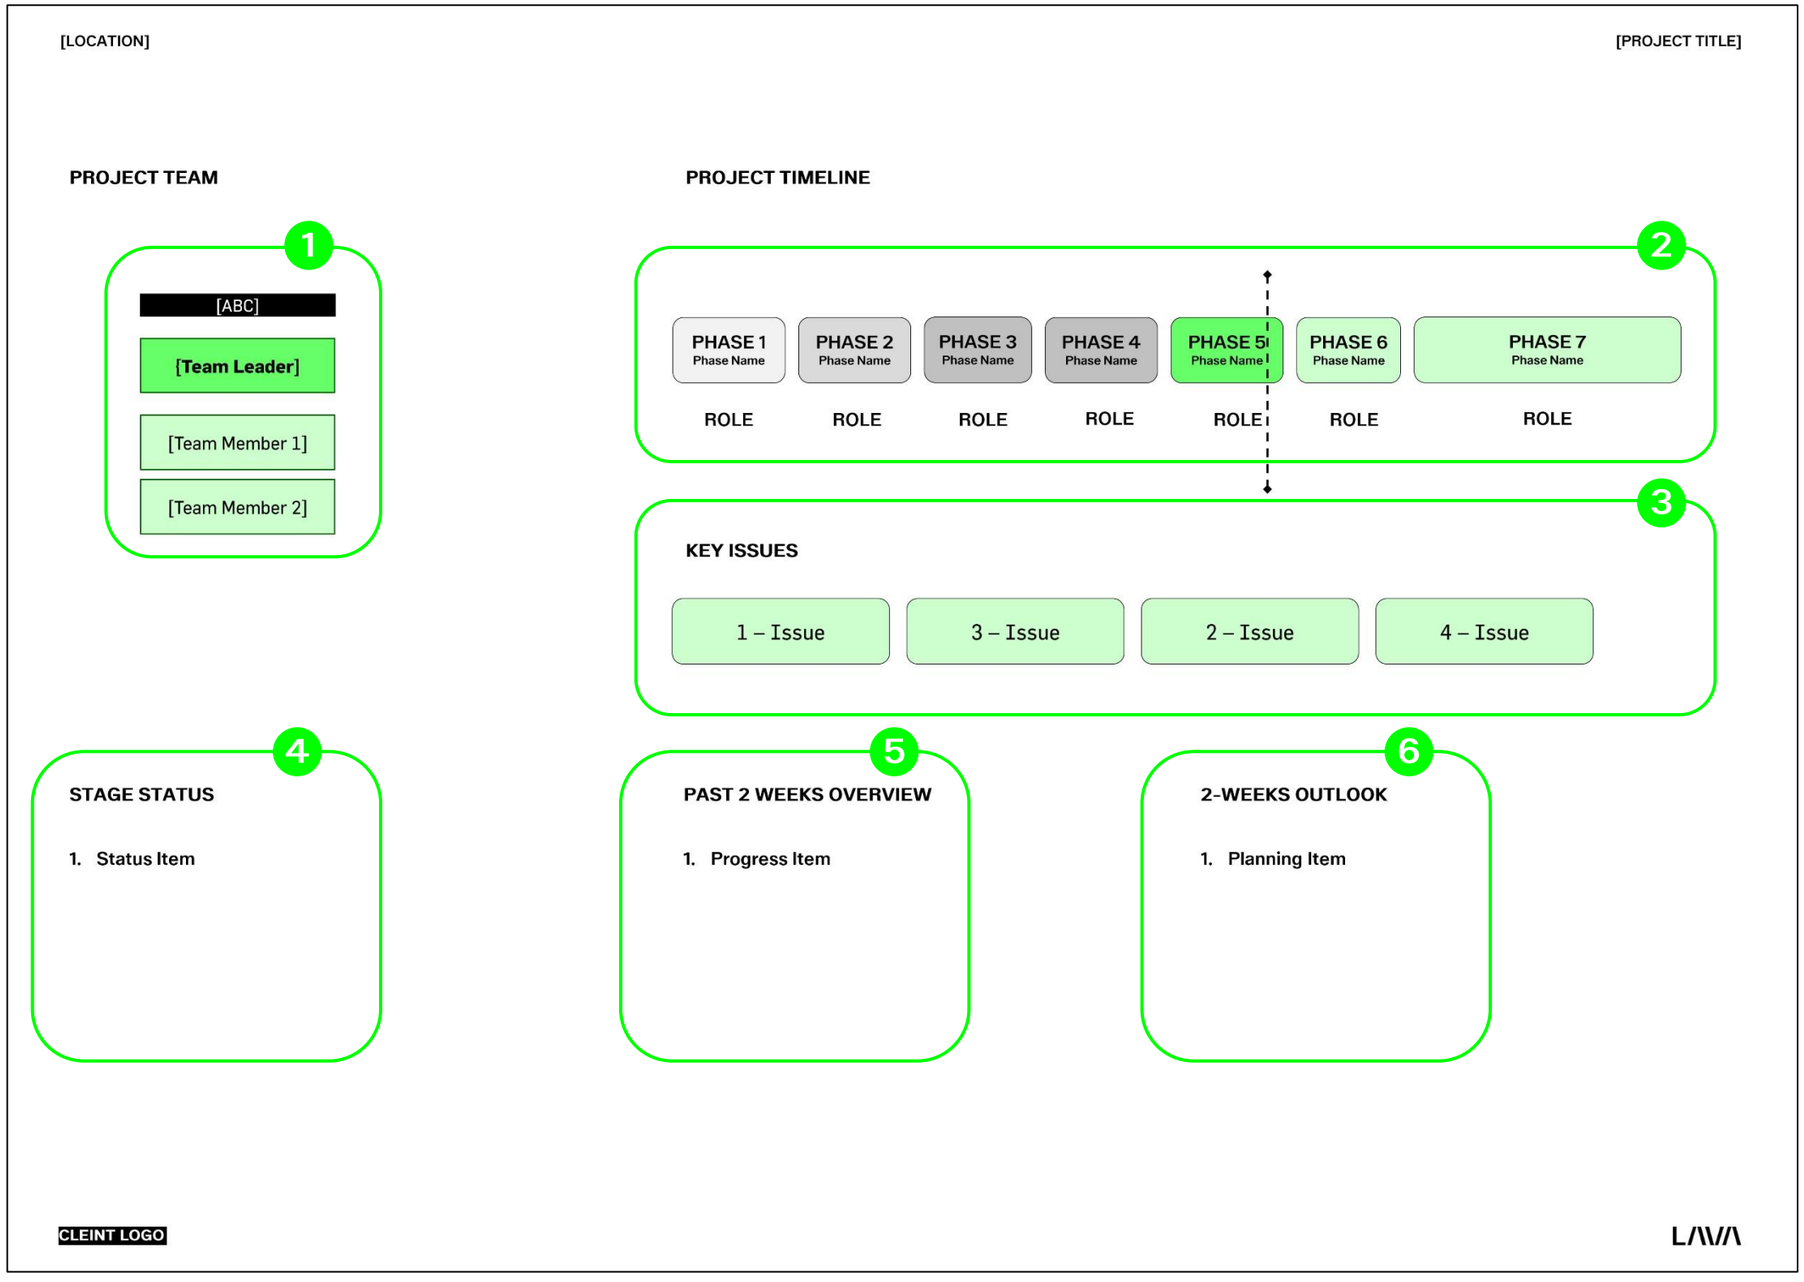

3.3.5 REPORTING

WHICH FORMAT TO CHOOSE FOR REPORTING ?

POWERPOINT OR INDESIGN

This table helps guide whether you should be creating a document in PowerPoint or Indesign

Factors	PowerPoint	Indesign
Document Function	- Client facing presentations that require client to be able to update document - Collaborative documents - Kick-off meetings - Video presentations/Mixed media - Internal work	- Internally controlled documents that will not require client functionality - Detailed longer documents - Printed books, reports, submissions - Multiple chapters/repetitively structured documents
Document Length	- Shorter documents (approx. 30 pages) - One-off documents	- Mid to Longer Documents (30 pages+) - Multiple versions of similar document (i.e. ULM reports with different sites but same layout)
Medium (How is presentation viewed)	- Interactive web-based presentations - Screen presentations	- Printed presentations - Read document
Graphics	- Less high-fidelity graphics - Simpler graphics - Less precision, more big-picture	- Multiple high-fidelity images - More graphics functionality - More precision
User Interface	- Easy to use - Very imprecise, hard to make things neat - Less time to setup a document - Easier to teach team how to use correctly - Less options - Does not interface with Adobe programs - Good for videos and buttons	- More complex but more control - Precise, can set up guides to keep things neat - Needs time to setup a document correctly - Needs time to teach team how to use correctly - More customisable and advanced options - Interfaces with Adobe programs - Not so good for video and buttons
Collaboration	- Can have multiple people working on same document at once - No live link for images	- Only can have one user in a document at a time - Live link updates for images

3.3.5 REPORTING

HOW TO BEST USE POWERPOINT ON SHAREPOINT?

Factors	DOs	DON'T's
Master Slides	- Take time to setup your Master Slides because they will define how neat your document is. - Use as few Master Slides as possible so other team members are not confused about which layout to use.	- When in Normal View, do not delete or move around editable elements from the Master Slides because when the layout is updated, things will not be in the right place.
Text and Spelling	- Try to maintain one font through the document (usually Flama or Brown) and a readable font size. - Make sure the correct language is used. - Use CTRL+F to find words that have been spelled wrong and use REPLACE ALL to change all these instances to the correct spelling.	- Use lots of different fonts and font sizes that jump around from page to page - Use too much text, PowerPoint is more for visuals and clarity. If you have lots of text, consider using Indesign.
Drawing in PowerPoint	- If you have to draw in PPT, minimise the drawn elements to annotations, arrows, maybe a path but not anything that needs to be accurate/look nice.	- Don't do it as default. It is imprecise and a pain.
Icons and Images	- PPT has built in stock images and icon library which is sometimes good enough so will save you time. - Compress images if they are super heavy and just need to be viewed on screen. This will make the file lighter	- Drop lots of massive images into presentation, it will slow it down.
Saving Files	- Check things are saving at the status bar at the top, if unsure save a backup. - Regularly check with team members that changes you are making are being seen by them.	- Work in the teams browser version because sometimes the saves don't work and things get lost. - Save offline all the time and forget to upload changes. - Close the document before it has finished saving.
Copy Paste, Lock, Arrange	- PPT has a quirk that sometimes things can not paste in place exactly on top of things that are already there so you need to check your copy paste placement from slide to slide. - Use GROUPS so things can be copied together. - With Microsoft apps (e.g. Excel), usually can livelink copy paste so if it is changed in the other app, it can automatically update. - LOCK certain content so it does not move on the page - ARRANGE can BRING FORWARD or SEND TO BACK	- Copy paste Slide Master elements, these should be untouched so they remain consistent.

3.3.5 REPORTING

HOW TO BEST USE INDESIGN ?

Factors	DOs	DON'T's
Master Pages	- Take time to setup your Master Pages because they will define how neat your document is. - Use as few Master Pages as possible so other team members are not confused about which layout to use.	- Put loads of elements in the Master Page that will need to become editable as you will then spend a lot of time unlocking things etc. Master Page should contain permanent elements that do not change, a couple placeholder textboxes and frames and the guides
Paragraph Styles & Character Styles	- Be strict with Paragraph Styles and if you are making multiple changes, make a new style. - Turn off hyphenate	- Do not use one style and change text from page to page as when you update the style, it will change ALL the text to one style so your customisations will disappear
Drawing in Indesign	- Try to keep all drawing on a Diagram Layer so it is separate from text and images (as drawing should always be on top of images anyway) - Use the eyedropper tool to quickly get similar linestyles/fill and stroke colour	- Do complicated drawing in Indesign that you an do in Illustrator as you can also just link Illustrator files into the presentation so they update
Links and Images	- Make sure everything is linked - Use the speedier preview mode when working in the document and use SHIFT+W to go into presentation mode if you want to see what it will export as	- Have messy links, keep all your links in a folder if possible so that you will not move them around by accident and break all the links in the document
Saving Files	- Save when you make changes and have clear communication with the team member managing the Indesign file so they can collate changes and upload to Teams	- Work in different versions of Indesign as team members as they will not be able to open the work if someone works in an older version than someone else
Copy Paste, Lock, Arrange	- COPY+PASTE IN PLACE will copy things into the same location on each page, would recommend changing the keyboard shortcut as you will use this a lot - LOCK will ensure content does not move on the page, CTRL+L is the shortcut - You can BRING FORWARD or SEND TO BACK in Indesign but note, LAYERS supersede this, a higher layer can never have work sent beneath a lower layer	- Misalign things, Indesign is set up to be as neat as possible. If something is going wrong and things are not lining up, there is a problem in the Master Page or a team member's workflow

3.3.6 QUALITY CONTROL

HOW DOES LAVA DEFINE QUALITY IN A PROJECT?

Quality :the totality of features and characteristics of an entity that bear on its ability to satisfy stated or implied needs

The above is extracted from ISO 8402 – Quality Definitions. Additionally for reference, the PMI (Project Management Institute) more broadly states that quality is **“conformance to the Customer’s requirements”.** Finally, Quality is **design-driven** at LAVA, and is achieved by ensuring the Project Team follows the processes which are laid out to support Inquiry, Imagination and Invention.

1. How well does the design fit into LAVA’s **goals and strategies** ?
2. Does the design progress LAVA’s exploration of its key **Themes** ?
3. Are the project **Objectives** identified and does the design respond to them ?
4. Does the design address the Client’s **stated and implied needs** ?
5. Are we complying with any relevant **regulations, codes, standards and guidelines?**
6. Is the project on track with **time, scope and cost constraints** ?
7. Have we explored **design optimization** ?

etc..


3.3.6 QUALITY CONTROL

QUALITY CONTROL DURING THE PROJECT

Quality Assurance & Control during the Project is achieved through:

- Guides and manuals
- Team training
- Regular reviews by LAVA Leadership (internal bi-weekly reports)
- Milestone documentation review
- Milestone processes review
- Internal Audits
- External Audits

For further information on QC see **LAVA 2.5 Quality Manual.**

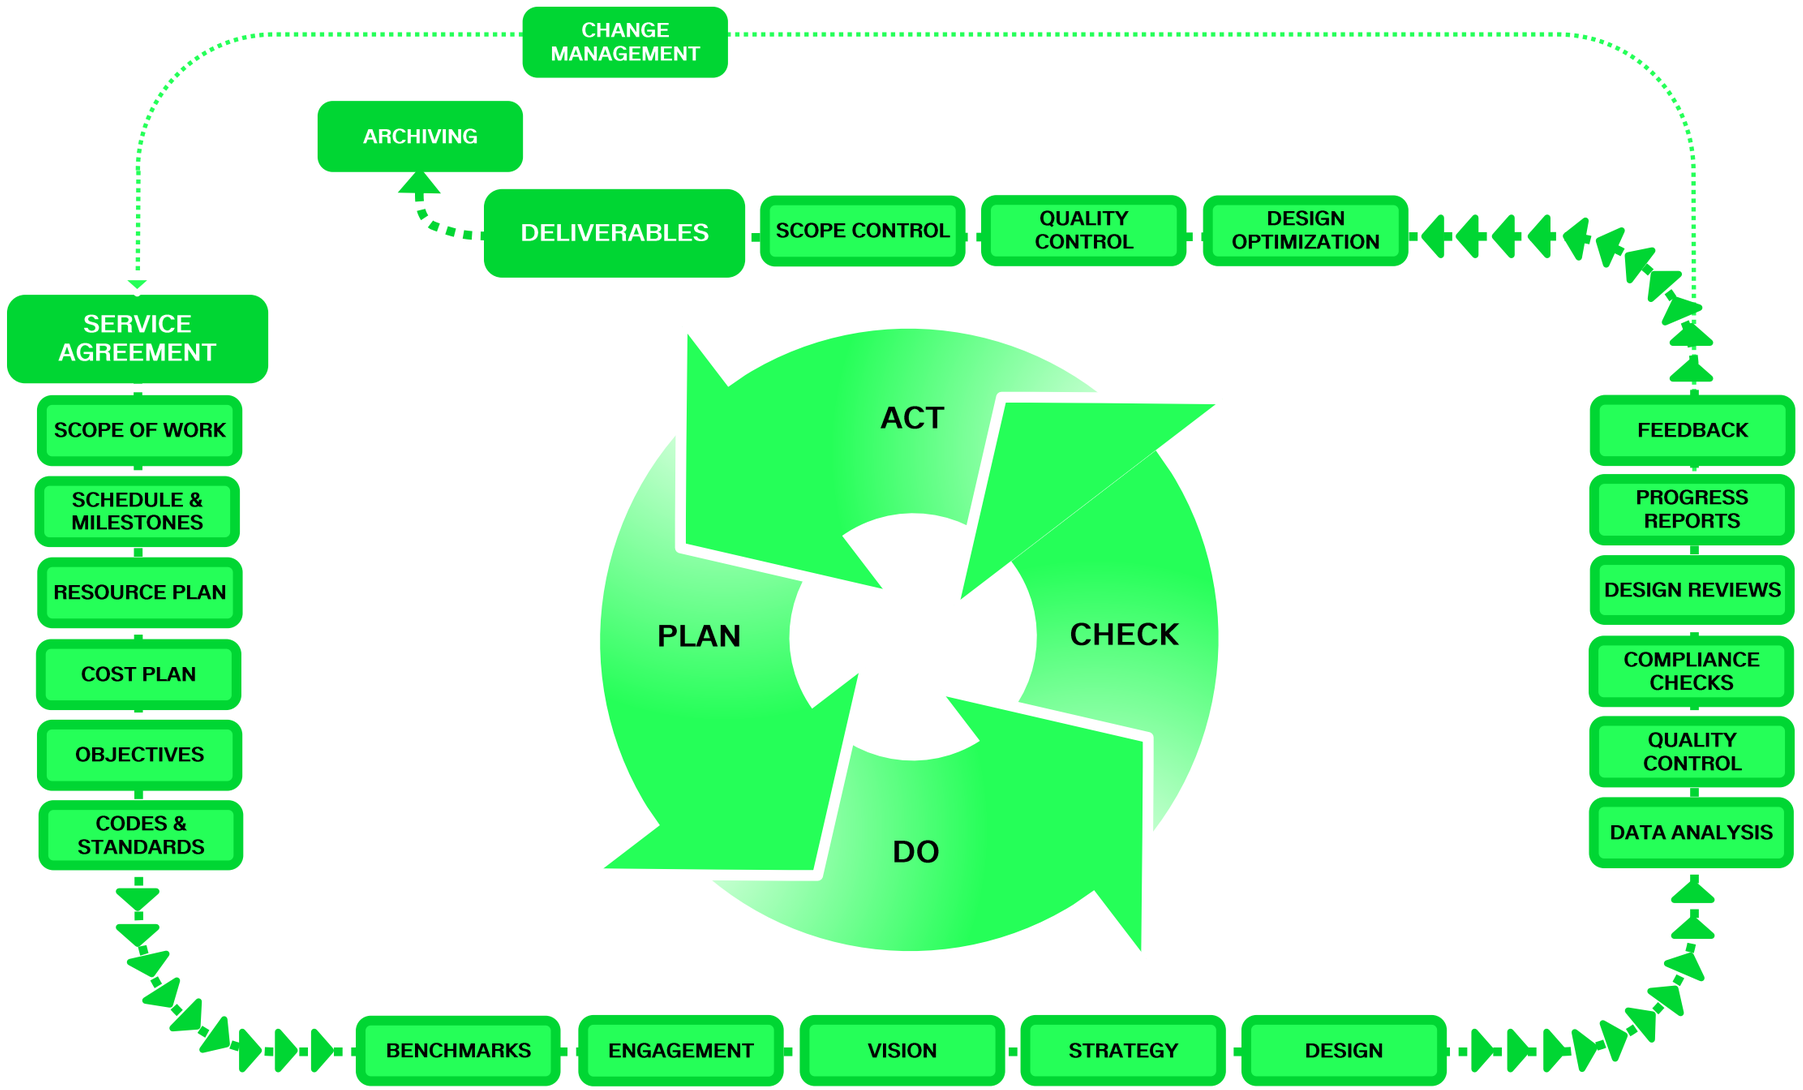



3.3.6 QUALITY CONTROL

QUALITY CONTROL DURING THE PROJECT

Quality Audits happen regularly and in various forms as part of the Project Team responsibilities. The more often the work is **inspected**, the more **preventative and corrective actions** are taken to ensure our **design is optimized** and our **deliverables are free of errors**. The following is a summary of the different ways quality must be checked during the Project :

- **Processes Checklist** – As part of the Project Checklist template, a list of steps to be verified for implementation at each phase of the Project starting from Bidding and ending in its closeout. This can be implemented at any moment of the project.
- **Progress Reporting –** Provides opportunities for Clients to vocalize feedback, or their implied or emerging needs.
- **Bi-Weekly Reporting** – Provides an opportunity for Partners to steer the Design Direction accordingly.
- **Milestone Draft Reviews** – Project Leadership organize internal deadlines for the Team to prepare draft documentation.
- **External Review Buffers** – LAVA is responsible for the works of sub-consultants. Therefore it is required to ensure their work is issued in a timely manner to LAVA to facilitate at least one round of internal reviews and corrective actions.
- **Final Checks** – Scope Validation by Project Management, and conformance checks by Project Leadership, to ensure that Projects can be formally closed out with full confidence that requirements are met.

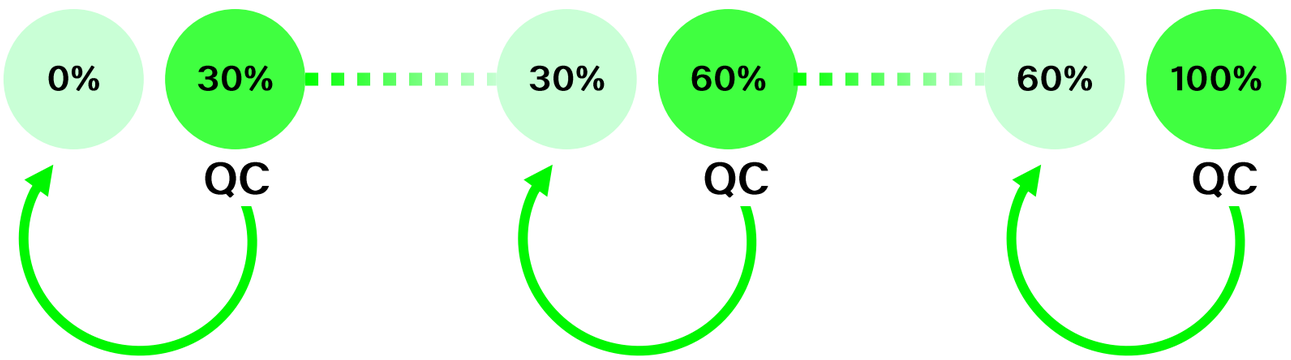

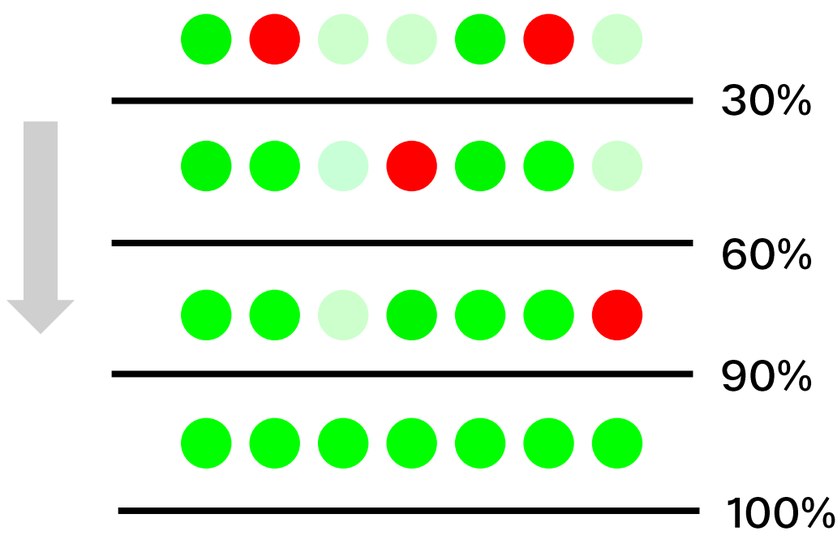

3.3.6 QUALITY CONTROL

QUALITY CONTROL DURING THE PROJECT

The need for **Prevention, Corrective Actions, and Design Optimization measures** will emerge during the Project. It might be equally noted by the Client, by our Senior Leadership, or by members of the Project Team. All of these can be considered as **Issues** which are logged and tracker by the team accordingly, to ensure we maintain a record of what must be done and can communicate over how it can be addressed accordingly.


Priority can be adjusted using a drop-down list ranging from Low to High

Background Information on the particular issue can be logged (Category, Location, Item, Description)

Images can be inserted into the table to visually track the issues, while **Reference** can point to a particular document

Action, Action By and Due Date can track how and when the issue can be resolved

Status can be adjusted using a drop-down list depending on completion or level of progress

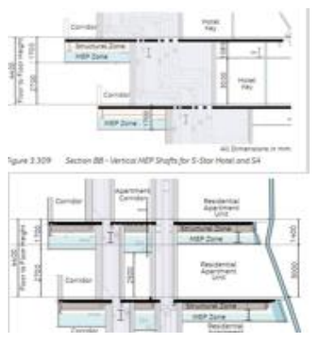Nr	Priority	Category / Topic	Location	Item	Description	Image	Reference	Date added	Proposed Action	Action by	Due Date	Status
2	High	ARCH	Location in the project	Bridge Geometry	Bridge geometry to be adjusted to the updated structures		Document to reference	01.02.25	Action plan 1	LAVA	02.03.25	Todo
3	Low	ARCH								MDC		In Progress
4	Low	ARCH								Consultant 1		In Progress
5	High	FAC								Consultant 2		Complete
6	Medium	STR	Location in the project							Consultant 1		On Hold
7		STR										
8												

04


AFTER THE PROJECT

4 AFTER THE PROJECT


WHAT TAKES PLACE AFTER THE PROJECT ?

After passing the end date of a Project or a particular stage of the Project, certain processes must be fulfilled before a Project Team can be demobilized and the Project officially ends :


1. **Archiving** – All Project documents must be properly stored on the Server, including not only Milestone Deliverables, but also relevant editable files.
2. **Fact Sheet** – The key information which summarizes the project must be filled out in a template so that it is centralized and easily accessible in the future by anybody for any purposes.
3. **PR Content** – The images which represent the project in the best possible manner are to be selected and linked accordingly in a document. This may include not only the best visualizations, but also the most relevant architectural drawings and successful concept diagrams that illustrate the vision and methodologies.

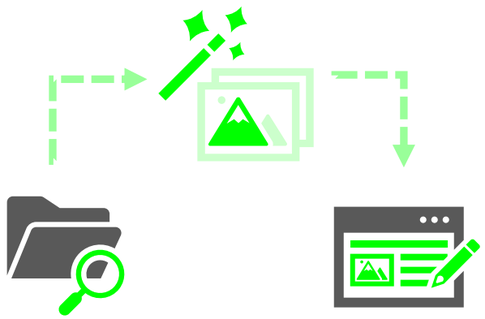

1. **Accessibility –**
Ensure all relevant files are correctly stored, can be easily found, edited and used in the future

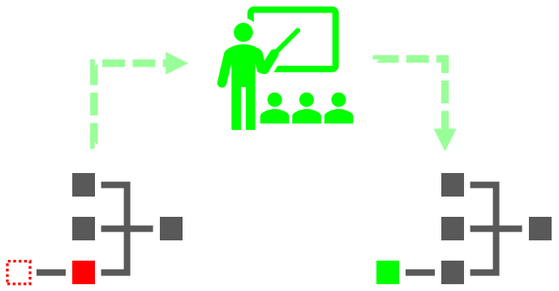

2. **Lessons Learned –**
Debrief, reflections and reviews to evaluate what worked well and what to improve next time



3. **Closing Out the Project –**
The Project is not finished until all processes are completed

4 AFTER THE PROJECT


WHO IS RESPONSIBLE FOR WHAT AFTER THE PROJECT ?

	PARTNERS	DIRECTORS	PR & ACQUISITIONS	PROJECT MANAGEMENT	IT & TECHNICAL SUPPORT	PROJECT LEAD
1. Archiving		**Informed.** Given confirmation when project is fully archived on the server.		**Consulted.** Control and confirm to Director that Project Team has completed the process.		**Responsible.** Ensure all Project files are stored on the server according to standard folder structure.
		Confirmation of completion				
2. PR Content & Fact Sheet	**Consulted.** Review the selection of images and Fact Sheet. Approve before usage in PR Content (e.g. Portfolio, Website, etc.)	**Accountable.** Ensure that the use of PR content and Fact Sheet is accurate, compliant with NDAs, LAVA motivation & Design ethos.	**Informed.** Given notice that a Project is cleared for use in PR functions, as well as access to Content & Fact Sheet upon approval.	**Consulted.** Control and confirm to Director that Project Team has completed the processes.		**Responsible.** Ensure PR Content & Fact Sheet templates are filled at end of project. Consult Director on choice of content.
	Seek Approval		Confirmation of completion			
3. Digital Collaboration		**Informed.** Given confirmation when Digital Collaboration platforms and tools are shut down for the project.		**Consulted.** Control and confirm to Director that Project Team has completed the processes.	**Responsible.** Ensure that Digital Collaboration platforms and tools are properly archived by Project Team before shutting down.	**Consulted.** Confirm to IT & Technical Support that Digital Collaboration platforms and tools no longer in use.
		Confirmation of completion				
4. Lessons Learned	**Consulted.** Provide top-down feedback to Director on project performance and design success.	**Responsible.** Gather feedback from Partners and Project Lead and conduct debriefs with respective parties as required.		**Informed.** Given feedback from Director and Project Lead. Recommend PM improvements to Director.		**Consulted.** Exchange insights and feedback with Director and Project Management.
	Feedback		Feedback		Feedback	

4.1.1. ARCHIVING

ARCHIVING AFTER THE PROJECT

Milestone Packages are submissions to the client as required per scope and must be clearly archived. In addition to formal deliverables, important editable files should be archived as well.

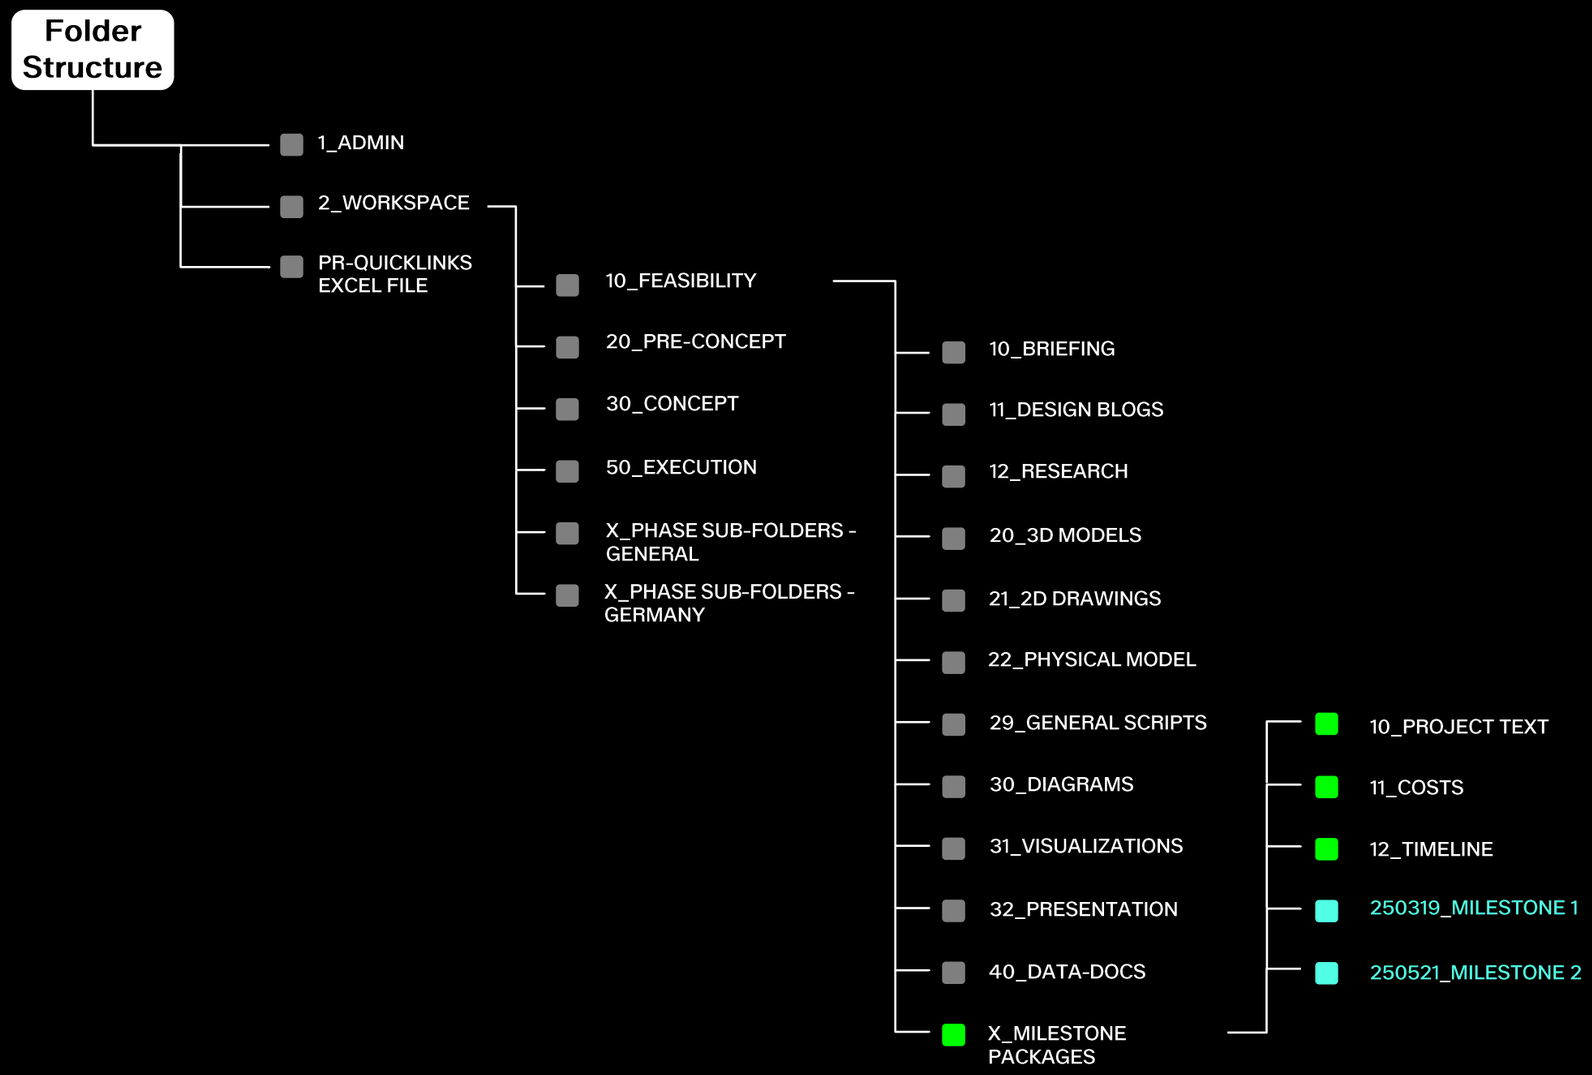


INCLUDE EDITABLE FILES (E.G. ILLUSTRATOR, POWERPOINT, ETC.) WITHIN THE FOLDER LINKS FOR DIAGRAMS, DRAWINGS AND VISUALIZATIONS. THIS ALLOWS FOR CUSTOMIZATION OF CONTENT FOR MARKETING PURPOSES.


4.1.2 PR CONTENT

DOCUMENTING PR CONTENT AFTER THE PROJECT

A selection of the most important Project Facts, Information and Graphics must be clearly referenced through links to the respective folder under the **Project Factsheet** or PR-Quicklinks Template. Content selected for each Project is intended to be featured on the Website and in the Portfolio.

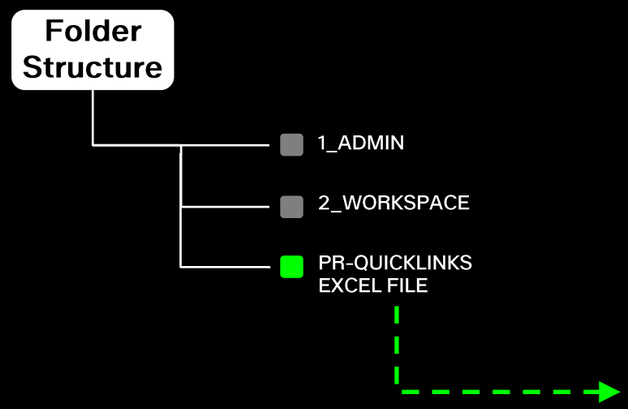

Content	Path
Project Info	P:\example path\example folder
Areas	P:\example path\example folder
Costs	P:\example path\example folder
Diagrams	P:\example path\example folder
Drawings	P:\example path\example folder
Visualization	P:\example path\example folder
Presentation	P:\example path\example folder
Photos	P:\example path\example folder
Exhibition	P:\example path\example folder

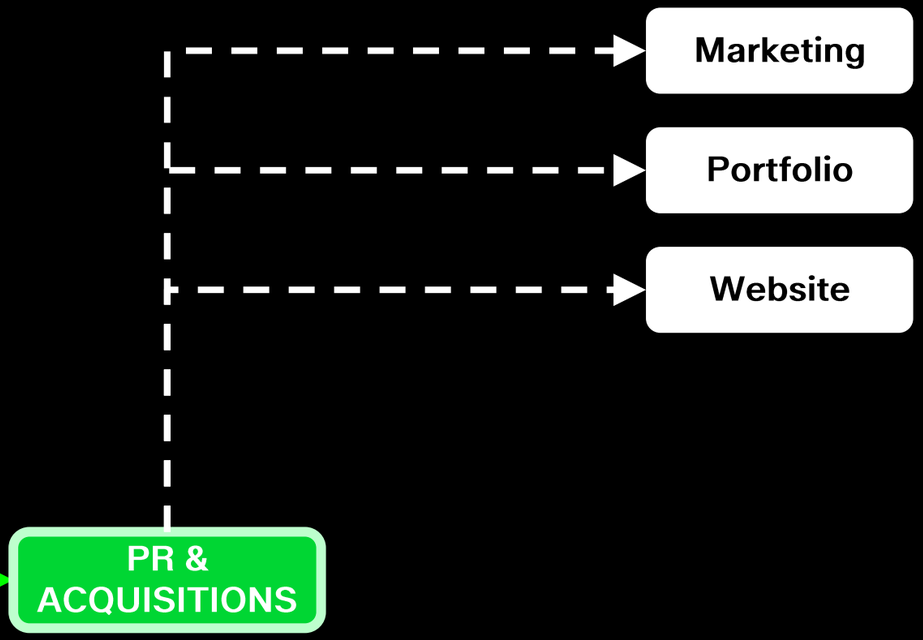

4.1.3 PROJECT FACT SHEET

WHAT IS THE PROJECT FACT SHEET?

The Project Fact Sheet contains all **key information and data** related to a Project, which can be used by LAVA at any point to summarize and communicate the most relevant points, particularly through **PR functions** (e.g. website, portfolio, marketing, etc.). It is recommended to start filling out the Fact Sheet **as soon as possible**, and **no later than once the Project is concluded.**

Name of Project	**Project name for publication**
Location	Location
Strategic Framing	
Headline for project text	Example text : The Energy Storage Tower replaces a gas tank, and will be a strong symbol of the transition towards renewable energy resources
Key words / topics from the project text	Example text : energy transition, infrastructure
How does this project relate to the overall themes ?	Example text : Project XXX relates to the theme XXX through its usage of...
What was the lab approach with this project ?	Example text : The lab approach of Project XXX was LAVA's ...
What is the design ethos ?	Example text : design ethos of Project XXX is ...
Project Description	Example text: LAVA was commissioned to supply the innovation for this project and address the social and practical roles of this new form of infrastructure. The result, a luminous otherworldly-looking tower with a diameter of 26m and a height of 56m, will be the tallest building in the area, and when finished aims to be the city's symbol of its sustainability commitments. Built in an industrial park on the site of a 1950s cylindrical gas tower, this new structure, although similar in design, is the antithesis of last century's extractive way of thinking. Instead of drawing energy from finite resources, the Energy and Future Storage center trailblazes into the future with a tank that stores water heated to 115 degrees by solar and wind energy that is then sold back to the grid. LAVA created an architecture and information beacon by "skinning" the existing structure and building a restaurant and exhibition space on top of it..

Project Information	
Type	Study / Competition / Project
Project Scope / Function	Masterplan / Office Building / School / Mixed-Use
LAVA Role	Architect / Lead / Consultant
Data	
Year	Year
Size	xxx m2
Status	Built, Under Construction, Under Development
Planning / timeline	
Phase	Pre-Concept / Concept / LPH2
Client	
Company	Name of Company
Contact Person	Name and Contact details such as telephone number, e-mail address
Project Team	
Project Leader	First Name Last Name
Team Members	First Name Last Name; First Name Last Name; First Name Last Name;
Credits for publication	LAVA (Tobias Wallisser, Alexander Rieck; Chris Bosse)
Consultants	List all sub-consultants which must be credited

L/\\//\
LABORATORY FOR
VISIONARY
ARCHITECTURE
